


Untitled project

	Name	Assigned to	Start	Finish	% Complete	Oct	Nov	Dec	Jan 2023
1	Site set up and mobilisation		21/11/2022	25/11/2022	0				
2	Time related preliminaries		21/11/2022	17/8/2023	0				
3	Foundations and substructure up to DPC		28/11/2022	30/12/2022	0				
4	External walls - block/brick cavity ground floor		4/1/2023	20/1/2023	0				
5	Scaffolding installation		23/1/2023	25/1/2023	0				
6	First floor- floor structure		26/1/2023	31/1/2023	0				
7	External walls - block/brick cavity		1/2/2023	17/2/2023	0				
8	Loft floor-floor structure		20/2/2023	24/2/2023	0				
9	Roof structure		27/2/2023	10/3/2023	0				
10	Roof covering flat/pitched roof		13/3/2023	31/3/2023	0				
11	First fix partition walls		3/4/2023	14/4/2023	0				
12	Stairs fit out		10/4/2023	14/4/2023	0				
13	Installation of windows		17/4/2023	21/4/2023	0				
14	First fix M&E		17/4/2023	5/5/2023	0				
15	First fix plumbing		17/4/2023	5/5/2023	0				
16	Underfloor heating installation		8/5/2023	12/5/2023	0				
17	ASHP installation		8/5/2023	11/5/2023	0				
18	Second fix walls and ceilings		8/5/2023	19/5/2023	0				
19	Plastering		22/5/2023	2/6/2023	0				
20	Bathroom installation and tiling		24/5/2023	16/6/2023	0				
21	Kitchen fit out		29/5/2023	15/6/2023	0				
22	Second fix M&E		16/6/2023	6/7/2023	0				
23	Second fix plumbing		19/6/2023	7/7/2023	0				
24	Flooring installation		19/6/2023	4/7/2023	0				
25	Doors and joinery fit out		5/7/2023	21/7/2023	0				

Untitled project

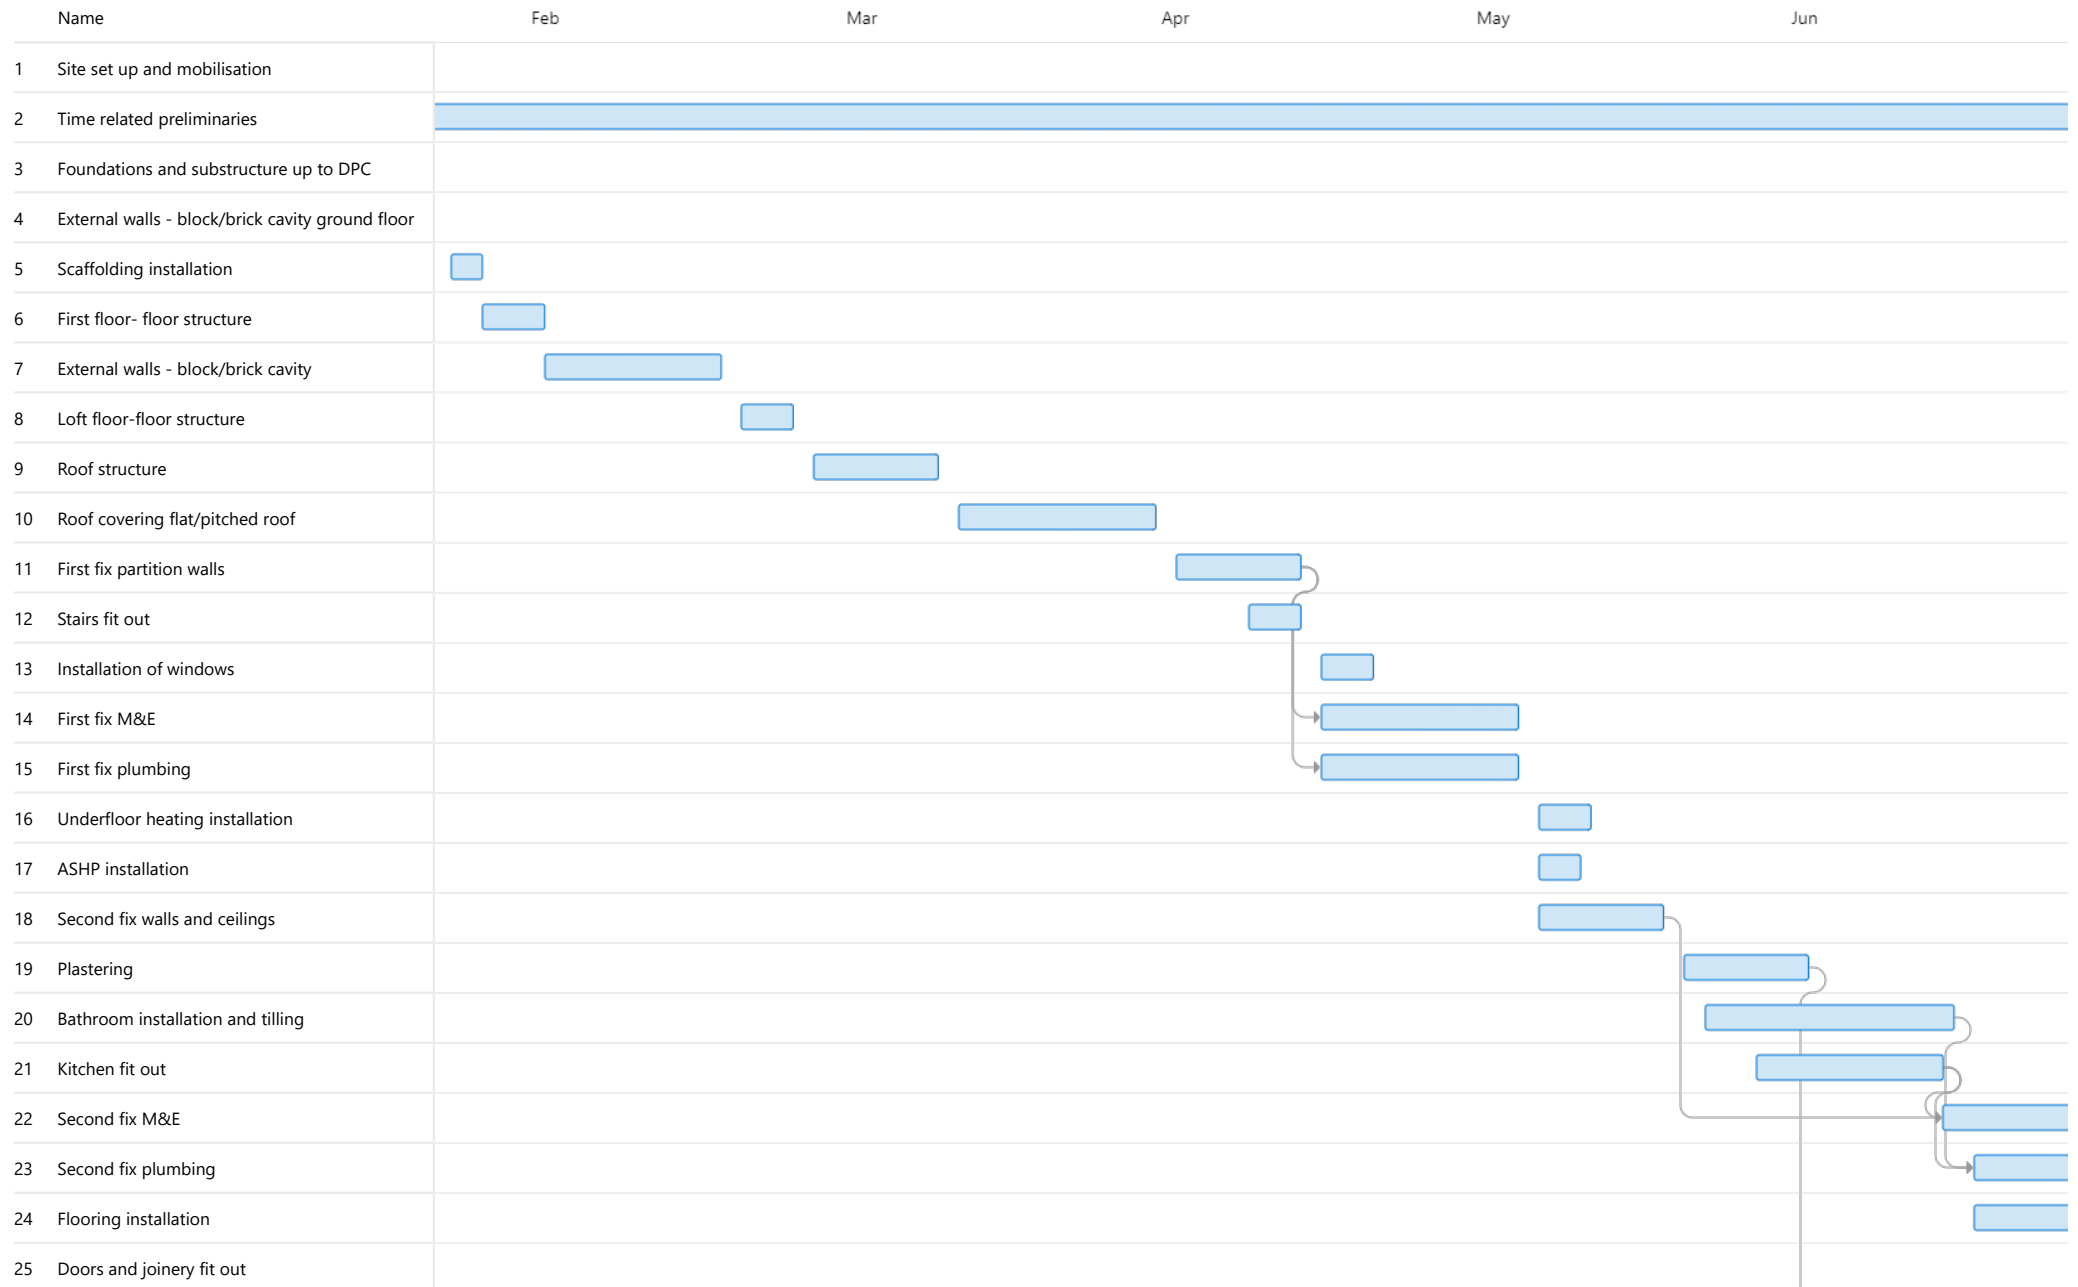

Untitled project

Name	Jul	Aug	Sep	Oct	Nov	De
1 Site set up and mobilisation						
2 Time related preliminaries						
3 Foundations and substructure up to DPC						
4 External walls - block/brick cavity ground floor						
5 Scaffolding installation						
6 First floor- floor structure						
7 External walls - block/brick cavity						
8 Loft floor-floor structure						
9 Roof structure						
10 Roof covering flat/pitched roof						
11 First fix partition walls						
12 Stairs fit out						
13 Installation of windows						
14 First fix M&E						
15 First fix plumbing						
16 Underfloor heating installation						
17 ASHP installation						
18 Second fix walls and ceilings						
19 Plastering						
20 Bathroom installation and tiling						
21 Kitchen fit out						
22 Second fix M&E						
23 Second fix plumbing						
24 Flooring installation						
25 Doors and joinery fit out						

Untitled project

	Name	Assigned to	Start	Finish	% Complete	Oct	Nov	Dec	Jan 2023
26	M&E testing and commisioning		26/6/2023	30/6/2023	0				
27	Painting and decorating		5/6/2023	11/8/2023	0				
28	Landscaping and fencing		5/6/2023	4/8/2023	0				

Untitled project

Name		Feb	Mar	Apr	May	Jun
26	M&E testing and commisioning					
27	Painting and decorating					
28	Landscaping and fencing					

Untitled project

