



GEOSHIELD

Verification Report



PROJECT REFERENCE:

GEO101436

REPORT NUMBER:

009

PROJECT:

GCL - Clarendon Road PHASE 3

PROJECT ADDRESS:

Clarendon Road

Hornsey

N8 0JU

MEMBRANE SPECIFICATION:

Gas membrane to specification BS8485 2015

Installed to CIRIA 735

Pudlo GP Ultra+ Gas Barrier

Pudlo GP Ultra Tape

Pudlo GP Ultra EXT Tape

Pudlo Liquid Gas Barrier



GEOSHIELD Verification PLAN



SPECIFICATION:

INFORMATION INCLUDED:

Material specification technical data sheets

5192204/P3_RemStrat Rev0.4

W257-PUD-D1-00-DR-S-02-1000

W257-PUD-D2-00-DR-S-02-1001

W257-PUD-D3-FN-DR-S-02-1002

W257-PUD-D3-XX-DR-S-02-1005

W257-PUD-D3-XX-DR-S-05-1000

W257-PUD-D4-00-DR-S-01-1006

W257-PUD-D4-BL-DR-S-02-1003

W257-PUD-DD-XX-DR-S-03-0001 to W257-PUD-DD-XX-DR-S-03-0024

W257-PUD-DD-XX-SK-S-03-0001 to W257-PUD-DD-XX-SK-S-03-0003

Information brought forward from the Pre Verification Plan. Any alterations to the originaally submitted design should be made aware to Geoshield



GEOSHIELD Verification Report



VERIFICATION OFFICER: John Cornish

VERIFICATION COMPANY: GeoShield Limited

Icon Business Park, 4100 Park Approach

Thorpe Park, LEEDS

West Yorkshire

LS15 8GB

CONTACT NUMBER: 07493769477

EMAIL ADDRESS: Jcornish@Geoshield.co.uk

ORDER NUMBER:

PER VISIT: YES:



NO:



PROJECT: YES:



NO:





GEOSHIELD

Verification Report



CLIENT DETAILS

CLIENT CONTACT: Rohallah De Sousa

CONTACTS ROLE: Ground Construction Ltd

MOBILE PHONE: 02082387000

EMAIL ADDRESS: RohallahDeSousa@GroundConstruction.com

CLIENT CONTACT:

CONTACTS ROLE:

MOBILE PHONE:

EMAIL ADDRESS

NOTES:

NOTES:

NOTES:



GEOSHIELD Verification Report



APPLICATION TEAM LEADERS

APPLICATOR NAME: Ermal

COMPANY: GCL - Site Engineer

APPLICATOR TEL: 07479553833

APPLICATOR EMAIL:

APPLICATOR NAME: Adrian Toderasc

COMPANY: GCL

APPLICATOR TEL:

APPLICATOR EMAIL:

NOTES: Installers have been toolbox talked by Geoshield during Visit no.6.

NOTES: The application standard will be monitored throughout and during each

NOTES: future inspection visits.

NOTES: Further training will be provided if deemed necessary.



GEOSHIELD Verification Report



AREA SURVEYED: Block D1 - Pour 3, Pour 4, Pour 5

Block D1 - Substation wrapped.

Block D2 - I-L/7-12.

SITE CONDITIONS:

WEATHER: Overcast.

TEMPERATURE: 11c.

MEMBRANE TEMPERATURE: N/A

RELATIVE HUMIDITY: N/A

TIME: 08:00 - 10:0


REPORT NUMBER: 009

DATE: 29/01/2021

ACCOMPANIED: Ermal - GCL Site Engineer

GEOSHIELD Verification Report

VERIFICATION LAYOUT

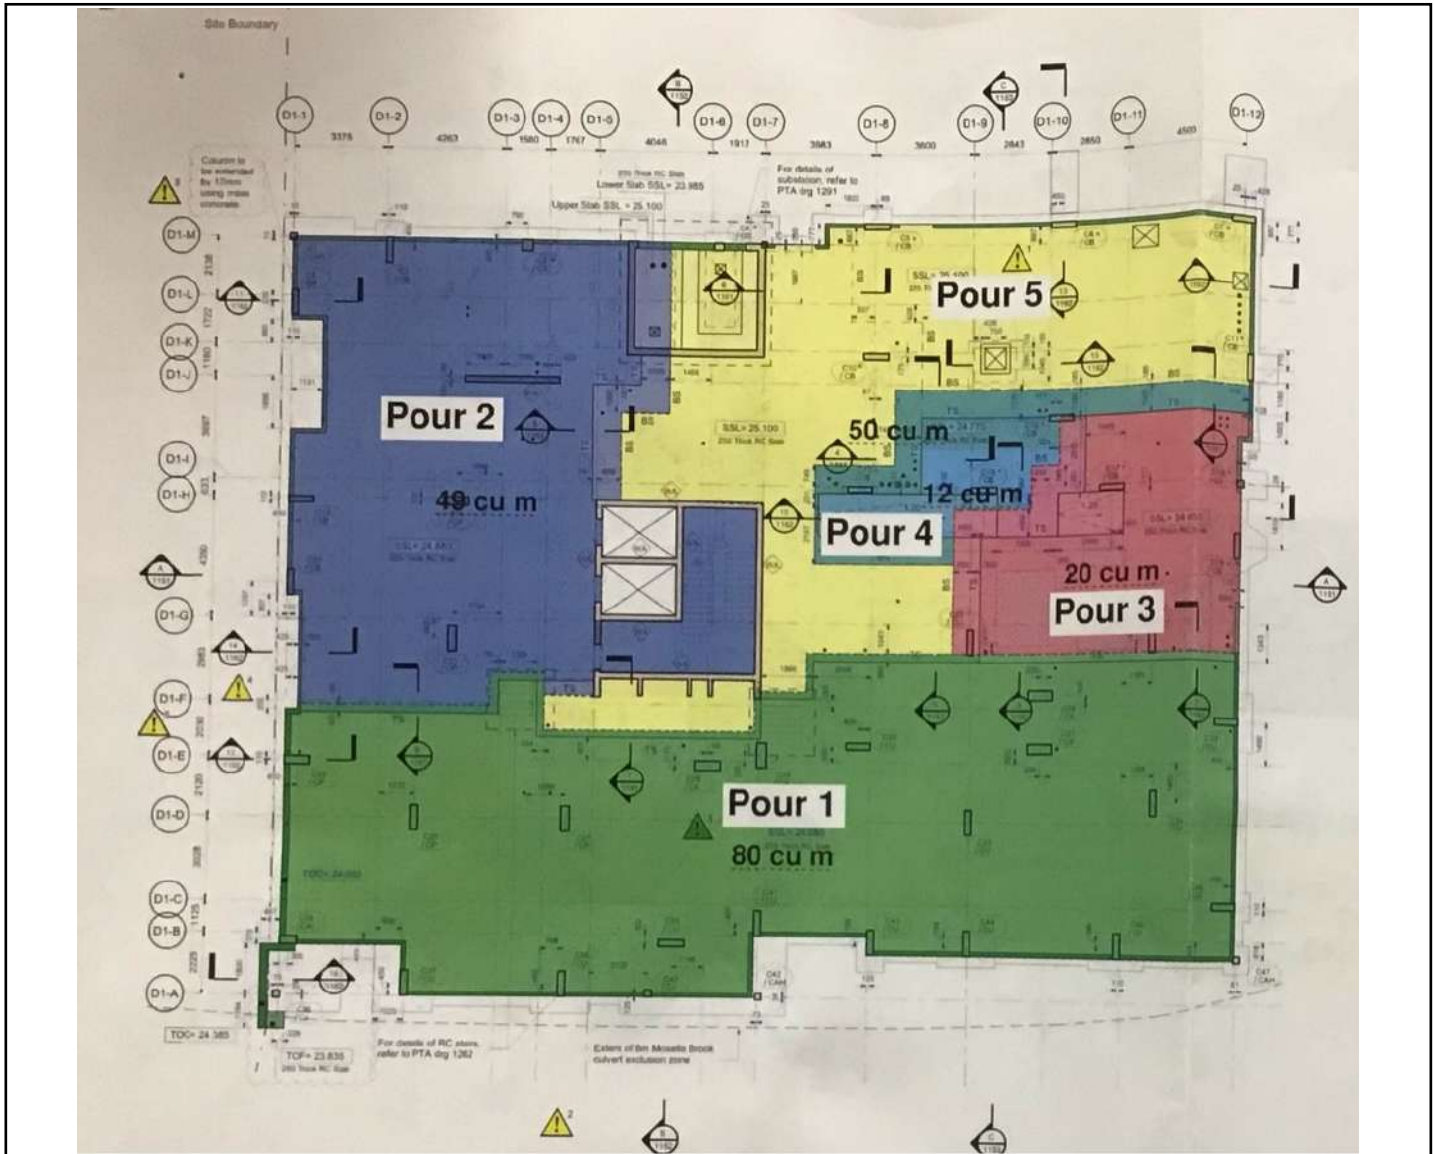

Verification of Block D1 Pour 3, 4, and 5 took place during this visit. Pour 3 and 4

have now been verified and signed off. Pour 5 will need another visit before the

area can be signed off.

GEOSHIELD Verification Report

OVERVIEW PHOTOGRAPHS



The photograph above shows the area of Block D2 which was verified during this visit. The installers have installed the Pudlo GP Ultra+ Gas Barrier to the area but not all details have been completed.



GEOSHIELD Verification Report



OVERVIEW PHOTOGRAPHS



The photograph above shows Block D1 substation which has been wrapped and verified during this visit.



GEOSHIELD Verification Report



VERIFICATION ITEM ONE

LOCATION/GRID LINE: Block D1 - Pour 4 and 5 and Block D2 slab area.

NOTES: Installation of Pudlo GP Ultra+ Gas Barrier.

The first photograph below shows an overview of a welded lap of the Pudlo GP Ultra + Gas Barrier. The installers have used a hot air leister and roller to achieve a consistent 40mm weld.



The second photo above shows a pick and probe test carried out to a welded lap.

No faults or defects identified. Verified in accordance with CIRIA 735.



GEOSHIELD Verification Report



VERIFICATION ITEM TWO

LOCATION/GRID LINE: Block D1 - Pour 4 and 5 and Block D2 slab area.

NOTES: Piles and pipe penetrations sealed.

The two photographs below show examples of sealed piles. The installers have first applied a coat of Pudlo liquid membrane to all pile heads. Once dry the installers have the used a hot air leister and roller to adhere the EXT tape to the membrane and ...



.... the painted pile head. The installers have also used the EXT tape to seal each steel bar. The Dina tellers have achieved a strong seal.

No faults or defects identified.

Installed in accordance with BS8485:2019.

GEOSHIELD Verification Report

VERIFICATION ITEM TWO



The photograph above shows a pick and probe test carried out to a sealed pipe

penetration. The installer have used a hot air leister and roller to achieve a good

seal. No faults or defects identified.

Verified in accordance with CIRIA 735.



GEOSHIELD Verification Report




VERIFICATION ITEM THREE

LOCATION/GRID LINE: Block D1 substation.

NOTES: Substation wrapped.

The first photograph below shows the installers have wrapped the substation. They first applied a coat of primer to all areas of concrete where the tanking had been adhered to. The installers have then welded the previously installed membrane....

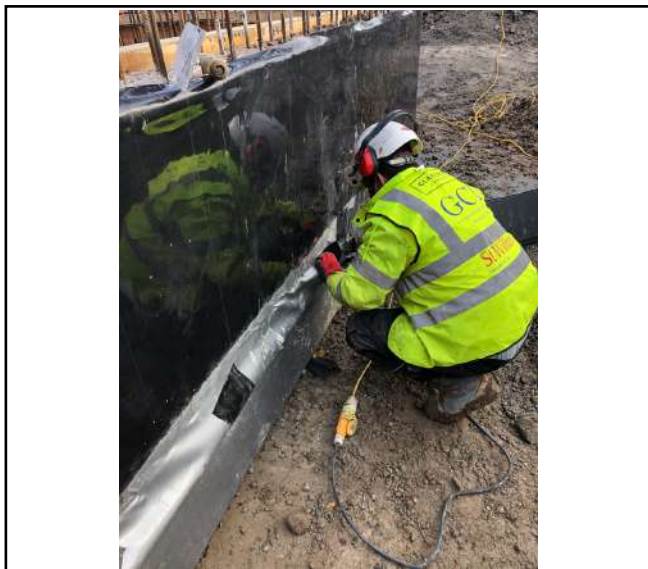

... to the newly installed tanking. A large number of holes were identified in the Pudlo GP Ultra+ Gas Barrier installed to the base of the substation. As shown in both photos above the installers have patched all the holes using EXT tape and a hot air leister and roller to aid in the adherence of the patches.

GEOSHIELD Verification Report

VERIFICATION ITEM THREE



The photograph above shows a pick and probe test carried out to a patched hole which was identified when inspecting the Substation. A strong seal has been achieved by the installers. No faults or defects identified.

Verified in accordance with CIRIA 735.

GEOSHIELD Verification Report

ADDITIONAL PHOTOGRAPHS



Penetrations from last visit have now
been sealed.



Pick and probe test to penetrations
through steel.



Fault identified in welded lap.



Installers have rectified the gap.



GEOSHIELD Verification Report



REMEDIATION LOG

Date	Nr	Remediation Description	Y/N
10/11/2020	001	No faults found	✓
12/11/2020	002	Damaged corner repaired	✓
01/12/2020	003	1. Damage to the membrane had been patched but the fleece	✓
		below had not been removed and therefore the seal wasn't very	✓
		strong. This patch was removed and the damage was repaired	✓
		correctly during this visit.	✓
		2. 3 x pile caps sealed using the Pudlo Liquid GB had been	✓
		chipped and therefore additional Liquid Gas Barrier had to be	✓
		applied to small areas.	✓
10/12/2020	004	1. Incorrect sealing of lap joints in membrane - taped not welded.	✓
		2. 3 x pipe penetrations not sealed.	✓
18/12/2020	005	No faults or defects identified during this visit.	✓
12/01/2021	006	1. Some pile caps incomplete as per the detail for sealing.	✓
		2. Several welded joints required re-welding to achieve a seal.	✓
		3. Corner details not sealed due to access required to the area.	✓



GEOSHIELD Verification Report



REMEDIATION LOG

Date	Nr	Remediation Description	Y/N
15/01/2021	007	1. 1 lap had not been welded correctly the installers have used	✓
		a hot air leister and roller to ensure that a 40mm weld has been	✓
		achieved.	✓
22/01/2021	008	1. One hole in the membrane identified. The installers have	✓
		patched the hole by removing the fleece around the hole and then	✓
		a hot air leister has been used to adhere EXT tape ove the hole.	✓
		2. A couple small areas in the laps of the Pudlo GP Ultra+ Gas	✓
		Barrier did not have a 40mm weld. Installers have re welded	✓
		these areas during this visit.	✓
		3. Some penetrations of the membrane have not been sealed	✓
		these will have to be sealed and verified during the next visit	✓
		(See verification item 3 - Report 8)	✓
29/01/2021	009	1. A couple pipe penetrations had been sealed but a sufficient lap	✓
		using the EXT tape had not been achieved. The installers have	✓
		applied additional patches of EXT tape during this visit.	✓



GEOSHIELD

Verification Report



GAS MEMBRANE TESTING

VISUAL:	☐ YES	☒	☐ NO	☐	SMOKE TEST:	☐ YES	☐	☐ NO	☒
COMPRESSED AIR:	☐ YES	☐	☐ NO	☒	DILECTIC	☐ YES	☐	☐ NO	☒
DESTRUCTIVE:	☐ YES	☐	☐ NO	☒	OTHER:	☐ YES	☒	☐ NO	☐
Testing checklist attached:	☐ YES	☐	☐ NO	☐					

Gridline/Plot Sign off

Gridline/Plot Sign off	Block D1 - Core - Lower	☒
Gridline/Plot Sign off	Block D1 - Core - Middle and Upper	☒
Gridline/Plot Sign off	Pump Chamber Base	☒
Gridline/Plot Sign off	Block D2 - Core.	☒
Gridline/Plot Sign off	Block D1 Slab - Pour 1 (50%)	☒
Gridline/Plot Sign off	Pumping station.	☒
Gridline/Plot Sign off	Block D1 Slab - Pour 1 (Base installation only).	☒
Gridline/Plot Sign off	Block D1 slab - Pour 1 (100%)	☒
Gridline/Plot Sign off	D1 Substation.	☒
Gridline/Plot Sign off	Block D1 - Pour 2	☐
Gridline/Plot Sign off	Block D1 - Pour 3	☒
Gridline/Plot Sign off	Block D1 - Pour 4	☒



GEOSHIELD Verification Report



VERIFICATION SUMMARY

This was the 9th visit to site where verification of the installation of the Pudlo

GP Ultra+ Gas Barrier to Block D1 and D2 slab areas as well as the wrapping of

D1 substation was required. The installers have welded all laps of the Pudlo

GP Ultra+ Gas Barrier using a hot air leister and roller to achieve a consistent

40mm weld. All piles and pipe penetrations that have been sealed, have been

sealed correctly and as per the detail. Incomplete works are still outstanding for

Block D1 pour 2 and 5 as well as Block D2 I-L/7-12.

Installed in accordance with BS 8485:2019.

Verified in accordance with CIRIA 735.

GEOSHIELD SIGNATURE:

DATE: 29/01/2021
