

BS 5837 Arboricultural Report

Impact Assessment & Method Statement



at

**9 Waverley Road
London
N8 9QS**



**Dated
14th May 2021**



CROWN
Tree Consultancy

Branching out through England and Wales



PDF readers select page-width for detail & page-view for scrolling

Arboricultural Report to BS 5837: 2012 for: Stockwool

Crown Ref: 10524

Site: 9 Waverley Road, London

Author: Emma Hoyle

Date: 14th May 2021

Contents

1.	Introduction	3
1.1.	Instruction	3
1.2.	Scope and Purpose of the Report	3
1.3.	References	3
1.4.	Survey Details and Findings	3
1.5.	Drawings	4
1.6.	Author	4
2.	Site Overview	5
2.1.	Brief Description	5
2.2.	Coordinates	5
2.3.	Survey Extent	5
3.	Vegetation Overview (independent of proposals)	6
3.1.	Preliminary Management Recommendations	6
3.2.	Work Priority and Future Inspections	6
3.3.	Tree Protection Status – Site Specific	7
3.4.	Tree Protection – General Notes	7
3.5.	Species Present – Additional Information	7
4.	Arboricultural Impact Assessment	9
4.1.	Overview	9
4.2.	Tree Removal	9
4.3.	Mitigation Planting	10
4.4.	Impact on Tree Canopies	10
4.5.	Impact on Tree Roots	10
4.6.	Demolition Activities	12
4.7.	Hazardous Materials	12
4.8.	Cabins and Site Facilities	12
4.9.	Boundary Treatments	12
4.10.	Impact of Retained Trees on the Development	12
4.11.	Summary	13
5.	Photographs	14
Appendix 1: BS 5837: 2012 – Guidance Notes		16
Appendix 2: Explanation of Tree Data & Glossary		18
Appendix 3: Survey Methodology		22
Appendix 4: Author's Qualifications		23
Appendix 5: Further Information		24
Appendix 6: Tree Data Schedule, Site Plans & Arboricultural Method Statement.		25



1. Introduction

1.1. Instruction

1.1.1. We are instructed by Stockwool to:

- Undertake an Arboricultural Survey at 9 Waverley Road and assess all trees potentially within influencing distance of proposed development within the site.
- Plot the trees on a Tree Constraints Plan and record the data in a Tree Data Schedule.
- Provide an overview of the site and any management recommendations.
- Determine if any of the trees are growing within a conservation area or are protected by a tree preservation order.
- Provide guidance for architects or developers to enable them to understand and design within the existing tree constraints.
- Assess the potential impact of the development proposals and provide guidance as to appropriate mitigation measures.
- Produce an Arboricultural Impact Assessment for submission to the local authority once the design has been finalised.
- Produce a Tree Protection Plan and Arboricultural Method Statement specifying how the retained trees shall be protected from inadvertent damage by demolition or construction activity.

1.2. Scope and Purpose of the Report

1.2.1. This report is designed to accompany a planning application for development proposals at the above site. Its purpose is to assist and inform the planning process. It is produced according to the guidance and recommendations within BS 5837: 2012 - *Trees in Relation to Design, Demolition and Construction*.

1.2.2. The accompanying Arboricultural Method Statement specifies the principles to be adopted during construction and demolition that will minimise any impacts on trees. However, specific construction activities proposed within Root Protection Areas may need to be agreed in more detail if requested by the local authority at the reserved matters stage (for an outline planning applications) or via planning conditions.

1.3. References

1.3.1. We have liaised with our client to attain an adequate understanding of the project to enable us to carry out an accurate assessment of the proposals and to specify suitable tree protection measures.

1.4. Survey Details and Findings

1.4.1. A visual ground level inspection of all trees was undertaken on the 15th April 2020 by Joe Taylor. No climbed inspections or specialist decay detection were undertaken. Details of how the survey was undertaken can be found in Appendix 1.

1.4.2. The findings of the survey are presented in The Tree Data Schedule which is provided as a separate document as well as being appended to the end of this document within Appendix 6. The vegetation is further discussed in Section 3.



1.4.3. The Schedule includes scaled tree images based on measurements recorded for stem diameter, crown spread, crown height and overall height. Their purpose is to indicate, at a glance, the relative dimensions of each tree.

1.4.4. A definition of the Retention Categories can be found in Appendix 1. All other terms used within the Tree Data Schedule are defined and explained in Appendix 2. A more detailed description of the survey method is detailed in Appendix 3.

1.5. Drawings

1.5.1. The tree locations shown on the accompanying plans which are reproduced in Appendix 6 are based on a measured plan of the site supplied to Crown Tree Consultancy. This plan had the tree positions already plotted. Where applicable, additional trees have been plotted by us according to measurements taken on site.

1.5.2. The *Tree Constraints Plan* shows the existing layout. For each tree the stem location is indicated and scaled according to its diameter, the canopy is indicated according to measurements taken along the four cardinal points of the compass. Root protection areas (RPAs) are indicated which are calculated according to the guidelines within BS 5837 (2012).

1.5.3. Where appropriate, the shapes of the RPAs have been amended to reflect actual site conditions or where trees have been heavily pruned. The 'original' RPAs are indicated as a dashed line whereas the amended RPAs are indicated as a solid line.

1.5.4. The *Impact Assessment Plan* indicates the tree constraints with the proposals overlaid. Where applicable, this plan shows where works are proposed in Root Protection Areas and which trees are to be pruned or removed. This plan accompanies the Impact Assessment which is to be found in Section 4.

1.5.5. The *Tree Protection Plan* shows the protection measures that are to be installed during the construction phase. This plan forms part of the accompanying Arboricultural Method Statement which is also appended to this report (see Appendix 6).

1.6. Author

1.6.1. This report was compiled by Emma Hoyle FDS (Arboriculture), ED (Forestry & Arboriculture), M. Arbor. A. Details of the author's experience that qualify her to produce such a report are detailed in Appendix 4.



2. Site Overview

2.1. Brief Description

- 2.1.1. 9 Waverley Road is a detached, residential property. A dual entrance driveway and parking area occupies the front of the property with a low retained planter adjacent the front boundary wall. A Retention Category A Beech tree (T1) and a Retention Category B Lime tree (T3) grow at the front of the property.
- 2.1.2. The rear garden is largely given over to a lawn with steps leading down from the rear of the building onto pedestrian footpaths. One Retention Category A Ash tree (T4), seven Retention Category B trees (T7, T8, G9 and T17), four Retention Category C trees (T5, T6, T10 and T13) and one Retention Category U tree (T12) grow within the rear garden.
- 2.1.3. Adjacent to the site and overhanging the boundaries of the rear garden is a Retention Category B tree (T16), two Retention Category C trees (T11 and T14) and a Retention Category C hedge (H15). The roots of these trees may extend into the site.
- 2.1.4. The site is a rectangular plot measuring approximately 50m by 24m and the front of the property is at a slightly higher level than the rear.
- 2.1.5. The Tree Constraints Plan and Tree Data Schedule (see Appendix 6) should be referred to for descriptions and locations of all trees.

2.2. Coordinates

- 2.2.1. The site coordinates are 0° 7'30.23"W 51°34'32.38"N and the altitude is approximately 67m above sea level¹.

2.3. Survey Extent

- 2.3.1. We surveyed the front and rear gardens along with all trees beyond the curtilage of the property which could potentially be affected by any development within it. The area indicated below² shows the extent of the site.



¹ To access satellite imagery and street views of the site these co-ordinates may be entered into: <http://maps.google.co.uk/>

² Image taken from Google Earth and may not be current



3. Vegetation Overview (independent of proposals)

This section summarises all the recommendations within the Tree Data Schedule regardless of whether trees are to be retained, felled or pruned to facilitate the proposed development. It does not specify works that may be required to facilitate the development proposals. The protection status of the trees is also reported in this section.

3.1. Preliminary Management Recommendations

- 3.1.1. The following recommendations are made in order to maintain the trees in an acceptable condition:
- 3.1.2. **T1**, a mature Beech, has a significant cavity forming on the southern side of its stem at approximately 2.5m above ground level. We recommend a climbed inspection of the cavity is undertaken to determine the extent of any decay that may be present.
- 3.1.3. **T8**, a semi-mature London Plane, was observed to have a cavity where its secondary stem has torn out in the past. We recommend a climbed inspection is undertaken to inspect the cavity for any decay that may be present.
- 3.1.4. **T12** is a dead Pear tree. We recommend this tree is removed.
- 3.1.5. **T17** is a mature Lime tree. This tree has a dense canopy along with a covering ivy which prevented a detailed inspection. We recommend undertaking remedial pruning to clean the canopy of any dead, dying or defective branches and remove the ivy in order to enable a better inspection of the tree.
- 3.1.6. **T3** and **T7** could not be fully inspected due to a covering of ivy. We recommended the ivy is removed so that the stems may be re-inspected to ascertain their structural condition.
- 3.1.7. All other trees were deemed to be in an acceptable condition.

3.2. Work Priority and Future Inspections

- 3.2.1. The table below suggests a schedule for completing the works recommended in the Tree Data Schedule based on the perceived risk:

Work Priority	Definition	Tree Number
Urgent	As soon as possible	None
Very High	Within 1 Month	None
High	Within 3 Months	T1 and T17
Moderate	Within 1 year	T3, T7, T8 and T12
Low	Within 3 years	None

- 3.2.2. The table below suggests a schedule of future inspections based on the condition and location of each tree:

Inspection Frequency (years)	Tree Number
0.5	None
1	T1 and T3
1.5	T17
3	T2, T4, T5, T6, T7, T8, G9, T10, T11, T13, T14, H15 and T16

- 3.2.3. The trees should be inspected sooner if there is a noticeable decline in their condition or following extreme weather events.



3.3. Tree Protection Status – Site Specific

3.3.1. On 27th March 2020, we visited the local authority website (London Borough of Haringey) which informed us that:

- The site lies within Crouch End Conservation Area.
- There are Tree Preservation Orders affecting 2 x Beech and 3 x Lime trees within the site (TPO Refs: 2014/2178, 2014/1194 and 2014/1195). However, only two Lime and one Beech tree are present at the site. We believe trees T1, T3 and T17 (according to our numbering system) are protected by TPO's.
- There are Tree Preservation Orders affecting 8 x Lime trees at the adjacent property, Midhurst Court (TPO Ref: 2014/1122).

3.4. Tree Protection – General Notes

3.4.1. Before undertaking works to trees protected by a tree preservation order, consent needs to be obtained from the local authority which will provide application forms and advice to potential applicants. The removal of dead wood is exempt.

3.4.2. Where the works are proposed for reasons of safety or ill health, a report from a suitably qualified arborist will usually be required. Trees that are dead or imminently dangerous are technically exempt from protection, as are dead branches. If the tree work is not urgently necessary however, at least five working days notice of intention should be given to the local authority. In any case it would be prudent to take photographs before undertaking works without prior consent being granted. Unauthorised works to protected trees may result in a criminal prosecution and a large fine (unlimited).

3.4.3. Where trees are located in a conservation area (but not protected by a TPO), works are not permitted without first giving the local authority 6 weeks' notice of intention. During this time the local authority may elect to create a tree preservation order or to inform the applicant that they have no objection to the proposed works. If the local authority does not respond within 6 weeks, then the intended work may be undertaken. Note: the local authority cannot refuse consent for works to trees within a conservation area; they may only create a tree preservation order if they wish to have further control over what works are undertaken.

3.4.4. Where planning permission is granted and tree works have been approved as part of the planning consent, no further application is required in respect of protected trees and no further notice is required in respect of trees within a conservation area.

3.5. Species Present – Additional Information

3.5.1. The table below contains general information about the tree *species* (rather than the actual tree *specimens*) included in the survey. Its purpose is to assist readers who are unfamiliar with the characteristics of the various species.

Species	Typical Height at Maturity (m)	Typical Canopy Spread at Maturity (m)	General Notes
Ash	25	18	Large deciduous tree with a straight bole and a high open domed crown. Native to Britain and commonly found in woodlands and adjacent roadsides. Not suitable for small gardens. Easily identified by its oppositely arranged pinnate leaves and black buds. Branches are relatively brittle resulting in a fairly high incidence of small branch failure in windy conditions. Visit http://www.pfaf.org/user/Plant.aspx?LatinName=Fraxinus+excelsior for more info.



Species	Typical Height at Maturity (m)	Typical Canopy Spread at Maturity (m)	General Notes
Elder	8	8	Deciduous tree native throughout Europe, N Africa and W Asia. Untidy, shrubby habit. Very fast growing. Covered in dense creamy flowers and deep red berries which are excellent for making wine. Visit http://www.pfaf.org/user/Plant.aspx?LatinName=Sambucus+nigra for more info.
False Acacia	20	12	Deciduous fast-growing tree native to the US. Part of the pea family and its roots fix nitrogen. Bright yellow 'Frisia' cultivar is widely planted in gardens. All parts are toxic except the flowers which appear in June. Seed pods ripen in winter. Visit http://www.pfaf.org/user/Plant.aspx?LatinName=Robinia+pseudoacacia for more info.
Holly	16	12	Evergreen tree native across Western Europe. Many cultivars available, often with variegated leaves. Females produce bright red berries. Good wildlife value. Visit http://www.pfaf.org/user/Plant.aspx?LatinName=Ilex+aquifolium for more info.
Lawson Cypress	40	10	Erect, narrowly conical evergreen tree native to Southwest Oregon and N. W. California. Introduced to Britain in the 1850's and now a common tree in gardens and parks. Makes an excellent dense hedge. Many varieties are available including golden and miniature varieties. Easily distinguished from Leyland cypress by the presence of small cones. Visit http://www.pfaf.org/user/Plant.aspx?LatinName=Chamaecyparis+lawsoniana for more info.
Lime	25	12	Very common street tree. Several species exist; the one most often found in woods is 'common lime' which produces a mass of suckers at the stem base, making it very cheap to propagate. Limes have non-symmetrical heart shaped leaves which are much loved by aphids (hence the sticky honeydew on cars parked beneath). Limes are tolerant of heavy pruning and are often managed as pollards. Old limes tend to support a lot of small dead branches. Visit http://www.pfaf.org/user/Plant.aspx?LatinName=Tilia+x+europaea for more info.
London Plane	30	20	Deciduous tree arisen in cultivation probably as a cross between the Oriental Plane and the American Buttonwood. Has attractive bark which peels off in small plates leaving a multicoloured flecked pattern. Very common as a street tree, especially throughout London where it dominates the streetscape. Often managed as a pollard in order to constrain its large size to more manageable proportions, especially where there are clay soils and adjacent buildings. Somewhat susceptible to the decay fungus Inonotus hispidus. Visit http://en.wikipedia.org/wiki/Platanus for more info.
Pear	8	8	Deciduous tree native across Europe and W Asia. Hundreds of cultivars available due to its popular fruit. White flowers in spring along with bright green foliage. More upright growth habit than most apples.
Purple Beech	27	20	Purple variety of the common beech, also called Copper Beech. A majestic tree with grey bark and purple leaves. The best forms are grafted though this species does occasionally appear in the wild. Visit http://en.wikipedia.org/wiki/Fagus_sylvatica for more info.
Sycamore	25	16	Deciduous tree native to S. Europe, widely naturalised in the UK. Often regarded as a weed species due to its invasive nature and ability to tolerate most conditions. Responds well to pruning. Not a good tree to park beneath in summer due to the sticky sap secreted by aphids. Visit http://www.pfaf.org/user/Plant.aspx?LatinName=Acer+pseudoplatanus for more info.
Yew	14	12	Evergreen species native throughout Europe. Commonly planted in churchyards. Once revered by ancient Britons and thought to be the inspiration for our Christmas tree. Capable of remarkable regeneration and extreme longevity. Poisonous foliage and seeds. Slow growing. Visit http://www.pfaf.org/user/Plant.aspx?LatinName=Taxus+baccata for more info.

3.5.2. The figures quoted regarding typical height and canopy spread should be treated as approximate. Actual heights and spreads vary according to several environmental factors such as soil conditions, climate and presence of competing vegetation. The figures quoted are not the maximum dimensions that the species may attain.



4. Arboricultural Impact Assessment

4.1. Overview

4.1.1. It is proposed to construct a lower ground floor and extension to the rear of the building, construct an outbuilding and make landscape improvements as indicated on the plans in Appendix 6. The existing layout is indicated in black, the footprint of the proposed ground floor layout is indicated in pale green and the footprint of the proposed lower ground floor is indicated in pink.

4.1.1. The table below summarises the potential impact on trees due to various activities.

Activity	Trees Potentially Affected
Tree Removal: Retention Category A	T4
Tree Removal: Retention Category B	One of G9
Tree Removal: Retention Category C	T13
Tree Removal: Retention Category U	T12
Tree Pruning	T11, one Elder and a Cherry Laurel
RPA: Lower Ground Floor Foundations	T17
RPA: Outbuilding Foundations	T10, T11, T14 and H15
RPA: New Pedestrian Surface	T5, T6, T7, T8, G9, T14, T16 and T17
RPA: Underground Services	To be confirmed
RPA: Change of Ground Levels	None
RPA: Soil Compaction	Trees adjacent the construction area (preventable by installing tree protection measures)

4.1.2. Other potentially damaging activities often associated with construction sites include demolition or the careless use of plant machinery, hazardous materials, or fires. All of the above potential impacts are considered in detail throughout this section.

4.1.3. The accompanying Arboricultural Method Statement (duplicated in Appendix 6) specifies the measures proposed to minimise all possible potential risks of damage to the retained trees.

4.2. Tree Removal

4.2.1. All trees to be removed are indicated on the Impact Assessment Plan and listed below:

- Retention Category A:** It is proposed to remove one Retention Category A tree: T4.
 This tree is located so close to the proposal that its retention is not practicable and will require removal to facilitate the proposed excavations and facilitate construction activity. This tree is not considered to have a high amenity value as its visibility from public vantage points is very limited. Consequently, its removal shall not have a major impact upon local visual amenity.
- Retention Category B:** It is proposed to remove one Retention Category B tree from within G9.
 The southern-most tree within G9 is located so close to the proposed outbuilding (620mm away) that its retention is not practicable. Furthermore, this tree will require removal to facilitate the installation of the outbuilding and provide suitable room for construction activity. This tree is not visible from public vantage points and is considered to have a low amenity value.



- **Retention Category C:** It is proposed to remove one Retention Category C tree: T13.

This tree is located so close to the proposed outbuilding that its retention is not practicable. This is a small tree in a poor condition and is located within a rear garden. It is not visible from public vantage points and is considered to have a low amenity value.

- **Retention Category U:** It is proposed to remove one Retention Category U tree: T12.

T12 is a dead Pear tree and requires removal regardless of development proposals. Consequently, the removal of this tree is not considered to be a direct impact of the development.

4.2.2. The trees to be removed are all located within a rear garden and are not protected by a tree preservation order.

4.2.3. Details specific to each tree can also be found in the Tree Data Schedule.

4.3. Mitigation Planting

4.3.1. The site offers opportunity for the planting of small trees and vegetation as part of the proposed landscaping improvements. New tree planting is recommended where possible to mitigate the loss of trees.

4.4. Impact on Tree Canopies

4.4.1. It is proposed to prune the overhanging foliage of T11 back towards the boundary. Such pruning shall create suitable clearance from the proposed outbuilding, it shall enable tree protection fencing and scaffolding to be installed and shall reduce the risk of any accidental damage to branches during construction. Such pruning shall have no impact on local visual amenity.

4.4.2. The Cherry Laurel within the rear garden is also to be trimmed back to enable tree protection fencing to be installed and provide clearance for construction activity. Such pruning is not considered to be a material planning consideration.

4.4.3. The Elder situated adjacent the northern boundary is to be pruned back towards the boundary to avoid any accidental damage to overhanging branches during construction. Such pruning is not considered to be a material planning consideration.

4.4.4. The canopies of all other retained trees are located sufficiently far from proposed building works and sufficiently high over access routes throughout the site that they shall not be impacted upon by any construction activity. Restrictions are placed on activities throughout the site to ensure that no canopies are accidentally damaged – see the accompanying Arboricultural Method Statement.

4.5. Impact on Tree Roots

4.5.1. Lower Ground Floor Foundations:

4.5.2. The foundations for the new lower ground floor will extend into approximately 14% of the theoretical Root Protection Area of T17.

4.5.3. In order to ensure that the soils beyond the footprint of the lower ground floor remain undisturbed, it is proposed to install the foundations in a manner that does not disturb the soils beyond the footprint of the proposal. This may be done via contiguous piling, sheet piling, pinning or any similar method which restricts excavation to the footprint. Consideration should be given to the type of pile driver that is used and how soils may be protected from compaction. The pile driver should operate from within the building footprint wherever possible.



4.5.4. **Outbuilding Foundations:**

4.5.5. The foundations for the proposed outbuilding will extend into to the Root Protection Areas of T10, T11, T14 and H15. Such small portions of the RPAs of T10 and T11 shall be affected, the impact is considered to be negligible. A small portion of the RPA of H15 shall be affected and approximately 8% of the Root Protection Area of T14 shall be affected. Overall, the potential detrimental impact is considered to be relatively small.

4.5.6. In order to minimise the potential impact on the root system of T14, a shallow raft or beam foundation is proposed. The following restrictions shall apply:

- Excavation shall be limited to a maximum depth of 200mm to facilitate the installation of a raft or beam foundation.
- Only hand tools or a small, carefully marshalled mechanical excavator shall be used during the excavation.
- If roots in excess of 25mm diameter are encountered close to the edge of the excavation, they shall be retained wherever possible and protected with damp sacking during times that they are unearthed. Any roots that need to be severed shall be neatly pruned with secateurs.
- The raft/beam may be supported on narrow diameter piles (maximum diameter 250mm). Before installing such piles, their location shall be determined by trial pits excavated to a depth of 600mm using hand tools. Trial pit dimensions should not exceed 300mm x 300mm. If any roots in excess of 40mm diameter are encountered, the pile shall be relocated.
- Excavation shall be supervised by the project arborist.

4.5.7. **New Hard Surfaces:**

4.5.8. No significant hard or heavily engineered surfaces are proposed within the Root Protection Areas of any trees.

4.5.9. **New Pedestrian Surfaces:**

4.5.10. As part of the development, landscaping improvements are proposed within the rear garden. New pedestrian surfaces are to be installed over the Root Protection Areas of T5, T6, T7, T8, G9, T14, T16 and T17. In order to ensure impact is kept to a minimum, excavation shall be limited to a depth of 150mm, turf shall be removed using hand tools and permeable surfaces are to be installed.

4.5.11. **Underground Services:**

4.5.12. No underground services should be installed through any Root Protection Area without consulting the project arborist and if necessary, gaining approval from the local authority.

4.5.13. Due to the potential impact of excavating trenches within Root Protection Areas, the locations of all underground services should be approved by the local authority after consultation with a project arborist to assess the potential impact on trees.

4.5.14. **Changes in Ground Levels:**

4.5.15. No changes of ground levels in excess of 100mm within Root Protection Areas shall be made without consulting the arborist and if necessary, gaining approval from the local authority.

4.5.16. **Soil Compaction:**

4.5.17. The majority of tree roots lie within the upper soil horizons. This is because the availability of oxygen decreases with depth and roots need to breathe to stay alive. In



addition, nutrients are more readily available in the form of organic matter close to the soil surface.

- 4.5.18. Healthy soils contain about 25% air space between solid particles. Increased loading of the soils caused by construction activity causes air to be squeezed out as the soil becomes compacted preventing roots from breathing. Even an increase in pedestrian activity may cause some soil compaction.



- 4.5.19. It is important therefore that ground compaction and soil disturbance over Root Protection Areas should be avoided during the construction phase. This may be done by installing protective fencing and ground protection measures as recommended within the accompanying Arboricultural Method Statement.

4.6. Demolition Activities

- 4.6.1. There are no structures that require demolition or significant surfaces that require removal close to trees. The tree protection measures specified within the accompanying Arboricultural Method Statement should be installed prior to the commencement of all demolition activities (including soil stripping) to prevent any detrimental impact on tree health.

4.7. Hazardous Materials

- 4.7.1. All hazardous materials (including cement and petrochemical products) will need to be controlled according to COSHH regulations in order to ensure there is no detrimental impact on tree health. Provision shall need to be made to ensure that cement and cement run-off are contained outside of all Root Protection Areas.

4.8. Cabins and Site Facilities

- 4.8.1. Consideration should be given to the location of any site welfare facilities in terms of potential impact on trees. Where it is proposed to install cabins or site facilities in Root Protection Areas, the project arborist should be consulted and approval obtained from the local authority.
- 4.8.2. There is limited room for the siting of cabins and storage of materials / spoil during the construction phase so the logistics of the development shall need to be well organised to ensure that there is adequate space outside of the Tree Protection Zones for construction activity.

4.9. Boundary Treatments

- 4.9.1. We are not aware of any changes are proposed to the existing boundary features that might impact on trees.

4.10. Impact of Retained Trees on the Development

- 4.10.1. The outbuilding is not considered to be a living space so the shade cast by the trees is not considered to be relevant from a planning perspective.
- 4.10.2. The foundations and any new surfaces should be designed to accommodate all potential impacts due to future tree rooting activity. These include potential vegetation related subsidence, vegetation related heave, and lifting of surfaces / light structures due to direct root pressure.



- 4.10.3. The gutters for the outbuilding will need occasional maintenance to avoid blockage from leaves. This will be relatively easy to manage as the proposal is a single storey building. The outbuilding would benefit from the installation of leaf-guards.

4.11. Summary

- 4.11.1. In order to facilitate the development, it is proposed to remove four trees from within the rear garden of the property. The removal of these trees shall not have a significant impact upon local amenity.
- 4.11.2. The existing landscaping is not considered to be particularly attractive and landscape improvements are proposed as part of the development to enhance visual amenity.
- 4.11.3. Minor pruning works are proposed to one tree (T11) and two shrubs.
- 4.11.4. Foundations are proposed within the Root Protection Areas of five trees. Sympathetic excavations to facilitate foundations are proposed wherever possible to minimise impact.
- 4.11.5. No significant hard surfacing is proposed in Root Protection Areas.
- 4.11.6. Pedestrian paving is proposed as part of the landscaping improvements within the rear garden. Excavation for new surfaces shall be minimal and proposed surfaces shall be permeable.
- 4.11.7. Adequate space has been allowed between the proposal and all trees such that no future pressure to overly-prune or remove trees shall occur as a consequence of the proposal.
- 4.11.8. Please see the Arboricultural Method Statement and Tree Protection Plan in Appendix 6 which specifies measures to ensure trees are adequately protected during construction.



PDF readers select *page-width* for detail & *page-view* for scrolling

Arboricultural Report to BS 5837: 2012 for:

Stockwool

Crown Ref: 10524

Site: 9 Waverley Road, London

Author: Emma Hoyle

Date: 14th May 2021

5. Photographs



Photo 2.



Photo 3.



Photo 4.



Photo 5.



Photo 6.





PDF readers select *page-width* for detail & *page-view* for scrolling

Arboricultural Report to BS 5837: 2012 for: Stockwool

Crown Ref: 10524

Site: 9 Waverley Road, London

Author: Emma Hoyle

Date: 14th May 2021

Photo 7.



Photo 8.



Photo 9.



Photo 10.

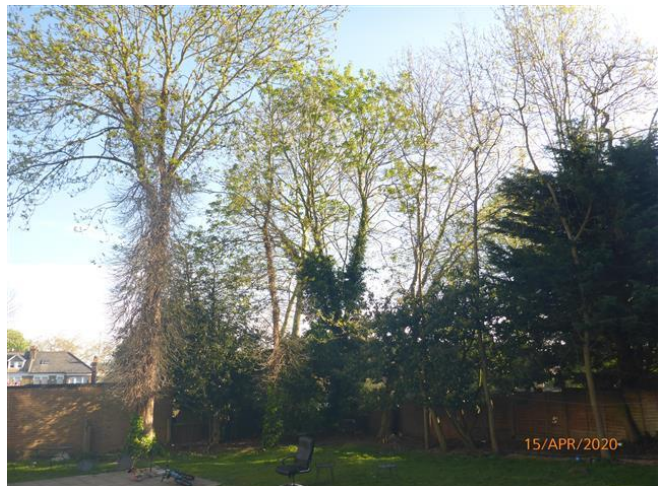


Photo 11.



Photo 12.





Appendix 1: BS 5837: 2012 – Guidance Notes

This Standard prescribes the principles to be applied to achieve a satisfactory juxtaposition of trees and structures. It sets out to assist those concerned with trees in relation to design, demolition and construction to form balanced judgements.

It acknowledges the positive contribution trees may offer to a site, as well as the negative aspects of retaining inappropriate trees. It addresses the negative impacts that construction activity may have upon trees and offers mitigation strategies to minimise these impacts.

The Standard suggests a three stage approach to ensure best practice is followed when developing close to trees:

A1.1 Stage 1: Survey Details and Notes

A ground level visual survey was undertaken. No climbed inspections or specialist decay detection were undertaken. Only trees with a stem diameter over 75mm, which lie within the site boundary or relatively close to it, were included.

Where applicable, trees with significant defects have been highlighted and appropriate remedial works have been recommended. However, this report should not be seen as a substitute for a full *Safety Survey* or *Management Plan* which are specifically designed to minimise risk and liability associated with responsibility for trees.

Wherever practicable dimensions were obtained using diameter tapes, logger's tapes, distometers and clinometers. Where obstacles prevent accurate measurement, dimensions are estimated. Trees on privately owned third party are surveyed from the best available vantage point and observations relating to the condition of these trees should be treated accordingly. All height measurements should be regarded as approximate.

Data is recorded for each tree and is presented in a Tree Data Schedule. Each tree is allocated a **Retention Category** according to its size, amenity value, condition and safe useful life expectancy. The categories are allocated independently of development proposals. Our interpretation of the Retention Categories is explained below:

A1.1.1 Retention Categories

A Category: Trees of high quality and amenity value. Usually, mature trees with a significant life expectancy which would enhance any development. Retention of these trees is strongly encouraged.

B Category: Trees of moderate quality and amenity value. Usually these are maturing trees or younger trees with exceptional form. Retention of these trees is desirable though the removal of occasional specimens may be acceptable.

C Category: Trees of low quality or small specimens with a relatively low amenity value. These trees are not considered to be a material planning constraint and their removal will generally be seen as acceptable in order to facilitate development.

U Category: Trees of such low quality that their removal is recommended regardless of development proposals.

Occasionally trees are borderline and do not fall neatly into one of the categories A, B or C. In such cases we apply a superscript (+/-) such that:

C* Indicates borderline C/B, though Category C is deemed to be most appropriate.

B* Indicates borderline C/B, though Category B is deemed to be most appropriate.



The British Standard suggests that each of the A, B and C categories may be further subdivided (A1, A2, A3, B1, B2, B3 etc) such that subcategory 1 denotes mainly arboricultural values, subcategory 2 denotes mainly landscape values and subcategory 3 denotes mainly cultural values (including conservation). Multiple subcategories may be used.

Our experience suggests that these subdivisions lack clarity and can be confusing. Within this report subcategories are **not** denoted. Where appropriate, the use of phrases such as 'Part of a formal group', or 'Has a high ecological value', or 'Offers good screening to the site' are incorporated into the observation section of the Tree Data Schedule. We believe this conveys all relevant landscape and cultural information without any confusion.

Tree Constraints Plan (TCP). This indicates the position, crown spread, Retention Category and Root Protection Area of each tree. It is used to inform where development may proceed without causing damage to trees.

Root Protection Area (RPA). This is the area around each tree likely to contain the majority of roots. It should ideally remain undisturbed to avoid a detrimental impact on tree health. For single stemmed trees it is calculated according to the formula "radius of RPA" = "12 x stem diameter". Where a tree has more than one stem, the equivalent-single-stem diameter is usually recorded. This is calculated by adding the squares of the stems and then finding the square root of this total. The radius of the Root Protection Area is then calculated by multiplying the equivalent-stem-diameter by 12.

Shade Constraints. The previous Standard (BS 5837 2005) suggested that shade constraints should be indicated on the TCP. These are denoted as a circle-segment drawn northwest to due east with a radius equal to the height of the tree. These do not represent the actual shade pattern which varies through the seasons. Rather, they indicate the area most shaded by the tree throughout the course of the year. Ideally habitable room windows should be located outside of these shade constraints. Where we consider it appropriate, we will include shade constraints information on our Impact Assessment Plan or Proposed Layout Plan.

A1.2 Stage 2: Arboricultural Impact Assessment

After the initial survey and the production of the Tree Constraints Plan, arborists and designers are encouraged to work together to establish a design proposal with minimal impact on the high quality trees. An assessment should be made of all possible impacts including the impact that the trees may have upon the proposal. The arborist may recommend mitigation strategies to minimise these impacts and help achieve a more harmonious juxtaposition between buildings and trees.

A1.3 Stage 3: Arboricultural Method Statement

This type of report specifies the measures necessary to protect trees against damage from construction activity. The Method Statement should be written in a manner that it may be conditioned and enforced by the local authority upon granting of planning permission. The site manager should be familiar with all aspects of the Method Statement and should ensure that all persons working on the site are aware of those aspects which appertain to their work. This includes service installation engineers and operators of plant machinery.



Appendix 2: Explanation of Tree Data & Glossary

This section explains the terms used in the **Tree Data Schedule** (see Section 3 and Appendix 6).

A2.1 General Observations

Numbering System:	Each item of vegetation has its own unique number prefixed by a letter such that T1=Tree 1, G2=Group 2, H3=Hedge 3 and W4=Woodland 4, S5=Shrub 5.
Age Categories:	
Young	Usually less than 10 years old.
Semi-Mature	Significant future growth to be expected, both in height and crown spread (typically below 30% of life expectancy).
Early-Mature	Full height almost attained. Significant growth may be expected in terms of crown spread (typically 30-60% of life expectancy).
Mature	Full height attained. Crown spread will increase but growth increments will be slight (typically 60% or more of life expectancy).
Veteran	A level of maturity whereby significant management may be required in order to keep the tree in a safe condition.
Over Mature	As for veteran except management is not considered worthwhile.
Species:	Common names and Latin names are given.
Height:	Measured from ground level to the top of the crown.
Stem Diameter:	Taken at 1.5m above ground level where possible. On multi-stemmed trees this measurement may be taken at ground level, though usually an indication of the number of stems and average diameter is given, e.g. 3 x 30cm.
Crown Height:	Measured from ground level to the height at which the main crown begins. Where the crown is unbalanced it is measured on the side deemed to be most relevant. This is usually the side facing the area of anticipated development.
Tree Diagram:	This scaled drawing is computer generated based on measurements taken for stem diameter, crown height and spread, and overall height. It is designed to help the reader rapidly assess the data. It is not an accurate representation of the form of the tree.
Crown Spread:	Measured N, E, S & W, taken from the centre of the stem and usually rounded up to the nearest metre.
Observations:	If a tree's position is considered to be relevant it will be commented upon (e.g. overhanging a children's play area). Tree form and pruning history are also recorded along with an account of any significant defects. Defects and descriptive terms are dealt with in more detail at the end of this section.
Recommendations:	Usually based on any defects observed and intended to ensure that the tree is in an acceptable condition.
Priority Scale:	Depending upon the threat posed by the tree, and the likelihood of failure, recommendations should be carried out according to the following priority scale:
Urgent	To be carried out as soon as possible.
Very High	To be carried out within 1 month.
High	To be carried out within 3 months.
Moderate	To be carried out within 1 year.
Low	To be carried out within 3 years.
Inspection Frequency:	An interval of 6 months, 1 year, 1.5 years or 3 years is allocated before the next inspection is due. Wherever practical, consideration should be given to seasonal changes so that deciduous trees are not always surveyed in winter when they have no leaves, or in summer when leaves may obscure branches within the upper crown.
Vigour:	An indication of growth rate and the tree's ability to cope with stresses:
High	Having above average vigour.
Moderate	Having average vigour.
Low	Having below average vigour.
Very Low	Tree is struggling to survive and may be dying.
Physiological Condition:	
Good	Healthy and with no symptoms of significant disease.
Fair	Disease present or vigour is impaired.
Poor	Significant disease present or vigour is extremely low.
Very Poor	Tree is dying.
Structural Condition:	
Good	Having no significant structural defects.
Fair	Some defects observed though no high priority works are required.
Poor	Significant defects found. Tree requires monitoring or remedial works.
Very Poor	Major defects which will usually require significant remedial works or tree removal.
Amenity Value:	
Very High	Exceptional specimen, observable by a large number of people.
High	Attractive specimen, observable by a significant number of people.
Moderate	One of the above factors is not applicable.
Low	Unattractive specimen or largely hidden from view.
Life Expectancy:	The estimated number of years before the tree may require removal. Classified as (<10), (10 – 20), (20 – 40), or (40+).
Retention Category:	These are explained in detail in Appendix 1.

A2.2 Evaluation of Defects

Cavities, wounds, deadwood etc are all evaluated as follows:

Major	Such that structural integrity is, or will become, compromised and the tree is, or will inevitably become, hazardous.
Significant	A defect that may over time become a major defect, though not necessarily so. This will depend on the vigour of the tree and its ability to deal with decay etc.
Minor	A defect that is not likely to compromise the tree's structural integrity.



General Glossary

Adaptive growth	In tree biomechanics, the process whereby wood formation is influenced both in quantity and quality by the action of gravitational forces and mechanical stresses on the cambial zone.
Aerobic	Conditions in which oxygen is freely available, or to biomechanical processes that depend on the presence of oxygen.
Anaerobic	A condition marked by the absence of oxygen; Generally such areas are unsuitable for normal life and growth of plant tissues. These sites tend to be populated by bacteria capable of surviving low oxygen conditions often associated with Slime Flux.
Arboriculture	The culture and management of trees as groups and individuals primarily for amenity and other non-forestry purposes.
Arborist	A person possessing the technical competence through experience and related training to provide management of trees or other woody plants in a landscape setting. Generally involved with the development or management of trees for visual amenity or land management rather than the growth of trees for product or profit.
Barrier zone	A layer within an annual increment of wood which contains abnormal xylem cells, laid down by the cambium in response to wounding or other trauma.
Body language	In trees, the outward display of growth responses and or deformation in response to mechanical stress.
Bole	Or Trunk, the main stem of a tree below its first major branch.
Bracket	A type of fruiting body produced by various fungal species, plate like to hoof like in shape and often a one sided attachment to the wood or bark.
Branch bark ridge	A ridged area located at the union of a branch to a trunk or stem.
Branch Collar	Trunk tissue that forms around the base of a branch between the main stem and the branch, or between a main branch and a lateral branch. As a branch decreases in vigour or begins to die, the collar usually becomes more pronounced and completely encircles the branch.
Brown Rot	Form of decay where cellulose is degraded, while lignin is only modified.
Buttress Root	Roots that emerge from the base of the tree stem, normally large and well developed that rapidly reduce in diameter to create the Root Plate this offers structural support for the tree. Buttress roots divide rapidly forming the connection between the stem and the transport roots.
Cabling Bracing	Installing cables within the crown of a tree to prevent collapse.
Callus	Undifferentiated cells often formed at the edges of recent injuries. This tissue quickly becomes differentiated, forming cells of the type characteristic of that position on the tree (e.g. forming wood, bark, roots, etc.) see wound response tissue.
Cambium	A thin layer of actively growing and dividing cells, located between the xylem (sapwood) and bark of a plant; the part responsible for radial growth of a tree stem or branch.
Canopy	The topmost layer of twigs and foliage in a woodland, tree or group of trees.
Canker	A localised area of dead bark and cambium on a stem or branch, caused by fungal or bacterial organisms, characterised by woundwood development on the periphery. This may be annual or perennial.
Cavity	An open and exposed area of wood, where the bark is missing and internal wood has been decayed and dissolved.
Chlorotic	Also Chlorosis. A condition of the plant marked by yellowing of normally green foliage, often indicating nutrient deficiency or plant dysfunction.
Clinometer	Devices that measures vertical angles, and provides direct height measurements of objects by triangulation.
Co-dominant stems/trunk	Are forked branches or trunks of nearly the same size in diameter and lacking a normal branch union.
Compacted soils	Soils in which the air-space (oxygen space) has been reduced or eliminated, reducing water infiltration and percolation, reducing root presence and inhibiting new root development.
Compartmentalisation	The physiological process that creates the chemical and mechanical boundaries that act to limit the spread of disease and decay organisms.
Compression Failure	Localized buckling of fibres and other longitudinal elements produced by compression of wood along the grain; compression failures sometimes develop in standing trees.
Compression Strength	The ability of a material or structure to resist failure when subjected to compressive loading; measurable in trees using special drilling devices
Compression Wood	Abnormal wood formed on the lower side of branches and curved stems, with physical properties different from normal wood.
Conservation Area	In Great Britain, designated areas of architectural or historical interest, in which there are special procedures for planning applications. Additionally tree works cannot generally be undertaken without prior notification (Currently 6 weeks) to the relevant local planning authority. See also Tree Preservation Orders.
Core Sample	A sample of wood extracted from a trunk or branch, using an increment borer tool. The resulting core can be analysed for characteristics of growth, wood strength, structure, decay, and for species identification.
Crotch	The union of two or more branches; the auxiliary zone between branches.
Crown	The upper canopy of a tree, including upper trunk, scaffold branches, secondary branches, stems and leaves.
Crown lifting / raising	Crown Lift The removal of the lowest branches, usually to a given height. It allows more residual light and greater clearance underneath for vehicles etc.
Crown reduction	The reduction of a tree's height or spread while preserving its natural shape.
Crown thinning	The removal of some of the density of a tree's crown, usually 5-25% allowing more light through its canopy and reducing wind resistance.
Deadwood (noun)	Deadwood is often present within the crown or on the stems of trees. It may be an indication of ill health, however, it may also indicate natural growth processes. If a target is present beneath the tree, deadwood may fall and cause injury or damage and should be removed, otherwise deadwood can remain intact for conservation purposes (insects, fungi, birds etc.).
Deadwood (verb)	The removal of dead branches from a tree's canopy, usually of a specified size (in diameter).
Decay	Progressive deterioration of organic tissues, usually caused by fungal or bacterial organisms, resulting in loss of cell structure, strength, and function. In wood, the loss of structural strength.
Decay Detection	The assessment of decay within a tree has been traditionally difficult, but recent advances have made it possible to achieve accurate representations of the internal section of a tree in both 2D and 3D, removing doubt over the condition of the tree and allowing accurate management decisions.
Defect	In relation to tree hazards, any feature of a tree which detracts from the uniform distribution of mechanical stress, or which makes the tree mechanically unsuited to its environment.
Defoliation	The losing of plants foliage.
Dieback	Progressive death of buds, twigs and branch tissues, on individual limbs resulting in Deadwood, or throughout the canopy,



	extreme cases can result in Stag Heading.
Dripline	A projected line on the ground that corresponds to the spread of branches in the canopy; the farthest spread of branches.
Epicormic shoots	Fast growing, weakly attached shoots/branches that often grow as a response to stress factors upon a tree or branch removal.
Failure	In connection with tree hazards, a partial or total fracture within the wood tissue or loss of cohesion between roots and soil. (In total failure affected parts will snap or tear away completely, Partial failure there is a crack or deformation, which results in an altered distribution of mechanical stress.
Feeder Roots	Fine fibrous Water and nutrient absorbing roots located in the outer root system.
Flush-Cut	In trees and shrubs, a pruning cut close to the parent stem, which removes the branch bark ridge.
Foliage	The live leaves or needles of the tree; the plant part primarily responsible for photosynthesis.
Formative pruning	The trimming of a tree to remove weaknesses and irregularities which may lead to problems. The formative pruning operation is aimed at reducing the potential for future weaknesses or problems within the tree's crown.
Gall	An abnormal, disorganized growth of plant tissues, caused by parasitic or infectious organisms such as insects, fungi, bacteria, or viruses.
Girdling	In woody plants, any form of damage that destroys the bark and / or the Cambium all the way around the stem, branch or root, normally resulting in death of the damaged section.
Girdling Root	In woody plants, a root that grows across the buttress, or across other roots, eventually causing constriction of the radial growth.
Growth Increment	The incremental growth added as new annual ring develops each season over existing wood. This is seen as (growth) rings in cross-sections of wood.
Hazard beam	An upwardly curved branch in which strong internal stresses may occur without the compensatory formation of extra wood (longitudinal splitting may occur in some cases).
Heartwood	Inner non functioning tissues that provide structural support to trunk.
Heave	In relation to shrinkable clay soils, expansion due to rewetting of a volume of soil previously subjected to the removal or water by plant / trees following felling or root severance. Also in relation to root growth, the lifting of pavements and other structures by radial expansion. Also in relation to tree stability, the lifting of one side of a wind rocked root plate.
Herbicide	A chemical compound that causes the death of a plant.
Included Bark	Bark that becomes embedded in a crotch between branch and trunk or between co-dominant stems, usually found in narrow or tight crotches, and causes a weak structure.
Increment Borer	A tool that cuts and extracts a narrow cylinder of wood from a tree for analysis of the wood tissue and growth increments.
Leader	The primary terminal shoot or trunk of a tree.
Limb	A large lateral branch growing from the main trunk or from another larger branch.
Lion Tailing	Often the result of poor pruning practices; the main leader or branches are largely devoid of side branches, growth is restricted to the end of branches and is likely to suffer damage through end loading.
Lopping	In trees, a general term that related to the removal of branches from a tree.
Monitoring	Due to the relative life span of trees in relation to our own, long-term monitoring provides a valuable insight to the health of trees, identifying decline and or stabilisation and or improvement.
Mulch	A material laid over the root system of a tree to help conserve moisture within the soil. Additionally it may help control the development of weeds close to the tree.
Mycelium	A mass of growing filaments (hyphae) formed by fungi.
Mycorrhizae	The symbiotic relationship between roots and certain beneficial fungi. Mycorrhizae are the combined root / fungal growth.
Occluding tissue	The general term of wood, cambium and bark that develop around the site of a wound on a woody plant
Pathogen	A microorganism that causes diseases within another organism.
Phloem	The principle conductive tissue that the products of Photosynthesis are transported around the plant
Photosynthesis	The process were light energy is used to create energy (Carbohydrate) for use within the plant.
Pollard	A term for a pollarded tree.
Pollard head	The swollen section of branch / stem that forms behind the pollarding cut.
Pollarding	The complete or partial removal of the crown of a young tree so as to encourage the development of numerous branches either for amenity or historically as fodder, repeated management is required cyclically to maintain the feature
Prune or Pruning	Selective removal of woody plant parts of any size, using saws, Loppers, Secateurs, or other pruning tools.
Reaction Wood	Wood with distinctive anatomical characteristics, formed in parts of leaning or crooked stems and in branches to provide additional strength / support. In hardwoods, tension wood usually forms. In conifers, compression wood is usually found.
Reaction Zone	A zone normally darker than surrounding wood that denoted the boundary often a defensive one between functional sapwood and dysfunctional or decaying wood.
Re-grading	The raising or lowering of a soil profile from its original grade.
Remedial pruning	The removal of old stubs, deadwood, epicormic growth, rubbing or crossing branches and other unwanted items from the tree's crown.
Resistograph	Invasive decay detection technique whereby the resistance offered by the timber to a spinning probe is measured and plotted.
Rib	In tree body language, a long narrow, axial protuberance which often over lays a crack.
Ring Barking	Artificial Girdling of the stem, to result in the death of a tree. May be used in habitat creation were the retention of dead standing trees is required.
Rod Bracing / Bolting	Traditionally, this has relied upon the installation of steel rods or bolts through the stems or limbs, to reduce twisting or splitting of the wood. The installation of such features does require legal interpretation.
Root Barriers	Both Buildings and services can benefit from the installation of root barriers to protect a soil volume from the ingress of roots.
Root Collar	The basal area of the tree; transition zone from trunk to root. Also sometimes called trunk flare.
Root Plate	The primary support area for the tree; an area of the root system close to the base that structurally anchors the tree to the soil.
Root Rot	Either a general term for decay within the wood of the lower stem / buttress roots, or a disease in which the fine roots are killed.
Root System	The portion of the tree containing the root organs, including buttress roots, transport roots, and fine absorbing roots; all underground parts of the tree.
Root Zone	The area and volume of soil around the tree in which roots are expected. May extend to three or more times the branch spread of the tree, or several times the height of the tree.
Sail Area	That area or the tree subjected to wind load.



Arboricultural Report to BS 5837: 2012 for: Stockwool

Crown Ref: 10524

Site: 9 Waverley Road, London

Author: Emma Hoyle

Date: 14th May 2021

Sapwood	Xylem wood tissue, usually light in colour, representing the outer growth rings of the wood. Usually living, reactive wood tissue, in a healthy tree. See heartwood
Scaffold limbs / scaffold Branches	The branches that from the main network framework of the crown of a tree.
Senescent	A decline in growth and vigour due to age or stress factors.
Shrub	A woody plant that branches at or close to the ground level and so does not have a single stem.
Slime Flux	Relating to a toxic condition from the spreading of bacteria or their products from a source of infection; characterized by malodorous gases, or salt deposits upon the bark. If these products enter the sap stream, localised vessel necrosis can result, usually associated with anaerobic conditions.
Soft Rot	A kind of wood decay, were a fungi degrades cellulose within the cell wall, without causing overall degradation.
Soil Compaction	The compression of soil, causing a reduction of pore space and an increase in the density of the soil. Air is squeezed out and nutrients become locked. Tree roots cannot grow in compacted soil.
Sonic Decay Detection	Non invasive method whereby sound waves are passed through the tree and the speed is measured. Slow speeds indicate decay and a tomography picture representing the inner stem is produced.
Stag Heading	In a tree, a state of dieback where dead branches protrude beyond the current living crown.
Stress	In plant physiology, conditions where one or more physiological functions are not working within normal parameters.
Stump Grinding	The removal of a tree stump using a specialist grinding machine.
Subsidence	In relation to vegetation, the removal of water by plant growth resulting in localised shrinkage in the soil volume.
Sucker	Same as sprout.
Suppressed	Trees which are dominated by surrounding vegetation and whose crown development is restricted from above.
Systemic	Affecting the whole plant or organism. A systemic compound is carried throughout the entire plant to all parts through the vascular system.
Target	Any person or object within reach of a falling tree or part of a tree that may be injured or damaged.
Target Pruning	The pruning of a branch where the wound affects only branch material, often result in a target shaped wound.
Tension Wood	Reaction wood typically formed on the upper side of limbs or curved stems; characterized by lack of cell wall lignifications (higher ratios of cellulose to lignin).
Tight Union / Tight Crotch	Also, narrow crotch. A crotch with a narrow angle between branches, often having included bark.
Tomography	The comparison of sound or stress waves through the tree allows the creation of a 2D or 3D representation of the internal structure of a stem or branch section and highlights areas of damage. Virtually non-injurious.
Topography	The configuration of surface features, including the vertical and horizontal relationships of the ground and other features.
Topping	Cutting large limbs back severely, without regard to form or habit of the tree. Cuts are usually made between lateral branch nodes. This practice is extremely injurious to trees, and promotes decay and structural weakness within the crown.
Tree	A woody plant that typically has a single stem, at maturity has a height of at least 4 metres and a stem diameter at breast height of at least 75mm.
Tree Preservation Order	In Great Britain, an order made by the local planning authority, where consent must be gained before undertaking all but exempt works to a tree.
Trunk Flare	The basal area of the trunk that flares or widens, and merges with the main roots. See root collar
Veteran Tree	Veteran trees are often found in large parks or estates and commonly affected by extensive decay or have been subject to extensive works. These trees are retained for historical importance and often pose greater risk than normal, which is generally justified. They need careful management and often propping or bracing to support them, some require fencing to limit access.
Vigour	Active, healthy growth of plants: ability to respond to stress factors.
Visual Tree Assessment (VTA)	An assessment of the mechanical condition of trees based upon their 'body language'. Trees are dynamic and respond to faults / decay / environmental factors in various ways, these responses can be indicative of structural integrity.
Wetwood	An infection caused by bacteria living inside the plant tissues. The bacteria ferment the plant fluids, resulting in death of nearby cells, and often causing exudations of fluid from the bark, often referred to as a Slime Flux.
White Rot	A kind of wood decay where a fungi attacks the lignin within the wood matrix
Wind loading	Forces placed upon tree canopy, branches, trunk and roots of a tree under windy conditions.
Wind Throw	The failure of a tree due to wind loading.
Witches Broom	A deformed or unusual growth of twigs from adventitious buds, caused by insects, disease, or dieback of twigs and buds.
Wood	Secondary Xylem; the main structural support and water conducting tissue of trees and shrubs.
Wound Response Tissue	Also Occluding Tissue, Wound Wood or Callus. Differentiated wood tissue that grows around the margins of a wound or injury.
Wound Wood	Wood with atypical features, formed in the vicinity of a wound and a term to describe the occluding tissues around a wound
Xylem	Plant tissues with special function of translocation of water and dissolved nutrients.



Appendix 3: Survey Methodology

Ground level visual surveys are carried out using the *Visual Tree Assessment* technique described by Mattheck and Broeler (1994) and endorsed by the Arboricultural Association (LANTRA Professional Tree Inspection course, 2007).

Structural condition is assessed by inspecting the stem and scaffold branches from all angles looking for weak branch junctions or symptoms of decay. Particular attention is paid to the stem-base. Cavities are explored using a metal probe in order to assess the extent of any decay. If this is not possible further inspection is recommended in the form of a climbed inspection or using specialist decay detection equipment.

The physiological condition is assessed by inspecting the stem, branches and foliage for symptoms of disease. The overall vigour of the tree is also taken into account.

Where significant defects are observed, recommendations are made according to a scale of priority in order to reduce the likelihood of structural failure. The position of the tree and its potential targets are taken into account.

Measurements are obtained using a diameter tape, clinometer, distometer and loggers tape. Where this is not practical measurements are estimated.

Some trees are surveyed as groups, though this is usually avoided close to areas likely to be developed.

Finally, a *Retention Category* is allocated as described in Appendix 1.1.1.



Appendix 4: Author's Qualifications

Qualifications & Experience of Ivan Button N.C.H. (Arb), FDS (Arb), BSc (Hons), P.G.C.E., M. Arbor. A.

Between 1983 and 1995 Ivan worked primarily within the construction industry and received training in a broad range of practical building skills and general construction principles. During this time he obtained a BSc (Hons) at Leeds University followed by a P.G.C.E at The University of Wales.

In 1995, Ivan obtained a NCH (Arboriculture) at the University of Lincoln and became a member of the Arboricultural Association. He then worked for an Arboricultural Consultancy for one year before establishing a tree surgery and landscaping business in 1998. In 2005 Ivan commenced full time employment with a leading Arboricultural Association approved consultancy and soon adopted a senior role responsible for five consultants.

He obtained a FDS in arboriculture at the University of Lancashire, which he passed with distinction and is now a Director and Principal Consultant of Crown Consultants Ltd. He is accredited as a LANTRA *Professional Tree Inspector*. A qualification produced in association with the Arboricultural Association and generally recognised as appropriate for all levels of tree inspection.

Ivan is a professional member of the Arboricultural Association, the International Society of Arboriculture and the Consulting Arborist Society

Ivan is trained and licensed in QTRA (Quantified Tree Risk Assessment). He has undertaken professional expert witness training provided by Bond Solon and has been registered as a Sweet and Maxwell Checked Expert Witness from 2008-2017, after which the service was no longer offered.

Throughout 2009 acted as the principal Tree Officer for Barnsley Metropolitan Borough Council.

Ivan has produced several hundred Arboricultural Reports for the purposes of Development, Safety, Management, Mortgage, Subsidence, Mitigation and Litigation.

Qualifications & Experience of Emma Hoyle FDS (Arboriculture), ED (Forestry & Arboriculture), M. Arbor. A.

Emma is a qualified Arboricultural Consultant educated to Level 5 in Arboriculture at Askham Bryan College and is a professional member of the Arboricultural Association. She has worked for Crown Consultants since 2015 and has since written numerous reports relating to all aspects of arboriculture including; planning and development, vegetation related subsidence, tree preservation orders and tree risk assessment. Emma regularly attends seminars and events in order to keep abreast with current knowledge and best practise in Arboriculture.

Prior to becoming an arboricultural consultant, Emma worked for two reputable tree surgery firms from 2008 and became an NPTC Qualified tree surgeon after completing a Level 3 Extended Diploma in Forestry and Arboriculture at Askham Bryan College. Emma also has experience in other areas of arboriculture such as forest clearance, tree planting, tree maintenance and landscaping.

Qualifications & Experience of Joe Taylor - MArborA, FdSc (Arboriculture)

Joe began his career in Arboriculture as a tree surgeon/climber. During his time as a tree surgeon, Joe has achieved City & Guilds NPTC qualifications in Chainsaw Maintenance and Cross Cutting, Tree Climbing and Rescue, Safe Use of Manually Fed Wood-chipper and Supporting Colleagues Undertaking Tree Related Operations.

Joe obtained a Foundation Degree in Arboriculture at Askham Bryan College in 2015 which he passed with merit. Joe is a professional member of the Arboricultural Association, the International Society of Arboriculture and the Royal Forestry Society and regularly attends industry related seminars in order to keep abreast of industry best practice.

Studying at Askham Bryan College reinforced Joe's passion for trees and drove his enthusiasm to learn more. Learning how trees interact with their surrounding environment and their importance within our urban and rural landscapes highlighted an interest in pursuing a career in consultancy.

Since working for Crown Consultants Joe has undertaken numerous surveys and produced numerous reports for the purpose of planning (BS 5837), tree condition surveys, subsidence risk assessments, root surveys and decay detection investigations.



PDF readers select page-width for detail & page-view for scrolling

Arboricultural Report to BS 5837: 2012 for: Stockwool

Crown Ref: 10524

Site: 9 Waverley Road, London

Author: Emma Hoyle

Date: 14th May 2021

Appendix 5: Further Information

Building Near Trees – General

National Joint Utilities Group publication # 10 (1995), *Guidelines for the Planning, Installation and Maintenance of Utility Services in Proximity to Trees*. Downloadable at www.njug.demon.co.uk/pdf/NJUG%20Publication10.pdf

NHBC Standards Chapter 4.2., *Trees and Buildings*.

Horticulture LINK project 212. (University of Cambridge, 2004), *Controlling Water Use of Trees to Alleviate Subsidence Risk*.

Tree Planting and aftercare

See www.trees.org.uk/leaflets.php# for downloadable leaflets on selecting a garden tree, planting, aftercare and veteran tree management.

British Standards

BS 5837: 2012. Trees in Relation to Design, Demolition and Construction – Recommendations.

Bs 3998: 2010. Recommendations for Tree Work.

BS 3936: 1992. Nursery Stock. Part 1: Specification for Trees and Shrubs.

BS 3936: 1992. Nursery Stock. Part 10: Specification for Groundcover Plants.

BS 4043: 1989. Transplanting Root-balled Trees.

BS 8004: 1986. Foundations.

BS 8103: 1995. Structural design of Low-Rise Buildings.

BS 8206: 1992. Lighting for Buildings.

BS 8545:2014. Trees: From nursery to independence in the landscape – Recommendations

BS 3882: 2007. Topsoil.

BS 4428: 1989. General Landscaping Operations (excluding hard surfaces).

Permission to do Works to Protected Trees / Tree Law

Forestry Commission (Edinburgh, 2003), *Tree Felling – Getting Permission*. Country Services Division - Forestry Commission. Downloadable at [www.forestry.gov.uk/website/pdf.nsf/pdf/wgsfell.pdf/\\$FILE/wgsfell.pdf](http://www.forestry.gov.uk/website/pdf.nsf/pdf/wgsfell.pdf/$FILE/wgsfell.pdf)

Transport and the Regions (Department of the Environment, 2000), *Tree Preservation Orders, A Guide to the Law and Good Practice*. Downloadable at www.communities.gov.uk/publications/planningandbuilding/tposguide

C. Mynors, *The Law of Trees, Forests and Hedgerows* (Sweet and Maxwell, London, 2002)

Communities and Local Government website with numerous downloadable documents, from:

<http://www.communities.gov.uk/planningandbuilding/planning/treeshighhedges/>

Lighting Levels

P.J. Littlefair, B.R.E. 209: *Site layout planning for daylight and sunlight A guide to good practice*. B.R.E. Bookshop, London.

British Standards Institution. Code of practice for day lighting. *British Standard BS 8206: Part 2* (1992).

Chartered Institution of Building Services Engineers. *Applications manual: Window Design* (London, 1987).

NBA Tectonics. A study of passive solar housing estate layout. *ETSU Report S-1126*. Harwell, Energy Technology Support Unit (1988).

I.P. Duncan; D. Hawkes, Passive solar design in non-domestic buildings. *ETSU Report S-1110*. Harwell, Energy Technology.

P. J. Littlefair, Measuring Daylight, *BRE Information Paper 23/93 f3.50*. (Advises on measuring daylight under the real sky or an artificial sky, allowing for the changing nature of sky light).

High Hedges

Communities and Local Government website with numerous downloadable documents, from:

<http://www.communities.gov.uk/planningandbuilding/planning/treeshighhedges/>

Tree Specific Websites

www.crowntrees.co.uk

Crown Consultants site containing useful information

www.trees.org.uk

Arboricultural Association

www.rfs.co.uk

Royal Forestry Society of England, Wales and N. Ireland

www.treehelp.info

The Tree Advice Trust

www.woodland-trust.org.uk

The Woodland Trust

www.treecouncil.org.uk

The Tree Council



PDF readers select *page-width* for detail & *page-view* for scrolling

Arboricultural Report to BS 5837: 2012 for: Stockwool

Crown Ref: 10524

Site: 9 Waverley Road, London

Author: Emma Hoyle

Date: 14th May 2021

Appendix 6: Tree Data Schedule, Site Plans & Arboricultural Method Statement.

The Tree Data Schedule and any drawings accompanying this report follow this page.
They are also provided as separate documents for ease of printing and screen viewing.


Reference G = Group H = Hedge	Age & Species	Height (m)	Crown Ht (m)	Diameter (cm)	Crown Spread (m) N W E S	Scaled Tree Diagram (m)	Notes	Recommendations (Independent of any development proposals)		Vigour	Amenity Value
								Priority	Inspect Freq (yrs)	Physiological Condition	Life Expectancy (yrs)
										Structural Condition	Retention Category
T1	Mature Purple Beech Fagus sylvatica 'purpurea'.	22	2	110 @ Base	8 9 9 9.5		Form: Multi-stemmed at 2m with a well-formed crown. History: Occasional pruning wounds due to crown lifting. Defects: Significant cavity forming at 2.5m above ground level to south.	Inspect cavity for decay.		Moderate Fair Fair	High 20-40 A
		High	1								
T2	Semi-Mature Yew Taxus baccata.	3.5	2	20	3 3 3 3		Position: Situated on third party land. Form: Single stemmed and vertical with a balanced crown. History: No evidence of significant pruning. Defects: No significant defects observed. Other: Limited inspection, dimensions estimated.	No action required.		High Good Good	Low 40+ C
		n/a	3								
T3	Mature Lime Tilia sp.	15	2	81	5 5.5 5 5.5		Form: Single stemmed and vertical with a balanced crown. History: No evidence of significant pruning. Defects: No significant defects observed. Other: Epicormic shoots throughout stem & ivy prevented detailed inspection.	Remove ivy and inspect stem for defects.		Moderate Fair Fair	High 20-40 B
		Moderate	1								
T4	Early-Mature Ash Fraxinus excelsior.	15	6	49	6 6.5 5 7		Form: Twin-stemmed at 6m with a balanced crown. History: No evidence of significant pruning. Defects: No significant defects observed.	No action required.		Moderate Good Good	Moderate 40+ A
		n/a	3								
T5	Semi-Mature Ash Fraxinus excelsior.	8	3.5	21	0.5 2 1 3		Form: Single stemmed with a slight lean and an unbalanced crown. History: No evidence of significant pruning. Defects: No significant defects observed.	No action required.		High Good Good	Low 20-40 C
		n/a	3								
T6	Semi-Mature Holly Ilex aquifolium.	5	1	26	3 3 3 3		Form: Single stemmed and vertical with a balanced crown. History: No evidence of significant pruning. Defects: No significant defects observed.	No action required.		High Good Good	Low 40+ C
		n/a	3								
T7	Early-Mature Sycamore Acer pseudoplatanus.	13	6	45	5 5 5 4		Form: Single stemmed with a slight lean and an unbalanced crown. History: No evidence of significant pruning. Defects: No significant defects observed. Other: Ivy prevented detailed inspection. Limited inspection, dimensions estimated.	Remove ivy and inspect stem for defects.		Moderate Good Fair	Low 40+ B
		Moderate	3								

Reference G = Group H = Hedge	Age & Species	Height (m)	Crown Ht (m)	Diameter (cm)	Crown Spread (m) N W E S	Scaled Tree Diagram (m)	Notes	Recommendations (Independent of any development proposals)		Vigour	Amenity Value
								Priority	Inspect Freq (yrs)	Physiological Condition	Life Expectancy (yrs)
										Structural Condition	Retention Category
T8	Semi-Mature London Plane Platanus x hispanica.	12	3	43	4 2 7 6		Form: Single stemmed with a slight lean and an unbalanced crown. History: No evidence of significant pruning. Defects: Cavity observed where secondary stem has torn out in the past.	Inspect cavity for decay.		Moderate Good Fair	Low 20-40 B -
	Moderate	3									
G9	Semi-Mature Ash Fraxinus excelsior.	av 12	av 2	av 20	av 2.5 2.5 2.5 each		Form: Four close growing specimens. History: No evidence of significant pruning. Defects: No significant defects observed.	No action required.		High Good Good	Low 40+ B -
	n/a	3									
T10	Semi-Mature Ash Fraxinus excelsior.	12	6	25	3 1.5 5 3		Form: Single stemmed and leaning with an unbalanced crown. History: No evidence of significant pruning. Defects: No significant defects observed. Other: Stem leans over boundary fence and wraps around 3 sides of the stem of T11.	No action required.		High Good Good	Low 40+ C
	n/a	3									
T11	Semi-Mature Lawson Cypress Chamaecyparis lawsoniana.	7	2	30	4 4 4 4		Position: Situated on third party land. Form: Single stemmed and vertical with a balanced crown. History: No evidence of significant pruning. Defects: No significant defects observed. Other: Stem of T10 wraps around stem in 3 places.	No action required.		High Good Good	Low 40+ C
	n/a	3									
T12	Dead Pear Pyrus sp.	5	2	22	0.5 2 1.5 1.5		Form: Dead specimen.	Remove.		Dead Dead Dead	Dead Dead U
	Moderate	N/A									
T13	Early-Mature Elder Sambucus nigra.	5	3	21	2.5 1.5 0.5 0.5		Form: Twin-stemmed at 1m with an unbalanced crown. History: No evidence of significant pruning. Defects: Decay tp multiple branches and scattered dead twigs throughout. Other: Poor specimen. Recorded stem diameter is equivalent for 2 stems (17cm, 12cm).	No action required.		Low Poor Fair	Low <10 C
	n/a	3									
T14	Mature False Acacia Robinia pseudoacacia.	14	4	85	6.5 3 4 4		Position: Situated on third party land. Form: Twin-stemmed at 3m with an unbalanced crown. History: Central stem reduced back to main fork. Defects: No significant defects observed. Other: Limited inspection, dimensions estimated.	No action required.		Low Poor Fair	Low 10-20 C +
	n/a	3									

Reference G = Group H = Hedge	Age & Species	Height (m)	Crown Ht (m)	Diameter (cm)	Crown Spread (m) N W E S	Scaled Tree Diagram (m)	Notes	Recommendations (Independent of any development proposals)		Vigour	Amenity Value
										Physiological Condition	Life Expectancy (yrs)
								Priority	Inspect Freq (yrs)	Structural Condition	Retention Category
H15	Early-Mature Yew Taxus baccata.	7	1.5	40	3 3 3		Position: Situated on third party land. Form: Vertical hedgerow. History: Topped at 7m. Defects: No significant defects observed. Other: Limited inspection, dimensions estimated.	No action required.		High Good Good	Low 40+ C
								n/a	3		
T16	Early-Mature Purple Beech Fagus sylvatica 'purpurea'.	10	4	55	4 5.5 5		Position: Situated on third party land. Form: Single stemmed with a slight lean and an unbalanced crown. History: Central stem reduce to a height of 7m. Defects: No significant defects observed. Other: Limited inspection, dimensions estimated.	No action required.		Moderate Good Fair	Low 20-40 B -
								n/a	3		
T17	Mature Lime Tilia sp.	20	2	104	6.5 6 6		Form: Multi-stemmed at 7m with a balanced crown. History: No evidence of significant pruning. Defects: No significant defects observed. Other: Ivy prevented detailed inspection. Dense canopy.	Remedial prune and remove ivy and inspect stem for defects.		Moderate Fair Fair	High 20-40 B
								High	1.5		



See the accompanying report
for more photographs



MN = Measured North:
Canopy spreads are sometimes measured to an approximation defined by site features. Often more accurate, especially where rows of trees are not aligned N-S or E-W.

Tree Ref.	Species	Height (m)	Root Protection Area		
			Radius (m)	m ² Square (m)	
1	Purple Beech	22	11.0	380	19.5
2	Yew	3.5	2.4	18	3.3
3	Lime	15	9.7	297	17.2
4	Ash	15	5.9	109	10.4
5	Ash	8	2.5	20	4.5
6	Holly	5	3.1	31	5.5
7	Sycamore	13	5.4	92	9.6
8	London Plane	12	5.2	84	9.1
9	Ash	14	2.4	19	4.3
10	Ash	12	3.0	28	5.3
11	Lime Cypress	7	3.6	41	6.4
12	Pear	5	2.6	22	4.7
13	Eldest	5	2.5	20	4.5
14	False Acacia	14	10.2	327	18.1
15	Yew	4	1.8	72	9.5
16	Purple Beech	10	6.6	137	11.7
17	Lime	20	12.5	489	22.1

Drawing No:	CCL 10524 / TCP	Rev: 1
Title:	Tree Constraints Plan (Existing Layout)	
Site:	9 Waverley Road, London N8 9QS	




Tree Retention Categories
Stems & canopies shown

	Category A tree
	Category B tree
	Category C tree
	Category U tree


	Trees of high quality with an estimated life expectancy of 40+ years. Usually large trees with significant presence or smaller trees with excellent form. Retention of these trees is highly desirable.
	Trees of moderate quality with a life expectancy of 20+ years. Usually maturing trees, or younger trees with good form. Retention of these trees is desirable though less than Category A trees
	Unremarkable trees of low quality and merit. Individual specimens are not considered to be a material planning consideration.
	Trees unsuitable for retention due to their very poor condition.

Tree Constraints Plan



Impact Assessment Plan
(Existing Layout with Proposals Overlaid)

Proposed Ground Floor (Pale Green)
Proposed Lower Ground Floor Footprint (Pink)

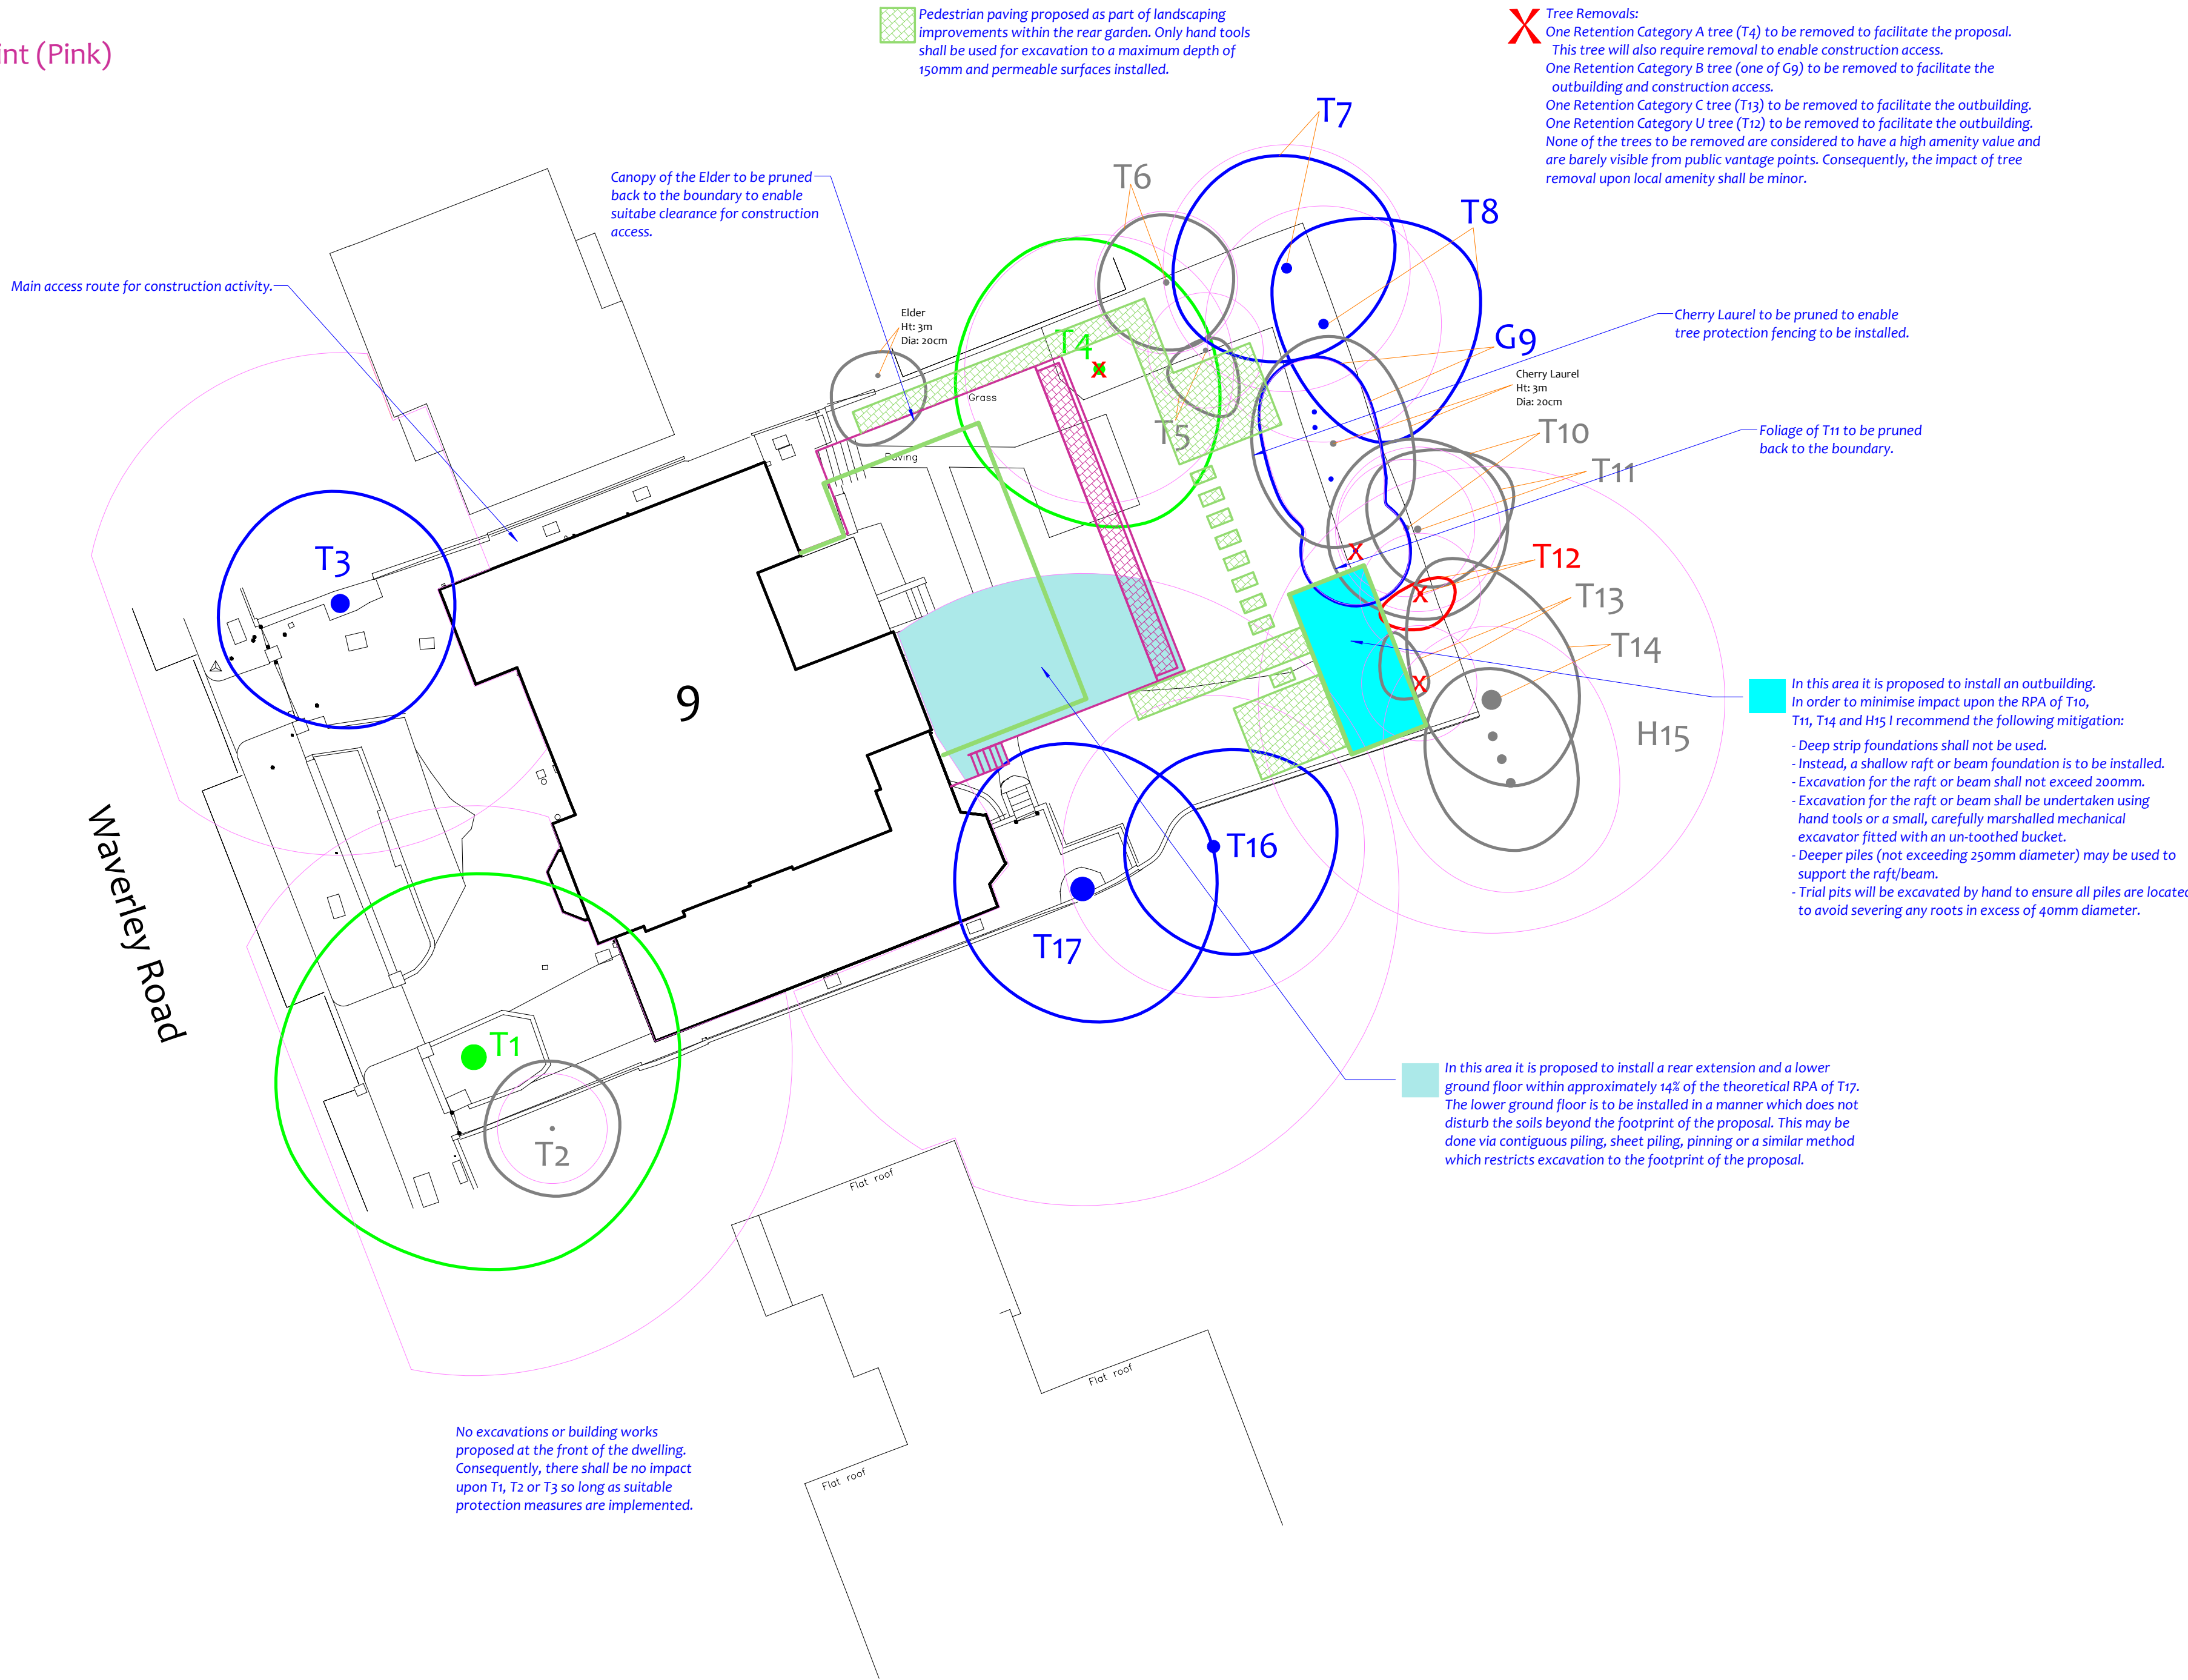


Tree Ref.	Species	Height (m)	Root Protection Area		
			Radius (m)	m ²	Square (m)
T1	Purple Beech	22	11.0	380	19.5
T2	Yew	3.5	2.4	18	4.3
T3	Lime	15	9.7	297	17.2
T4	Ash	15	5.9	109	10.4
T5	Ash	8	2.5	20	4.5
T6	Holly	5	3.1	31	5.5
T7	Sycamore	13	5.4	92	9.6
T8	London Plane	12	5.2	84	9.1
G9	Ash	12	2.4	18	4.3
T10	Ash	12	3.0	28	5.3
T11	Lawson Cypress	7	3.6	41	6.4
T12	Pear	5	2.6	22	4.7
T13	Elder	5	2.5	20	4.5
T14	False Acacia	14	10.2	327	18.1
H15	Yew	7	4.8	72	8.5
T16	Purple Beech	10	6.6	137	11.7
T17	Lime	20	12.5	489	22.1

Drawing No:	CCL 10524	/ IAP Rev: 1
Title:	Impact Assessment Plan (Existing Layout with Proposals Overlaid)	
Site:	9 Waverley Road, London N8 9QS	
Scale:	0 5 10m 1:2000	
Paper Size:	A1	
 CROWN Arboricultural Consultants 01422 316660	Tree Retention Categories Stems & canopies shown	
		Category A tree
		Category B tree
		Category C tree
	Trees of high quality with an estimated life expectancy of 40+ years. Usually large trees with significant presence or smaller trees with excellent form. Retention of these trees is highly desirable.	
	Trees of moderate quality with a life expectancy of 20+ years. Usually maturing trees, or younger trees with good form. Retention of these trees is desirable though less than Category A trees.	
	Unremarkable trees of low quality and merit. Individual specimens are not considered to be a material planning consideration.	
	Trees unsuitable for retention due to their very poor condition.	

Impact Assessment Plan
(Existing Layout with Proposals Overlaid)

	BS 5837 Root Protection Area (radius = 1xstem diameter)	
	Root Protection Area needing amendment due to site conditions, e.g. presence of existing road or building.	
	Root Protection Area having been amended to account for site conditions	
T1 = Tree No 1	G2 = Group No 2	H3 = Hedge No 3
		
		
		
		
		
		
		
		
		
		
		
		
		
		
		
		
		
		
		

MN = Measured North:
Canopy spreads are sometimes measured to an approximate N defined by site features. Often more accurate, especially where rows of trees are not aligned N-S or E-W.



Position	Name	Contact Phone & email	Roles
Project Manager	Insert Details	Insert Details	Liaising with site manager & project arborist regarding any potential issues relating to trees. Scheduling of meeting, excavations and inspections. Overseeing this monitoring schedule. Instructing the project arborist and arranging access. Liaising with local authority regarding discharge of planning conditions and variances to the Arboricultural Method Statement.
Site Manager	Insert Details	Insert Details	Day to day monitoring of tree protection measures. Fortnightly supply of site photographs showing all tree protection measures. Induction of all contractors. Reporting to the Appointed Arborist of any incidents or potential variations to the agreed tree protection measures. Liaising with LPA Tree Officer over all arboricultural matters. Initial inspection and signing off of tree protection barriers including ground protection measures. Monthly site visits and inspections. Oversight of excavation for basement down to 1.2m in Restricted Zones. Reporting to the local authority following site inspections and any variation or incidents.
Project Arborist	Crown Tree Consultancy Ltd 08000 14 13 30 0203 797 7449 info@crownntrees.co.uk	08000 14 13 30 0203 797 7449 info@crownntrees.co.uk	Reporting to the local authority following site inspections and any variation or incidents. Receipt of reports from the appointed arborist. Liaising with the appointed arborist to agree suitability of tree protection measures and any variations. Enforcement. Advice and assistance with the discharge of planning conditions relating to trees.
Local Authority	London Borough of Haringey	Insert Details	
Additional Contact	Insert Details	Insert Details	Insert Details
Additional Contact	Insert Details	Insert Details	Insert Details

Reference No	Age & Species	Height (m)	Crown (m)	Crown Spread (m)			Scaled Tree Diagram (m)	Notes	Recommendations (Replacement of any development in 10 years)			Vigour	Insect Value	Reaction Category
				W	N	E			Priority	Inspect Interval (yrs)	Phytological Condition			
T1	Mature Purple Beech <i>Fagus sylvatica</i> 'purpurea'	22	3	10	8	10		Form: History: Defects:	Multi-stemmed at 2m with a well-formed crown. Occasional pruning every 2 years due to crown lifting. Significant cavity forming at 2.5m above ground level to south.	Inspect cavity for decay	Moderate	High	20-40	
	Semi-Mature Yew <i>Taxus baccata</i>	3.5	2	30	15	15		Position: Form: History: Defects:	Situated on third party land. Single stemmed and vertical with a balanced crown. No evidence of significant pruning. No significant defects observed. Limited inspection, dimensions estimated.	No action required.	High	Low	40+	
T2	Mature Lime <i>Tilia sp.</i>	15	2	8	6	5.5		Form: History: Defects: Other:	Single stemmed and vertical with a balanced crown. No evidence of significant pruning. No significant defects observed. Epimoric shoots throughout stem & ivy prevented detailed inspection.	Remove ivy and inspect stem for defects	Moderate	Fair	20-40	
T3	Semi-Mature Ash <i>Fraxinus excelsior</i>	8	3.5	3	2	6.5		Form: History: Defects:	Single stemmed with a slight lean and an unbalanced crown. No evidence of significant pruning. No significant defects observed.	No action required.	High	Good	20-40	
T4	Mature Holly <i>Ilex aquifolium</i>	5	1	16	10	10		Form: History: Defects:	Single stemmed and vertical with a balanced crown. No evidence of significant pruning. No significant defects observed.	No action required.	High	Low	40+	
T5	Early-Mature Sycamore <i>Acer pseudoplatanus</i>	13	6	45	35	35		Form: History: Defects: Other:	Single stemmed with a slight lean and an unbalanced crown. No evidence of significant pruning. No significant defects observed. Ivy prevented detailed inspection. Limited inspection, dimensions estimated.	Remove ivy and inspect stem for defects	Moderate	Good	40+	
T6	Semi-Mature London Plane <i>Platanus x hispanica</i>	12	3	43	33	33		Form: History: Defects: Other:	Single stemmed with a slight lean and an unbalanced crown. No evidence of significant pruning. Cavity observed where secondary stem has torn out in the past.	Inspect cavity for decay	Moderate	Good	20-40	
T7	Mature Ash <i>Fraxinus excelsior</i>	20	2	20	20	20		Form: History: Defects: Other:	Four close growing specimens. No evidence of significant pruning. No significant defects observed.	No action required.	High	Good	40+	
T8	Semi-Mature Ash <i>Fraxinus excelsior</i>	12	6	75	65	65		Form: History: Defects: Other:	Single stemmed and leaning with an unbalanced crown. No evidence of significant pruning. No significant defects observed. Stem tears over boundary fence and wraps around 3 sides of the stem at 1m.	No action required.	High	Good	40+	
T9	Early-Mature Lawson Cypress <i>Chamaecyparis lawsoniana</i>	7	2	30	15	15		Position: Form: History: Defects: Other:	Single stemmed and vertical with a balanced crown. No evidence of significant pruning. No significant defects observed. Stem of 1m wraps around stem in 3 places.	No action required.	High	Good	40+	
T10	Semi-Mature False Acacia <i>Robinia pseudoacacia</i>	14	4	85	65	65		Position: Form: History: Defects: Other:	Situated on third party land. Twins stemmed at 3m with an unbalanced crown. Central stem removed at 1m as main fork. No significant defects observed. Limited inspection, dimensions estimated.	No action required.	Low	Poor	10-20	
T11	Early-Mature Yew <i>Taxus baccata</i>	7	1.5	40	20	20		Position: Form: History: Defects: Other:	Situated on third party land. Vertical hedgeform. Topped at 2m. No significant defects observed. Limited inspection, dimensions estimated.	No action required.	High	Good	40+	
T12	Mature Purple Beech <i>Fagus sylvatica</i> 'purpurea'	10	4	55	45	45		Position: Form: History: Defects: Other:	Situated on third party land. Single stemmed with a slight lean and an unbalanced crown. Central stem reduce to a height of 2m. No significant defects observed. Limited inspection, dimensions estimated.	No action required.	Moderate	Good	20-40	
T13	Semi-Mature Lime <i>Tilia sp.</i>	20	2	104	85	85		Form: History: Defects: Other:	Multi stemmed at 7m with a balanced crown. No evidence of significant pruning. No significant defects observed. Ivy prevented detailed inspection. Denia canopy.	Remove ivy and inspect stem for defects	Moderate	Fair	20-40	



The site plan illustrates the layout of a residential development with various trees and protection zones. Trees are labeled T1 through T17, with T1 and T2 highlighted in green. Construction exclusion zones are shown with hatched patterns, and restricted activity zones are indicated by orange hatching. The plan also shows 'Waverley Road' to the left, 'Flat roof' areas, and specific tree details like 'Elder Ht: 3m Dia: 20cm' and 'Cherry Laurel Ht: 3m Dia: 20cm'. Protection barriers and systems are also marked.

Inspection	Site Attendees	Comments
Pre-Start Desk-top To occur prior to any works taking place on the site.	N/A.	Project Manager and Site manager to study this Method Statement & contact the Project Arborist to agree all protection measures.
Pre-Start Meeting After tree works completed & tree protection barriers / ground protection measures installed. Prior to any other activity, inc. demolition & soil stripping.	Site manager, project arborist. Tree Officer invited.	Tree protection fencing locations & specification checked. Ground protection measures checked. Contractors to be inducted to all relevant aspects of the Arboricultural Method Statement. Responsibilities checked and acknowledged. Adherence to the Arboricultural Method Statement to be discussed and agreed. Report on findings to be sent to the local authority tree officer (see accompanying reporting template)
Monthly Inspection and Reporting To occur once per calendar month throughout the entirety of the project until the local authority agree that tree protection measures may be removed	Site manager and project arborist*	Tree protection fencing locations & specification checked. Ground protection measures checked. Past month, present and future month – activities and adherence to Arboricultural Method Statement discussed and checked. Report on findings to be sent to the local authority tree officer within 5 working days.
Overseeing Installation of foundations in Restricted Activity Zones. All excavation to be overseen.	Site manager and project arborist.	Two week's notice to be given prior to commencement. Excavation to be as specified in this Method Statement. Roots to be retained or pruned as specified in this Method Statement. Activities to be recorded and photographed. Mitigation measures to be employed specified by the project arborist.
Any other ground disturbance in Restricted Zones & Construction Exclusion Zones Including demolition, soil stripping, removal of hard surfaces, excavation for new surfacing, foundations, service trenches etc.	Site manager, project arborist.	Two week's notice to be given prior to commencement. Excavation to be as specified in this Method Statement. Excavations to be recorded and photographed. Mitigation measures to be employed specified by the project arborist.
Post-Construction Meeting Post external construction activity but prior to removal of fencing & landscaping operations.	Site manager, project arborist. Tree Officer invited.	Retained trees inspected. Ground conditions assessed and mitigation measures agreed where appropriate. Further landscaping operations and restrictions to be agreed.

* Where agreed with the L.A. it may be acceptable to supply photographs of the fencing to avoid the necessity for a site visit.
