

TH-IS – FERRY ISLAND BUILDING 1 [Scoping Drawings]



Legend & Quantities:

■	PODs (Towers)	
■	PODs (Link Building)	
■	PUCs (Towers)	
■	PUCs (Link Building)	
■	CIP Walls	381.7 m ²
---	PODs & PUCs temporary position	
■	Drylining	2707.9 m ²
■	Drylining – Smoke Shaft	65 m ²

Sequence for Towers:

1. CIPs to be installed with blue sky.
2. Bathroom Pods & PUCs to be placed into temporary position (1600 mm from core and CIPs).
3. Proppings and Planks setting out.
4. Structural topping and final pour.
5. Fire CIP head detail to be installed.
6. PODs and PUCs to be moved into final position.

Sequence for Link Building:

1. Slab pour consisting of traditional RC and PT
2. Bathroom Pods & PUCs to be placed into temporary position.
3. Drylining walls to be installed.

APPROVALS:

PROJECT TEAM:	
STRUCTURE:	
FAÇADE:	
MEP:	
DRYLINING:	
CIP:	

TH-IS – FERRY ISLAND BUILDING 1 [CIP Walls]



Legend & Quantities:

■	PODs (Towers)	
■	PODs (Link Building)	
■	PUCs (Towers)	
■	PUCs (Link Building)	
■	CIP Walls	381.7 m ²
---	PODs & PUCs temporary position	
■	Drylining	2707.9 m ²
■	Drylining – Smoke Shaft	65 m ²

Sequence for Towers:

1. CIPs to be installed with blue sky.
2. Bathroom Pods & PUCs to be placed into temporary position (1600 mm from core and CIPs).
3. Proppings and Planks setting out.
4. Structural topping and final pour.
5. Fire CIP head detail to be installed.
6. PODs and PUCs to be moved into final position.

Sequence for Link Building:

1. Slab pour consisting of traditional RC and PT
2. Bathroom Pods & PUCs to be placed into temporary position.
3. Drylining walls to be installed.




	PODs (Towers)	
	PODs (Link Building)	
	PUCs (Towers)	
	PUCs (Link Building)	
	CIP Walls	
		381.7 m ²
	PODs & PUCs temporary position	
	Drylining	
		2707.9 m ²
	Drylining – Smoke Shaft	
		65 m ²

1. CIPs to be installed with blue sky.
2. Bathroom Pods & PUCs to be placed into temporary position (1600 mm from core and CIPs).
3. Proppings and Planks setting out.
4. Structural topping and final pour.
5. Fire CIP head detail to be installed.
6. PODs and PUCs to be moved into final position.

1. Slab pour consisting of traditional RC and PT
2. Bathroom Pods & PUCs to be placed into temporary position.
3. Drylining walls to be installed.

TH-IS – FERRY ISLAND BUILDING 1 [Drylining]

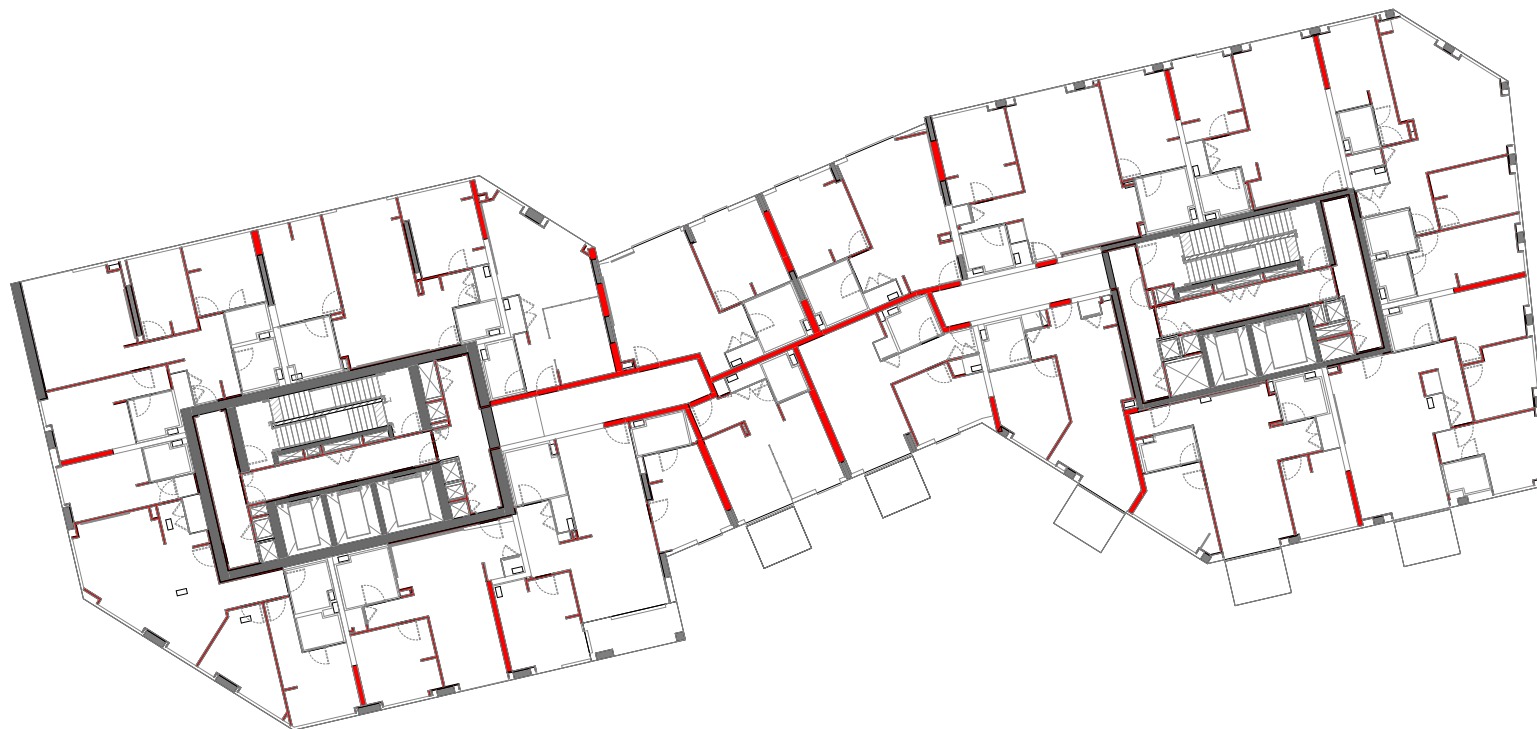

Legend & Quantities:

■	PODs (Towers)	
■	PODs (Link Building)	
■	PUCs (Towers)	
■	PUCs (Link Building)	
■	CIP Walls	381.7 m ²
---	PODs & PUCs temporary position	
■	Drylining	2707.9 m ²
■	Drylining – Smoke Shaft	65 m ²


Sequence for Towers:

1. CIPs to be installed with blue sky.
2. Bathroom Pods & PUCs to be placed into temporary position (1600 mm from core and CIPs).
3. Proppings and Planks setting out.
4. Structural topping and final pour.
5. Fire CIP head detail to be installed.
6. PODs and PUCs to be moved into final position.
7. Drylining walls to be installed.

Sequence for Link Building:

1. Slab pour consisting of traditional RC and PT
2. Bathroom Pods & PUCs to be placed into temporary position.
3. Drylining walls to be installed.

TH-IS – FERRY ISLAND BUILDING 1 [ISO view - Scoping Drawings]

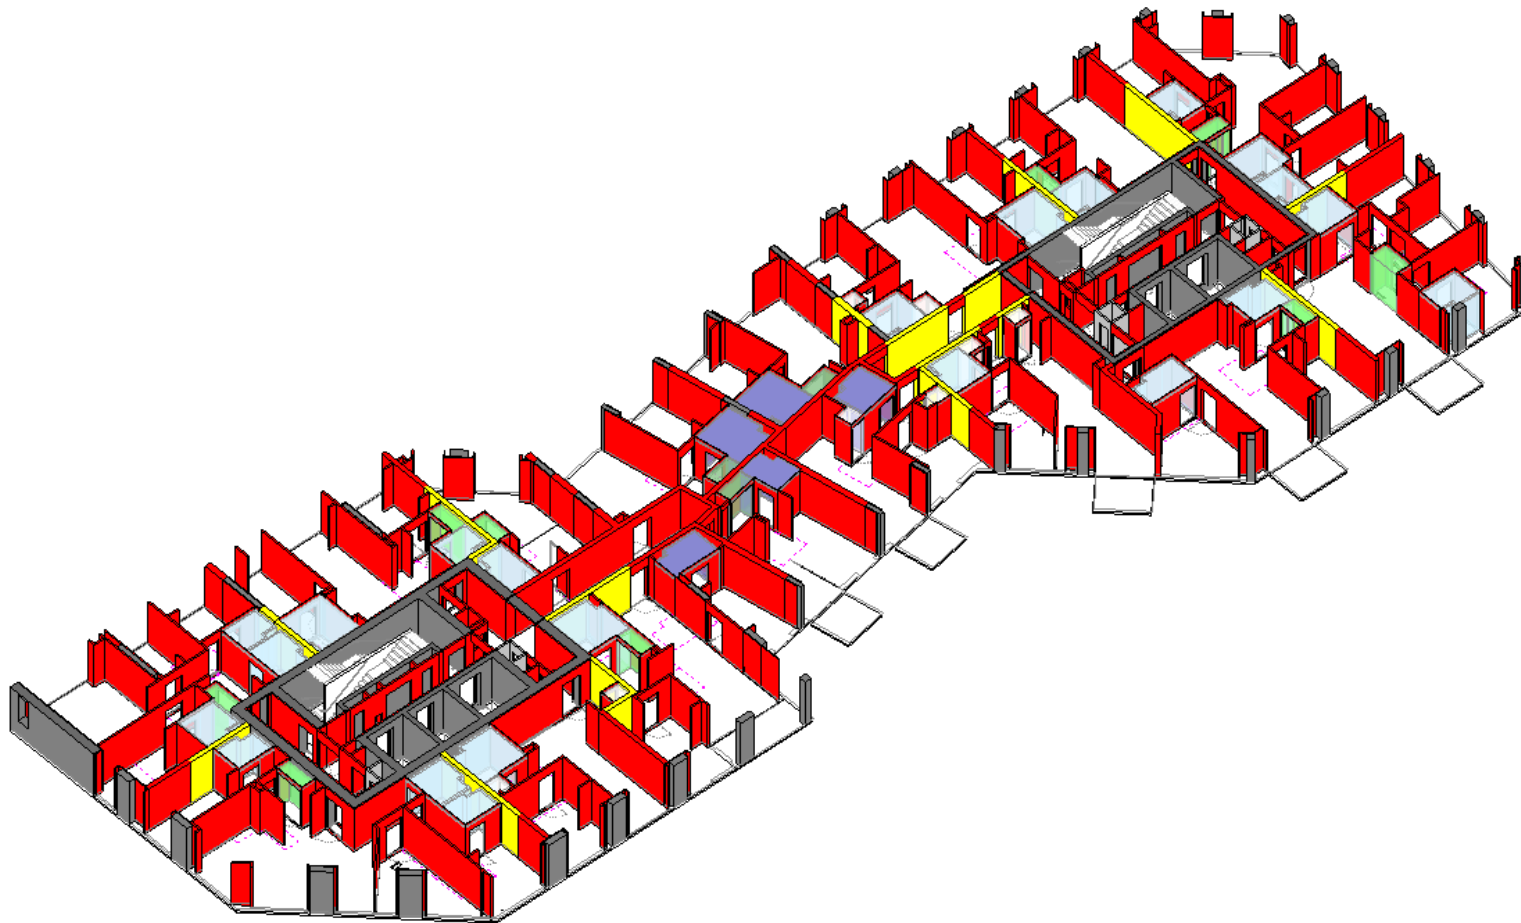

Legend & Quantities:

■	PODs (Towers)	
■	PODs (Link Building)	
■	PUCs (Towers)	
■	PUCs (Link Building)	
■	CIP Walls	381.7 m ²
---	PODs & PUCs temporary position	
■	Drylining	2707.9 m ²
■	Drylining – Smoke Shaft	65 m ²


Sequence for Towers:

1. CIPs to be installed with blue sky.
2. Bathroom Pods & PUCs to be placed into temporary position (1600 mm from core and CIPs).
3. Proppings and Planks setting out.
4. Structural topping and final pour.
5. Fire CIP head detail to be installed.
6. PODs and PUCs to be moved into final position.

Sequence for Link Building:

1. Slab pour consisting of traditional RC and PT
2. Bathroom Pods & PUCs to be placed into temporary position.
3. Drylining walls to be installed.

TH-IS – FERRY ISLAND BUILDING 1 [ISO view – CIP Walls]

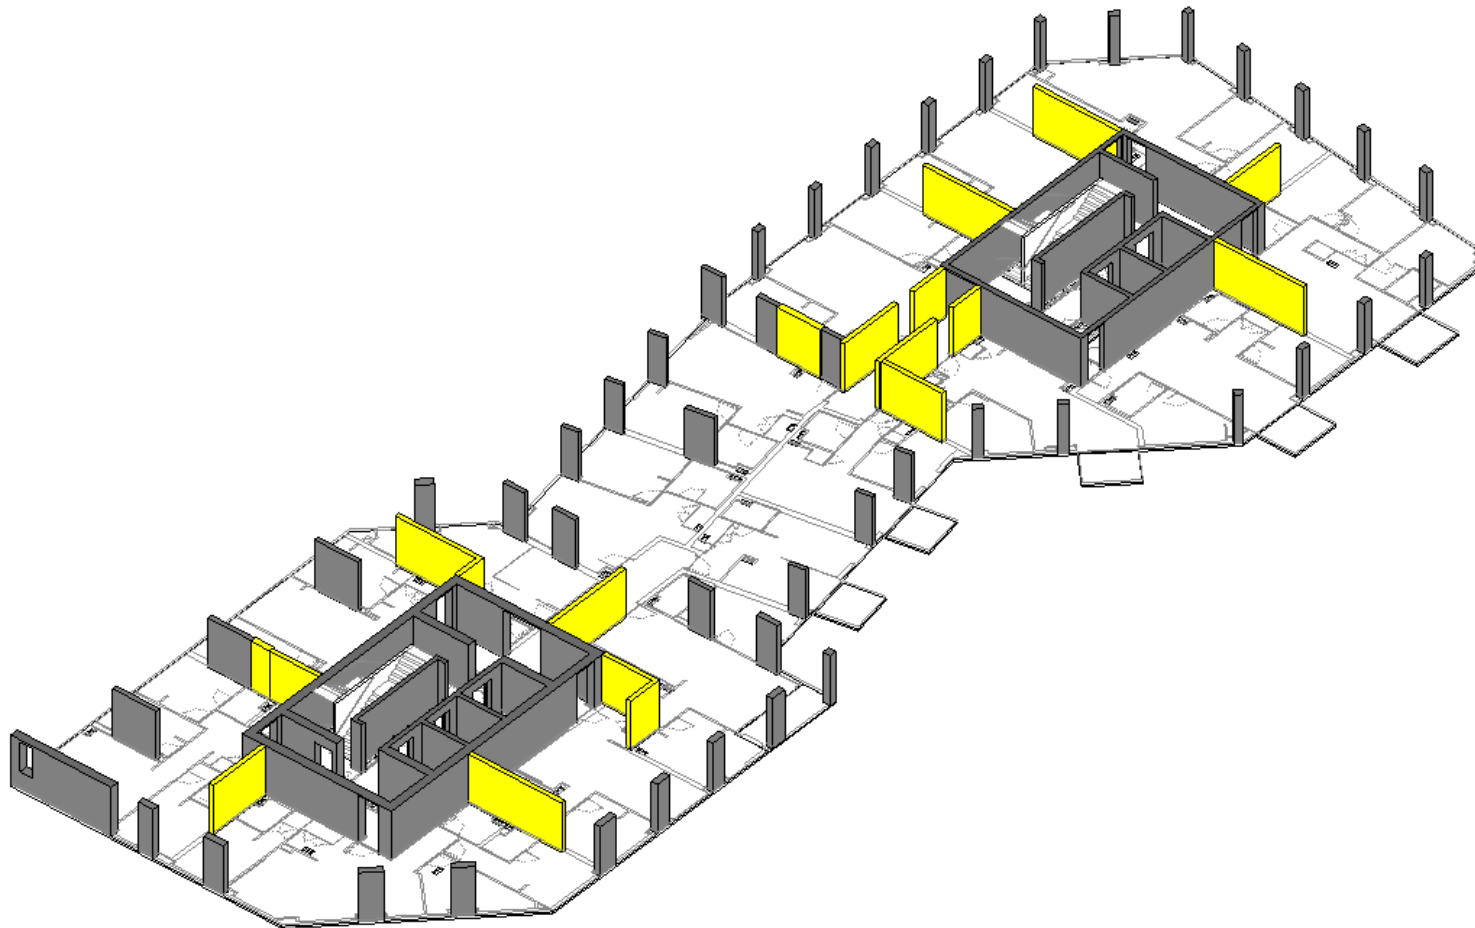

Legend & Quantities:

■	PODs (Towers)	
■	PODs (Link Building)	
■	PUCs (Towers)	
■	PUCs (Link Building)	
■	CIP Walls	381.7 m ²
---	PODs & PUCs temporary position	
■	Drylining	2707.9 m ²
■	Drylining – Smoke Shaft	65 m ²


Sequence for Towers:

1. CIPs to be installed with blue sky.
2. Bathroom Pods & PUCs to be placed into temporary position (1600 mm from core and CIPs).
3. Proppings and Planks setting out.
4. Structural topping and final pour.
5. Fire CIP head detail to be installed.
6. PODs and PUCs to be moved into final position.

Sequence for Link Building:

1. Slab pour consisting of traditional RC and PT
2. Bathroom Pods & PUCs to be placed into temporary position.
3. Drylining walls to be installed.

TH-IS – FERRY ISLAND BUILDING 1 [ISO view – Drylining]

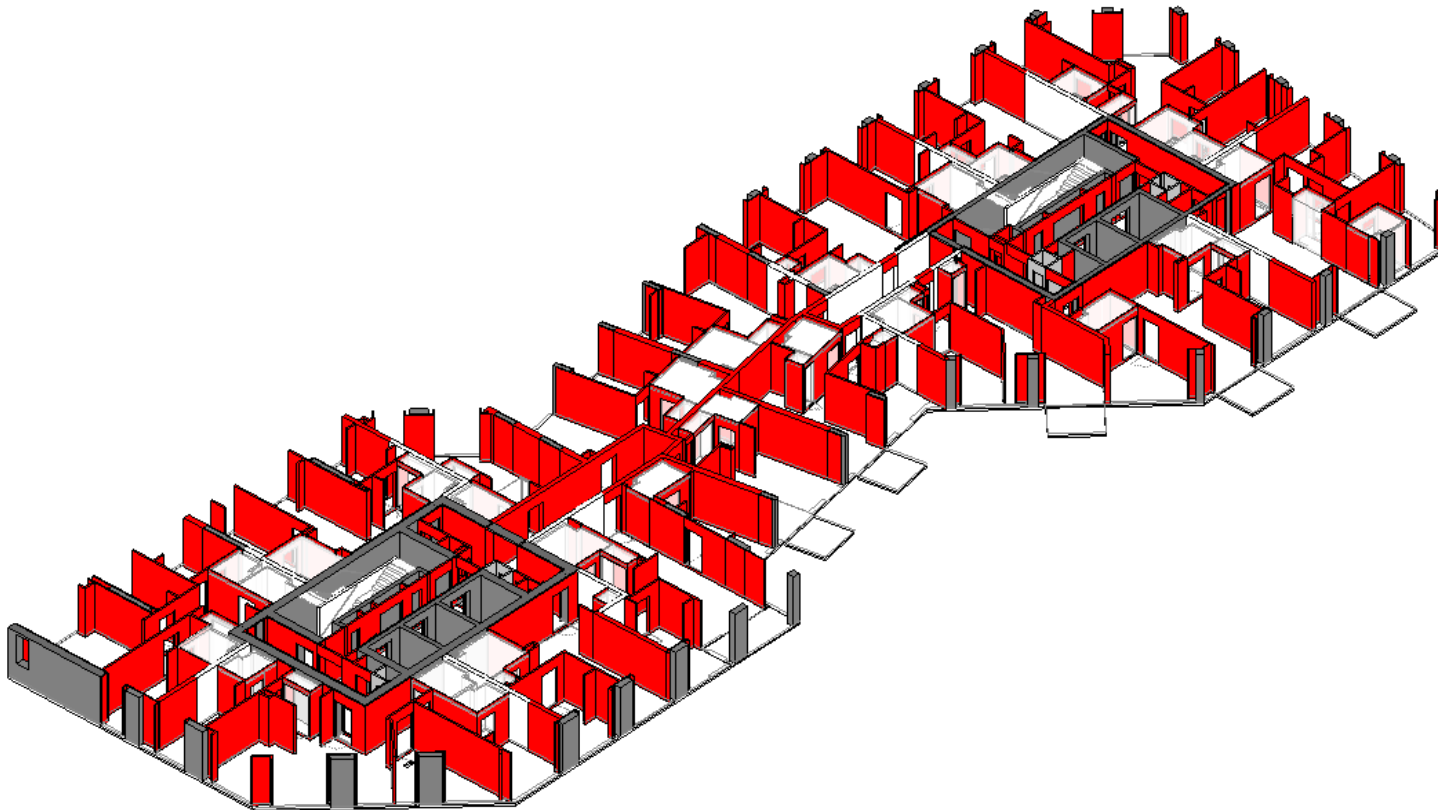

Legend & Quantities:

■	PODs (Towers)	
■	PODs (Link Building)	
■	PUCs (Towers)	
■	PUCs (Link Building)	
■	CIP Walls	
		381.7 m ²
---	PODs & PUCs temporary position	
■	Drylining	2707.9 m ²
■	Drylining – Smoke Shaft	65 m ²

Sequence for Towers:

1. CIPs to be installed with blue sky.
2. Bathroom Pods & PUCs to be placed into temporary position (1600 mm from core and CIPs).
3. Proppings and Planks setting out.
4. Structural topping and final pour.
5. Fire CIP head detail to be installed.
6. PODs and PUCs to be moved into final position.

Sequence for Link Building:

1. Slab pour consisting of traditional RC and PT
2. Bathroom Pods & PUCs to be placed into temporary position.
3. Drylining walls to be installed.
