


ROOF REPAIRS ELEVATION 1:1

Parking side.

Update on March 2025

Prepared For Metropolitan

16 Issues Identified

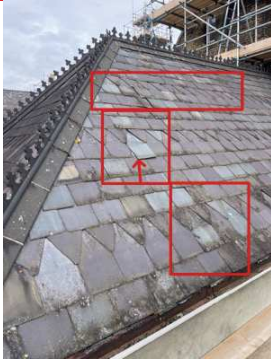

ISSUE 3

Assigned To RS7

6 x Slate to be re-arranged.

2 x slate to be changed

Total:

3 sqm of repairs.



ISSUE 4

Assigned To RS7

10 x slate to be re-arranged.

5 x slates to be changed

Total:

3 sqm of repairs.



ISSUE 7


Assigned To RS5

10 x slates to be replaced.

10 x slate to be re-arranged

Total:

3 sqm of repairs.

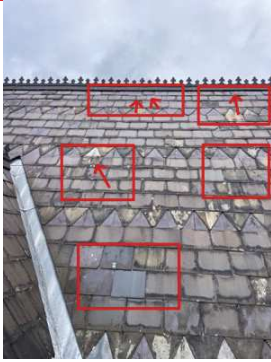

ISSUE 8

Assigned To RS5

10x slates to be replaced.

3 x ridge tiles re-arranged.

Total:

5 sqm of repairs.



ISSUE 9

Assigned To RS5

5 x slates to be replaced.

2 x ridge tile to be re-arranged.

Total:

4 sqm of repairs.



ISSUE 11

Assigned To RS5

5 x slates to be replaced.

Total:

2 sqm of repairs.



ISSUE 12

Assigned To RS5

5 x slates to be replaced.

Total:

2 sqm of repairs.



ISSUE 13

Assigned To RS5

5 x slates to be replaced.

Total:

3 sqm of repairs.



ISSUE 14

Assigned To RS5

5 x slates to be replaced.

2 x slates to be re-arranged.

Total:

1 sqm of repairs.



ISSUE 15

Assigned To RS5

5 x slate to be replaced.

1 x slate to be re-arranged.

Total:

3 sqm of repairs.




ISSUE 16

Assigned To RS1

5 x slate to be replaced.

Total:

2 sqm of repairs.

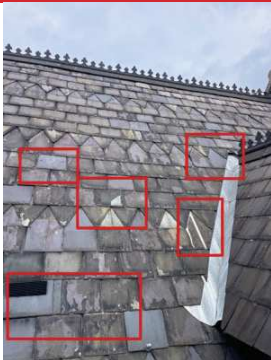

ISSUE 17

Assigned To RS1

5 x Slate to be replaced.

Total:

2 sqm of repairs.



ISSUE 18

Assigned To RS1

5 x slates to be replaced.

3m x renew lead flashing.

Clean Gutters and RWP.

Installed eaves.

Total:

4 sqm of repairs.



ISSUE 19

Assigned To RS1

3 x slate to be re-arranged.

2 x slates to be replaced

Total:

2 sqm of repairs.9



ISSUE 20

Assigned To RS1

5 x slates to be replaced.

5 x slate to be re-arranged.

Total:

2 sqm of repairs



ISSUE 21

Assigned To Rs1

1 x slate to be re-arranged.

5 x slate to be replaced.
