


SECOND FLOOR - OPERATIONS AND LOGISTICS PLAN
ENABLING WORKS



- NOTE
1. This drawing is copyright.
 2. All dimensions must be checked on site before proceeding.
 3. Dimensions of new work are to be adjusted to suit the existing building where necessary. Do not assume that the existing structure or details are plumb, square or level.
 4. The contractor must report any discrepancies to the architect before proceeding.
 5. All products are to be used strictly in accordance with the manufacturer's instructions.

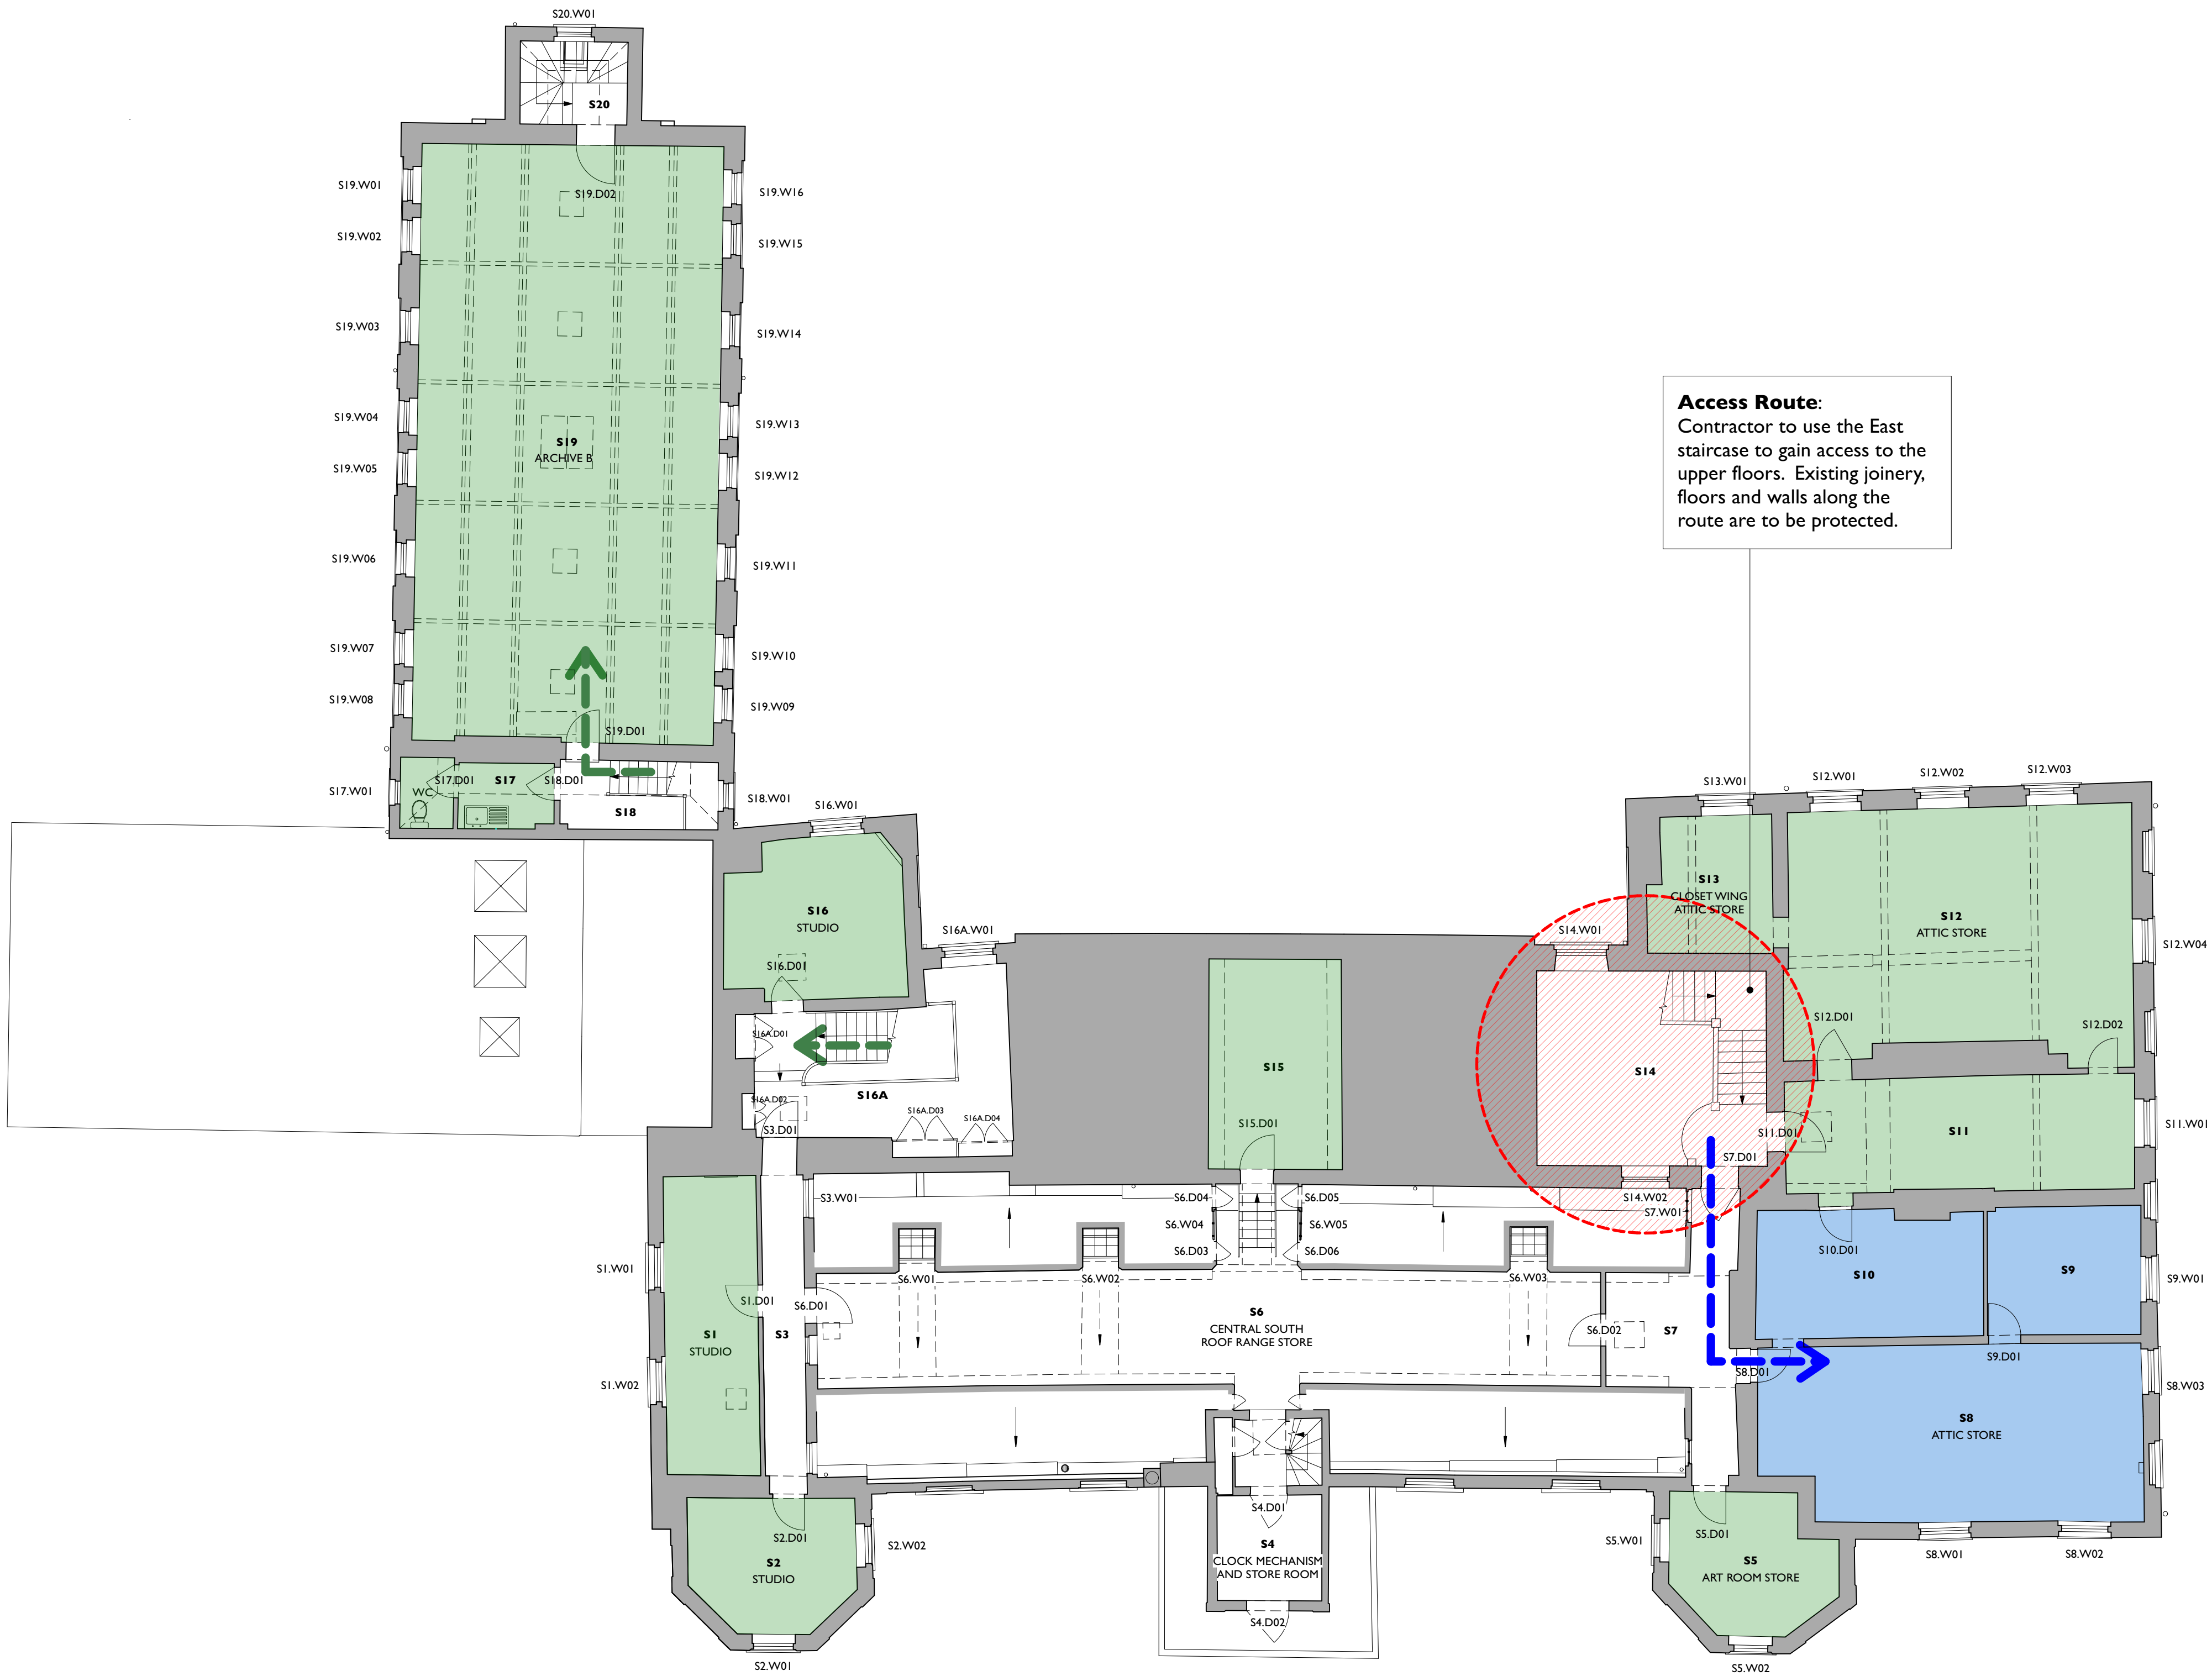

- KEY**
- MEND Funded Works - Enabling Works
 - Staff / Back of House Spaces
 - Public Spaces - Access to be maintained for the duration of the works
 - Contractor Access Routes
 - Staff Access Routes
 - Public Access Routes
 - Areas of Cross Over

Enabling and Opening Up Works

Refer to drawing 7440/132 for proposed enabling and opening up works in S8 - S10. The existing vinyl flooring and plywood sheathing beneath is to be lifted in full to these areas and removed from site.

Floorboards are to be labelled, lifted and stored elsewhere at Second Floor level to enable a full survey of the existing floor structure to be undertaken.

No asbestos removal works are proposed at this level.

- REVISIONS
- A Aug 2023 Additional notes added following initial Client comment
 - B Oct 2023 Access option updated

Rodney Melville + Partners
CHARTERED ARCHITECTS
HISTORIC BUILDING CONSULTANTS

10 EUSTON PLACE
LEAMINGTON SPA
WARWICKSHIRE
CV32 4LJ
T 01926 881311
F 01926 451766

E architects@rmpuk.com
www.rmpuk.com
Rodney Melville and Partners Limited

Client
London Borough of Haringey Council

Project
Bruce Castle

Title
Second Floor
Operations and Logistics Plan - Enabling Works

Scale	1:100 @ A1	Job No	7440
Date	Aug 2023	Dwg No	137
Drawn	HB	Rev	B
