



GEOSHIELD Verification PLAN



PROJECT DESCRIPTION

Pre Verification Plan for the Ground Gas Membrane at the Clarendon Road redevelopment Phase 3, former Hornsey Gasworks located at:

Clarendon Road
Hornsey
N8 0JU

Atkins Limited have produced Remediation Strategy based on the findings of the Geotechnical Survey Report. The strategy confirms the site is CS2 with continued monitoring form VOCs.

Phase 3 of the development consists of 4 residential blocks - Blocks D1, D2, D3 and D4. Under BS8485:2015+2019 the building type is classed as Type A. Therefore 3.5 points are required from the ground gas protection system.

This Pre Verification Plan reviews the proposed design and material specification and confirms it is compliant with the requirements of BS8485:2015+2019.

To ensure the relevant Planning Condition is discharged the installation of the ground gas protection system will be tested and documented in accordance with CIRIA 735. On successful completion of the works the subsequent reports are to be issued to The Local Planning Authority for approval.



GEOSHIELD Verification PLAN



CONTENTS

Section 1:	Project details	Page 1
Section 2:	Project material specification	Page 1
Section 3:	Project information	Page 2
Section 4:	GeoShield surveyor information	Page 3
Section 5:	Project information: Drawings, S.I, MSDS, Maps	Page 4/
Section 6:	Client Details	Page 15
Section 7:	Application team leaders	Page 16
Section 8:	Health and safety	Page 17
Section 9:	Applicator competence	Page 18
Section 10:	Gas regime	Page 19
Section 11:	Testing	Page 20
Section 12:	Risk assessment	Page 21
Section 13:	GeoShield competence	Page 23
Section 14:	Method Statement	Page 24
Section 15:	Project technical assessments	Page 25
Section 16:	Contractor Quality Assurance (CQA)	Page 27
Section 17:	Pre-Contract Meeting Checklist	Page 28
Section 18:	On-Site risk assessment	Page 29
Section 19:	Pre-Contract Meeting Summary	Page 30



GEOSHIELD
Verification
PLAN



Section 1:

GEO100/GCL/ClarendonRoadPHASE3

PROJECT:

GCL - Clarendon Road - Phase 3

PROJECT ADDRESS:

Clarendon Road - Phase 3

East of Mary Neuner Road, Hornsey, N22 6UG

SPECIFICATION:

Verified in accordance CIRIA 735.

Design in accordance with BS8485 2015 + 2019 for Methane and Carbon Dioxide.

Substrate prepared in-accordance with manufactures instructions and BS8485

Pudlo GP Ultra+ Gas Barrier

Pudlo GP Ultra Tape

Pudlo GP Ultra EXT Tape

Pudlo GP Ultra Seal

Pudlo Liquid Gas Barrier



GEOSHIELD Verification PLAN



SPECIFICATION:

INFORMATION INCLUDED:

Material specification technical data sheets

5192204/P3_RemStrat Rev0.4

W257-PUD-D1-00-DR-S-02-1000

W257-PUD-D2-00-DR-S-02-1001

W257-PUD-D3-FN-DR-S-02-1002

W257-PUD-D3-XX-DR-S-02-1005

W257-PUD-D3-XX-DR-S-05-1000

W257-PUD-D4-00-DR-S-01-1006

W257-PUD-D4-BL-DR-S-02-1003

W257-PUD-DD-XX-DR-S-03-0001 to W257-PUD-DD-XX-DR-S-03-0024

W257-PUD-DD-XX-SK-S-03-0001 to W257-PUD-DD-XX-SK-S-03-0003

Information presented to at the pre-verification stage assumed correct

Any change client will let GeoShield know or this Pre-verification Plan will be void.



GEOSHIELD
Verification
PLAN



SURVEYOR:

Chris Ingham

VERIFICATION COMPANY:

GeoShield Limited

Icon Business Centre

4100 Park Approach

Thorpe Park

Leeds

CONTACT NUMBER:

07555 214 679

EMAIL ADDRESS:

CIngham@geoshield.co.uk

ORDER NUMBER:

To be confirmed

PER VISIT:

YES:



NO:



PROJECT:

YES:



NO:





GEOSHIELD Verification PLAN



SPECIFICATION



Phase 3, Clarendon Road, Hornsey

Remediation Strategy

St William Homes LLP

May 2020



GEOSHIELD

Verification

PLAN



SPECIFICATION



Notice

This document and its contents have been prepared and are intended solely as information for St William Homes LLP and use in relation to Phase 3 of the former Hornsey Gasworks at Mary Neuner Road, Hornsey, N22 6UG.

SNC Lavalin assumes no responsibility to any other party in respect of or arising out of or in connection with this document and/or its contents.

Document history

Revision	Purpose description	Originated	Checked	Reviewed	Authorised	Date
Rev 1.0	Draft for Comment	VG	AN	AN	NK	14/02/2020
Rev 2.0	Final	VG	AN	AN	NK	20/02/2020
Rev 3.0	Final – following regulator comments	VG	AN	AN	NK	22/04/2020
Rev 4.0	Final – following regulator comments	AN	AN	AN	NK	13/05/2020

Client signoff

Client	St William Homes LLP
Project	Phase 3, Clarendon Road, Hornsey
Job number	5192204



GEOSHIELD Verification PLAN



SPECIFICATION

6.7. Gas and Vapour Mitigation

6.7.1. Ground Gas

Based on the ground gas risk assessment the site has been characterised as CS2 and therefore gas risk protection measures are required as part of the development. The following gas protection measures are recommended:

- Blocks D1 – D3 (without basement): a combination of the proposed suspended slab and gas resistant membrane or a dispersal layer is proposed for the Blocks D1-D3 in the northern area. Due to the greater relative difficulty in implementing a dispersal layer, it would usually be recommended that a gas resistant membrane is installed;
- Assuming the membrane solution is selected, any gas resistant membrane proposed for Blocks D1 – D3 shall meet all of the following criteria:
 - sufficiently impervious to the gases with a methane gas transmission rate <40.0 ml/day/m²/atm (average) for sheet and joints (tested in accordance with BS ISO 15105-1 manometric method);
 - sufficiently durable to remain serviceable for the anticipated life of the building and duration of gas emissions;
 - sufficiently strong to withstand in-service stresses (e.g. settlement if placed below a floor slab);
 - sufficiently strong to withstand the installation process and following trades until covered (e.g. penetration from steel fibres in fibre reinforced concrete, penetration of reinforcement ties, tearing due to working above it, dropping tools, etc);
 - capable, after installation, of providing a complete barrier to the entry of the relevant gas; and
 - verified in accordance with CIRIA C735.
- Blocks D4 and E1-E3 (with basement): no additional gas protection measures are required as the underground basement is assumed to be vented in addition to the gas resistance provided by the basement floor and wall construction itself. It is recommended that the service penetrations should be limited in number and sealed using 'top hats', to avoid introducing pathways for gas ingress into the basement.

6.7.2. Vapours from Soil and Perched Water

Assessment of potential risk from the migration of vapours into structures from soil identified the following recommendations/actions:

- Installation and verification of an appropriate soil vapour resistant barrier membrane protective of the contaminants identified to pose an unacceptable risk in key areas in accordance with industry good practice guidance [1] [3] [4] [16]; and

5192204/P3_RemStrat | 4.0 | May 2020
SNC-Lavalin | 5192204_p3_remstrat_rev4

Page 27 of 75



- Excavation and disposal of visual and olfactory contamination in Made Ground (where identified).

CIRIA C748 [17] provides guidance on the selection of appropriate vapour protection barriers, which should be undertaken in consultation with a specialist provider and the building designer. The selection should consider the following key properties to ensure fitness for use and prevent damage during construction activities:

- Membrane thickness;



GEOSHIELD Verification PLAN



SPECIFICATION

CIRIA C748 [17] provides guidance on the selection of appropriate vapour protection barriers, which should be undertaken in consultation with a specialist provider and the building designer. The selection should consider the following key properties to ensure fitness for use and prevent damage during construction activities:

- Membrane thickness;
- permeation rate for the contaminants of concern at various concentrations;
- tensile strength;
- puncture resistance;
- impact resistance; and
- tear resistance.

The detailed design of these protective measures including product selection and installation details is outside the scope of this report but should be addressed in conjunction with the building designer. In addition to the items detailed above, the membrane should comply with the following:

- sufficiently durable to remain serviceable for the anticipated life of the building and duration of any emissions;
- sufficiently strong to withstand in-service stresses (e.g. settlement if placed below a floor slab);
- sufficiently strong to withstand the installation process and following trades until covered (e.g. penetration from steel fibres in fibre reinforced concrete, penetration of reinforcement ties, tearing due to working above it, dropping tools, etc);
- capable, after installation, of providing a complete barrier to the entry of the relevant contaminants; and
- verified in accordance with CIRIA C735 [18].

A gas and vapour membrane specification is provided in Appendix D.

6.7.3. Verification of Gas and Vapour Membranes

Verification of the vapour and gas protection measures should be in accordance CIRIA C716 [19] and C735 [18] respectively, which provide advice on verification approaches relevant to different scenarios and protection measures.

The verification should include as a minimum;

- a verification report including a description of any measures installed – textual, photographic records, as-built construction drawings;
- details of who installed the measures and relevant warranties;
- details of who inspected or verified the installation/s and a description of how this took place, together with any constraints (i.e. areas that could not be inspected or tested) or other issues of uncertainty;
- verification test results, outcomes of inspections and compliance data should be provided, either within the main text or as an annex to the report; and
- details of any defects identified, together with corrective actions and subsequent verification checks.

Verification of gas protection measures will require approval via the LB Haringey as well as any other building control bodies involved in the scheme (i.e. NHBC).

6.8. Perched Water and Surface Water Management

Shallow groundwater / perched water encountered within excavations will be removed, tested and discharged to foul sewer wherever possible, under an appropriate discharge consent. Should free phase hydrocarbon product be encountered at any point during intrusive works on site, this will be removed via pumping/excavation in line with the earthworks and remediation contractor's



GEOSHIELD Verification PLAN



SPECIFICATION



PRODUCT DATA SHEET

PUDLO GB Ultra+

DESCRIPTION

PUDLO GB Ultra+ is a dual performance membrane that provides protection from gas including VOC's, Carbon Dioxide, Methane, Radon, Hydrocarbons and protects the structure from water ingress. **PUDLO GB Ultra+** is a multi-layer, polythene membrane which is fleece-backed (black fluffy side up) providing a fully bonded system to the concrete.

USES

For all aspects of gas protection and where a Grade 3 (waterproofing) environment is required as part of a dual system recommended in BS8102:2009. **PUDLO GB Ultra+** can be used in horizontal or vertical application. **PUDLO GB Ultra+** is suitable for all ground floor and basement construction including lift pits, slabs, liner walls, capping beams and service penetrations. **PUDLO GB Ultra+** can also be used as single system.

BENEFITS

- Recognised as an accepted system for gas and water protection by NHBC.
- Full surface contact between the membrane and concrete.
- Quick and easy installation.
- Can be installed in all weather conditions.
- No requirement for priming. Overlaps are sealed by hot welding or joint tape (dependant on gas present).



PUDLO GB Ultra+ is pre-applied with the fleece backed material side facing outwards towards the concrete. **PUDLO GB Ultra+** is classified as Type A (Barrier) system in accordance with BS 8102:2009. **PUDLO GB Ultra+** hydrocarbon barrier offers a safe solution for the protection of buildings and its occupiers against all levels of hydrocarbons, methane, carbon dioxide and radon. **PUDLO GB Ultra+** is manufactured and designed to withstand most aggressive environments.

TECHNICAL DATA

Testing has been completed and carried out in accordance with the new test criteria under BS 8485:2015 and CIRIA C748 to determine the permeation rates for a range of VOC's, methane and Carbon Dioxide. Immersion testing has been completed for chemical resistance to EN 1441 and EN 14415.

Physical Properties

Characteristics	Test Method	Unit	PUDLO GB Ultra+
Thickness	EN 1849-2	mm	1.0
Width	EN 1849-2	M	1.9
Length	EN 1849-2	M	25
Weight	EN 1849-2	g/m ²	700



GEOSHIELD

Verification

PLAN



SPECIFICATION



Part of the DB Group

PRODUCT DATA SHEET

Hydraulic Properties

Characteristics	Test Method	Unit	PUDLO GB Ultra+
Water Vapour Rate	EN 1931	g/m ² /day	0.14
Water Tightness (60kPa)	EN 1928	-	PASS
Water Tightness (196kPa – 20m water head)	EN 1928	-	PASS

Mechanical Properties

Characteristics	Test Method	Unit	PUDLO GB Ultra+
Resistance to Static Load	EN 12730	Kg	>20
Tensile Strength (MD)	EN 12311-1	N/50mm	>550
Tensile Strength (CMD)	EN 12311-1	N/50mm	>400
Tear Resistance (MD)	EN 12310-1	N	>300
Tear Resistance (CMD)	EN 12310-1	N	>300
Resistance to Impact	EN 12691-B	N	650
Reaction to Fire	EN ISO 11925-2	Class	E
Concrete Peel Adhesion	ASTM D903 (mod)	Kn/M	>3.0
Resistance to Artificial Ageing	EN 1296	-	PASS
Resistance to Chemicals	EN 1847	-	PASS

Vapour Permeability – 100% Concentration

Characteristics	Test Method	Unit	PUDLO GB Ultra+
Transmission Rate of Benzene	EN ISO 15105-2	mg/m ² /day	2250
Transmission Rate of Toluene	EN ISO 15105-2	mg/m ² /day	2370
Transmission Rate of Ethyl Benzene	EN ISO 15105-2	mg/m ² /day	400
Transmission Rate of Xylene (m.p.o)	EN ISO 15105-2	mg/m ² /day	690
Transmission Rate of Hexane	EN ISO 15105-2	mg/m ² /day	95.25
Transmission Rate of Vinyl Chloride	EN ISO 15105-2	mg/m ² /day	36.44
Transmission Rate of Trichloroethene (TCE)	EN ISO 15105-2	mg/m ² /day	1.44
Transmission Rate of Tetrachloroethene (PCE)	EN ISO 15105-2	mg/m ² /day	1.59

Gas Permeability

Characteristics	Test Method	Unit	PUDLO GB ULTRA+
Methane Permeability	EN ISO 15105-1	ml/m ² /day/atm	0.13
Methane Permeability (Welded Joint)	EN ISO 15105-1	ml/m ² /day/atm	1.00
Carbon Dioxide Permeability	EN ISO 15105-1	ml/m ² /day/atm	3.01
Transmission rate of Vinyl Chloride Gas	EN ISO 15105-1	ml/m ² /day/atm	0.04
Radon Permeability	SP Method 3873	m ² /s	3.0 x 10 ⁻¹²

Certification 7 Compliance

Organisation	Requirements
CE Mark	EN13967
NHBC	Chapter 5.4 & Traffic Light System
BS 8485:2015	Methane, Carbon Dioxide
CIRIA C748	VOC Barrier
BS 8102:2009	Type A (Barrier)

PUDLO GB Ultra+ complies with the latest codes of practice as set out by BRE, CIRIA C748, BS 8485:2015 and BS 8102. PUDLO GB Ultra+ is also suitable for use as a ground gas / Hydrocarbon protection from NHBC under the traffic light system (Green, Amber 1, Amber 2 and Red sites).



GEOSHIELD Verification PLAN



SPECIFICATION



Part of the DB Group

PRODUCT DATA SHEET

MEMBRANE OVERLAPS

Membrane overlaps are sealed using 2 different methods. The method of sealing overlaps is determined what gases are present and at what level following the review from the 3rd party gas verification plan. These methods are as follows:

VOC (Volatile Organic Compound) = Hot Welded Joints only.

Carbon Dioxide and Methane = Hot Welded Joints or Tape (Dependent on gas verification report).

Radon = Tape only.

Note: PUDLO do not offer a warranty on gas protection only for waterproofing. Gas membrane installation when hot welding must be carried out by a 3rd party approved installer.

PACKAGING

1.9m x 25m roll. (47.5m²). Roll Weight = 35kg

ANCILLARY PRODUCTS

- PUDLO GB Ultra Tape (100mm selfedge overlap tape)
- PUDLO GB Ultra EXT Tape (300mm roll end tape)
- Surestop BWB
- Surestop SWB
- Surestop Adhesive
- Surestop SM
- Surestop Voidformer

HEALTH & SAFETY

PUDLO GB Ultra+ rolls are heavy and may need mechanical lifting. Please refer to PUDLO GB Ultra+ MSDS for more information.

FIRE

PUDLO GB Ultra+ is a product that is non-toxic nor flammable.

STORAGE & SHELF LIFE

PUDLO GB Ultra+ has a shelf life of 12 months when kept in dry conditions at a temperature of 5°C to 45°C. Storage at higher temperatures and high humidity may reduce the shelf life of the product.

For further information on accessories that are used with PUDLO GB Ultra+ please contact PUDLO Head Office on 01954 780687 or email sales@pudlo.com.





GEOSHIELD Verification PLAN



SPECIFICATION



Part of the DB Group

Product data sheet

PUDLO Liquid GB

Description

PUDLO Liquid GB is a styrene, butadiene, latex-based liquid system.

PUDLO Liquid GB prevents gas penetration for Methane, Radon, Carbon Dioxide, air and moisture into buildings.

Uses

- PUDLO Liquid GB is used for the sealing of pile heads, prior to concrete slabs being cast across the top
- PUDLO Liquid GB is a barrier to moisture and can be used as a DPM on both floors and walls

Benefits

- Easy to apply
- Provides an effective gas and moisture vapour barrier
- Packaged in 15kg tubs
- Roll, brush or spray applied

Application

Refer to PUDLO GP Ultra+ installation manual.

Coverage /yield

A minimum dry-coated thickness of 1mm is needed to provide an adequate gas barrier.

To achieve 1.0mm thickness, a total of 2kg/m² is required. One 15kg tub will cover an area of 7.5m².



Packaging

15kg tubs - 33 tubs per pallet.

PUDLO supplies a 120mm x 5m reinforcing strip with every 3 tubs, for detailing around upstands and changes in level or angles.

Ancillary products

- PUDLO GP Ultra Range (all membranes)
- PUDLO Detailing Strip
- Surestop BWB / Surestop SWB (sealing construction joints)
- Surestop SM
- Surestop Adhesive
- Surestop Voidformer

Gas & Waterproofing - Below Ground - PUDLO Liquid GB

T: 01954 780687 W: pudlo.com E: sales@pudlo.com





GEOSHIELD

Verification

PLAN



SPECIFICATION



Product data sheet

Health & safety

Appropriate care must be taken when manual handling the product. After use, please ensure all tools are clean.

Fire

Refer to PUDLO Liquid GB MSDS for more information.

Storage & shelf life

Store tubs in dry conditions between 50C and 300C. Product has a 12-month shelf life.

For further information on accessories that are used with PUDLO Liquid GB please contact PUDLO Head Office on 01954 780687 or email technical@dbgholdings.com.

Technical data

PUDLO Liquid GB complies with the latest codes of practice, as set out by BR211, CIRIA and BS 8485:201. PUDLO Liquid GB is also suitable for use as a gas protection measure for NHBC, under the traffic light system (Green, Amber 1, Amber 2 and Red sites).

Physical properties

Characteristics	Test method	Unit	PUDLO GP Ultra+
Applied thickness	-	mm	>1.0
Form supplied	-	-	Viscous liquid
Pack size	-	-	15kg
Colour	-	-	Pink / purple
Chemical composition	-	mm	Advances SBS with specialty additives

Physical properties

Characteristics	Test method	Unit	PUDLO GP Ultra+
Water tightness	EN 1296, EN 1367, EN 1928	-	PASS
Methane permeability	BS EN ISO 15105-1	ml/m ² /day/atm	0.01
Radon permeability	Saarland University GER	mm	>1.0mm applied thickness provides a complete barrier to Radon

Gas & Waterproofing - Below Ground - PUDLO Liquid GB



GEOSHIELD Verification PLAN



SPECIFICATION



Part of the DB Group

Product data sheet

PUDLO GP Ultra Seal

Description

PUDLO GP Ultra Seal is a multi-layer, polyethylene membrane with an adhesive coating for vertical application.

Uses

- PUDLO GP Ultra Seal protects structures from gas, including VOC's, Carbon Dioxide, Methane, Radon, Hydrocarbons and moisture
- PUDLO GP Ultra Seal can be used as a post applied waterproofing and damp-proof membrane

Benefits

- BBA approved
- Easy to install
- Can be used in all weather conditions due to its all-weather adhesive backing

Application

Refer to PUDLO GP Ultra Seal installation manual.

Packaging

1.0 x 50m. Product is available in black and silver colour

Installation

Please refer to PUDLO GP Ultra Seal installation manual.

Fire

Refer to PUDLO GP Ultra Seal MSDS for further information.



Ancillary products

- PUDLO Ultra Detailing Strip
- PUDLO Self Seal Primer (2 coats)
- Surestop BWB
- Surestop SWB
- Surestop Adhesive
- Surestop SM
- Surestop Voidformer

Health & safety

PUDLO GP Ultra Seal rolls are heavy - in excess of 20kg.

Please refer to PUDLO GP Ultra Seal MSDS for more information.

Storage & shelf life

Rolls of PUDLO GP Ultra Seal should be stored horizontally and pallets should not be stacked on top of one another.

PUDLO GP Ultra Seal should be stored in a cool, dry place, protected from exposure to rain, sun, heat and cold temperatures prior to installation.

Gas & Waterproofing - Below Ground - PUDLO GP Ultra Seal



GEOSHIELD

Verification

PLAN



SPECIFICATION



Product data sheet

Exposure to sunlight for extended periods of time could cause difficulty with removal of the polyethylene release film.

For further information on accessories that are

used with PUDLO GP Ultra Seal, please contact PUDLO Head Office on 01954 780687 or email technical@dbgholdings.com

Technical Data

Physical properties

Characteristics	Test method	Unit	PUDLO GP Ultra Seal
Thickness	EN 1849-2	mm	1.2
Width	EN 1849-2	m	1 or 0.3
Length	EN 1849-2	m	20
Weight	EN 1849-2	g/m ²	1,000

Hydraulic properties

Characteristics	Test method	Unit	PUDLO GP Ultra Seal
Water vapour rate	EN 1931	g/m ² /day	0.14
Water tightness (50kPa)	EN 1928	-	PASS
Water tightness (196kPa - 20m water head)*	EN 1928	-	PASS

* basement application

Mechanical properties

Characteristics	Test method	Unit	PUDLO GP Ultra Seal
Resistance to static load	EN 12730	kg	>20
Tensile strength (MD)	EN 12311-1	N/50mm	>550
Tensile strength (CMD)	EN 12311-1	N/50mm	>400
Tear resistance (MD)	EN 12310-1	N	>300
Tear resistance (CMD)	EN 12310-1	N	>300
Resistance to impact	EN 12691-8	N	650
Reaction to fire	EN ISO 11925-2	Class	E

Gas & Waterproofing - Below Ground - PUDLO GP Ultra Seal



GEOSHIELD Verification PLAN



SPECIFICATION



Part of the DBGroup

Product data sheet

Resistance to artificial ageing	EN 1296	-	PASS
Resistance to chemicals	EN 1847	-	PASS

Vapour permeability - 100% concentration

Characteristics	Test method	Unit	PUDLO GP Ultra Seal
Transmission rate of benzene	EN ISO 15105-2	mg/m ² /day	2250
Transmission rate of toluene	EN ISO 15105-2	mg/m ² /day	2370
Transmission rate of ethyl benzene	EN ISO 15105-2	mg/m ² /day	400
Transmission rate of xylene (mpo)	EN ISO 15105-2	mg/m ² /day	690
Transmission rate of hexane	EN ISO 15105-2	mg/m ² /day	98,25
Transmission rate of vinyl chloride	EN ISO 15105-2	mg/m ² /day	36,44
Transmission rate of trichloroethene (TCE)	EN ISO 15105-2	mg/m ² /day	1,44
Transmission rate of tetrachloroethene (PCE)	EN ISO 15105-2	mg/m ² /day	1,59

Gas permeability

Characteristics	Test method	Unit	PUDLO GP Ultra Seal
Methane permeability	EN ISO 15105-1	ml/m ² /day/atm	0.13
Methane permeability (welded joint)	EN ISO 15105-1	ml/m ² /day/atm	1.00
Carbon dioxide permeability	EN ISO 15105-1	ml/m ² /day/atm	3.01
Transmission rate of vinyl chloride gas	EN ISO 15105-1	ml/m ² /day/atm	0.04
Radon permeability	SP Method 3873	m ² /s	3.0 x 10 ⁻¹²

Durability & chemical resistance

Chemical Resistance - SULPHURIC ACID (10% solution of Sulphuric Acid (H ₂ SO ₄)) 50° for 56 days.	EN 14414 – A	Tensile Strength	100%
		Result	PASS
Chemical Resistance - BASIC (Calcium Hydroxide saturated suspension) 50° for 56 days.	EN 14414 – B	Tensile Strength	100%
		Result	PASS



GEOSHIELD Verification PLAN



SPECIFICATION



Part of the DB Group

Product data sheet

Chemical Resistance - SOLVENTS (35% Diesel, 35% Paraffin, 30% Oil HD30 (vol) 50° for 56 days.	EN 14414 – C	Tensile Strength	100%
		Result	PASS
Chemical Resistance - SYNTHETIC LEACHATE (Mixture of 14 acids, chlorides, sulphates and phosphate) 50°C for 56 days.	EN 14414 – D	Tensile Strength	100%
		Result	PASS
Resistance to Leaching - HOT WATER (Deionised water) 50°C for 56 days.	EN 14415-A	Tensile Strength	100%
		Result	PASS
Resistance to Leaching - AQUEOUS ALKALINE (Saturated Calcium Hydroxide) 50°C for 56 days.	EN 14415-B	Tensile Strength	100%
		Result	PASS
Resistance to Leaching - ORGANIC ALCOHOL (30% methanol, 30% isopropanol, 40% glycol) 50°C for 56 days.	EN 14415-C	Tensile Strength	100%
		Result	PASS

*Table above, values are typical, with the exception of thickness, which is nominal. Typical indicates the mean value derived from the samples taken for any one test as defined in the BS EN ISO standard - usually the mean of five samples. Nominal is a guide value



GEOSHIELD Verification Plan



DETAILS




Development Layout - Phase 3 includes Blocks D1, D2, D3 and D4



GEOSHIELD Verification Plan



DETAILS

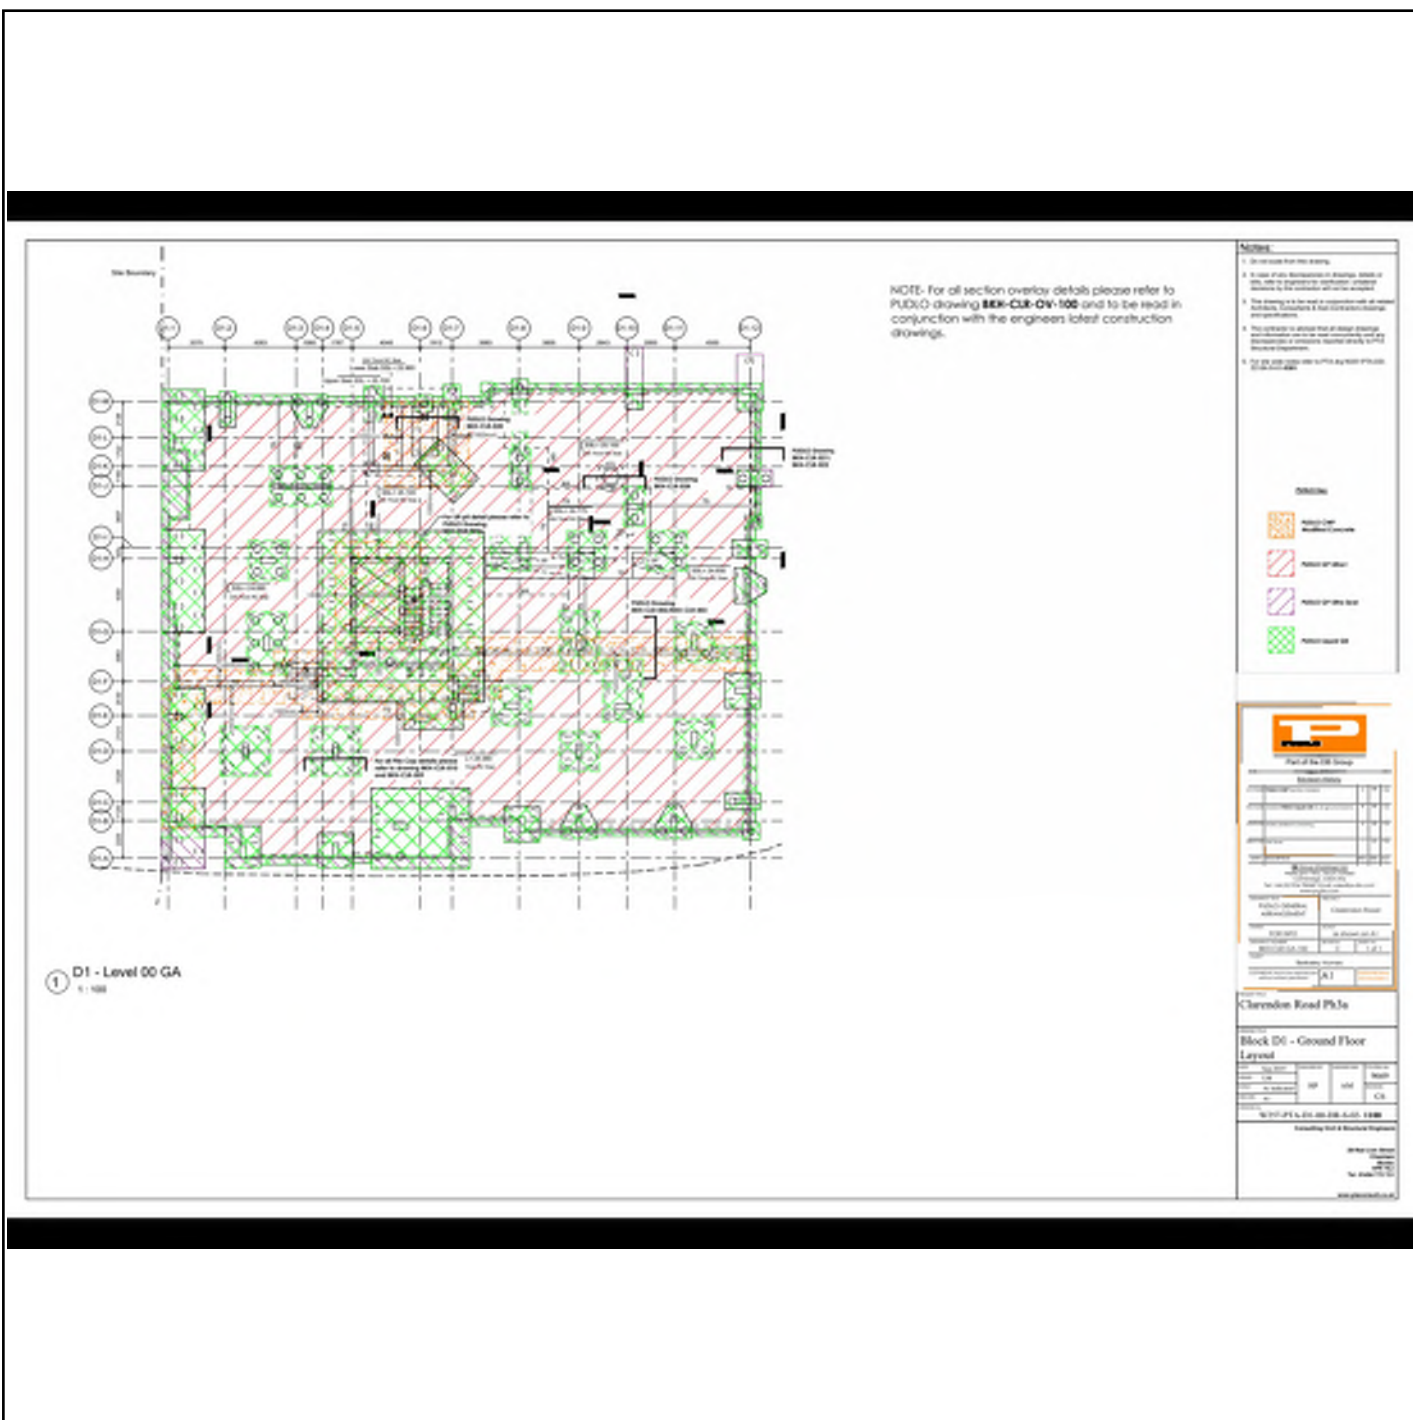

Block D1 Ground Floor Plan




DETAILS



GEOSHIELD Verification Plan



DETAILS

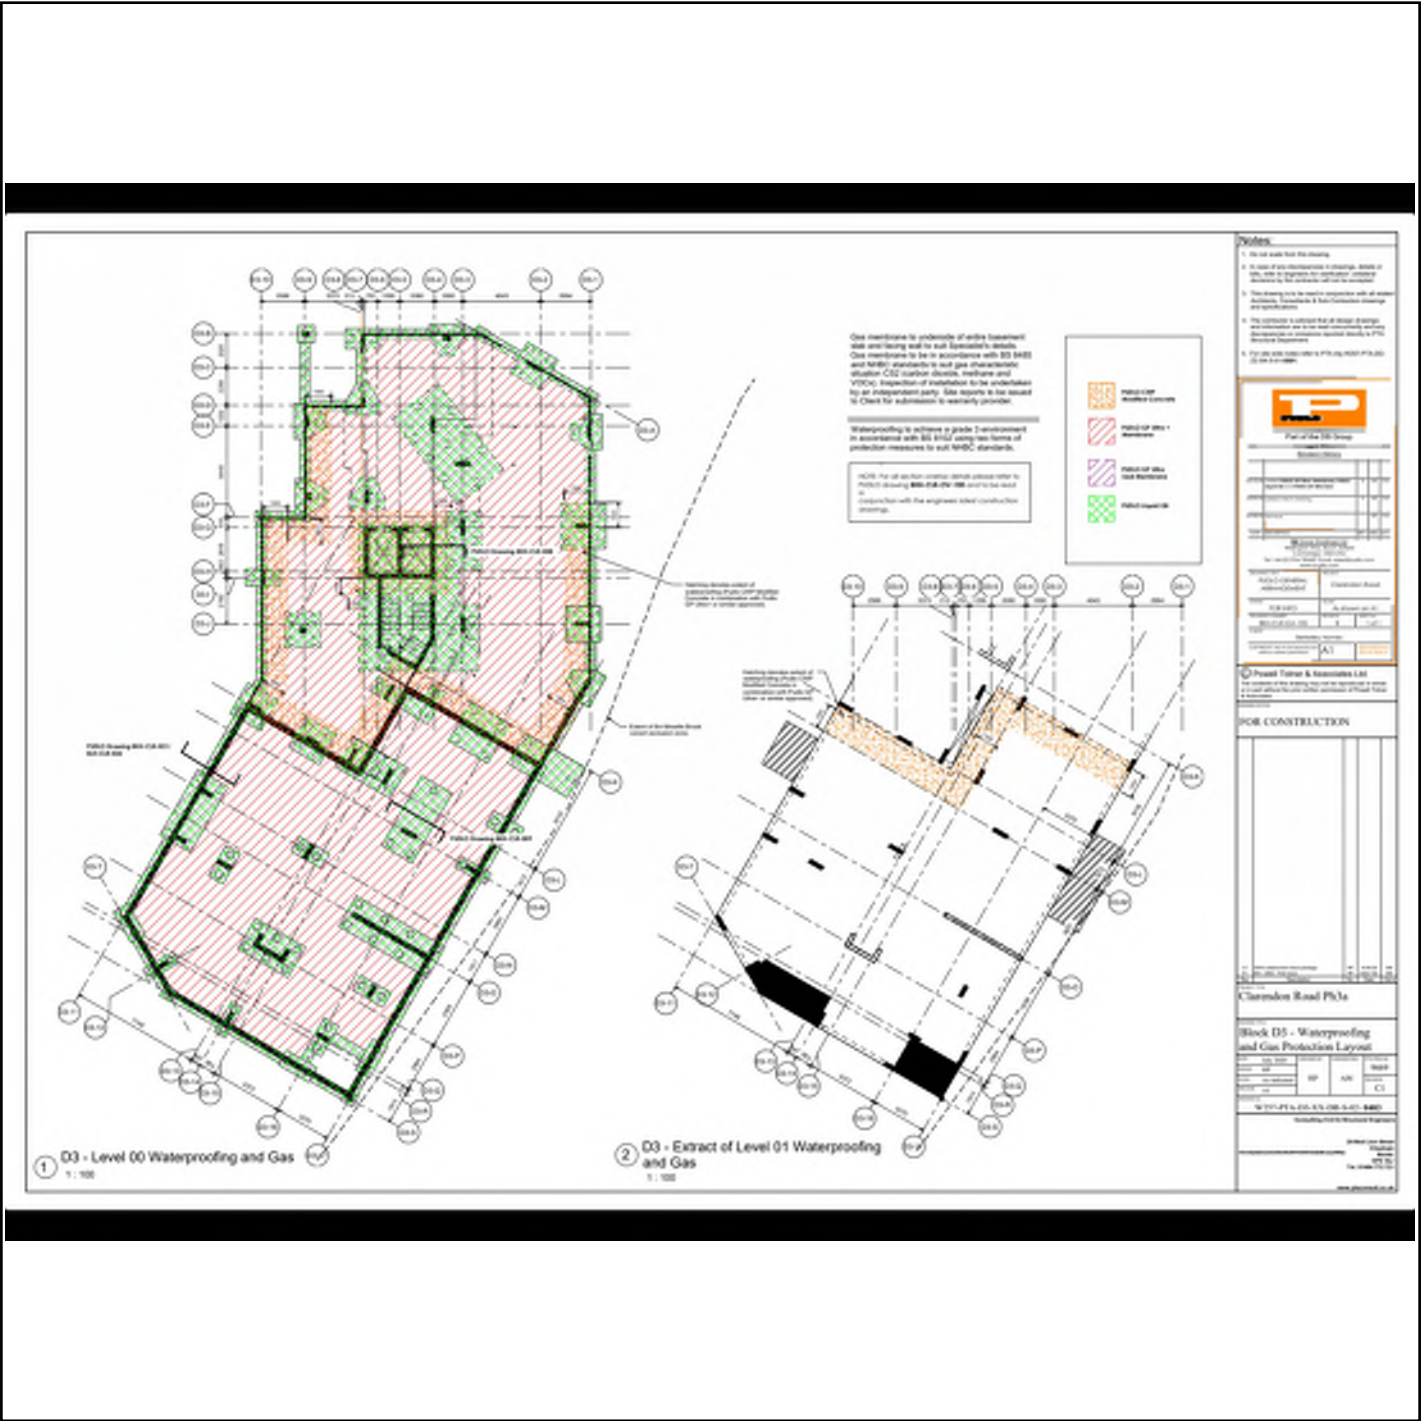


Block D3 Waterproofing and Gas Protection Layout



GEOSHIELD Verification Plan



DETAILS

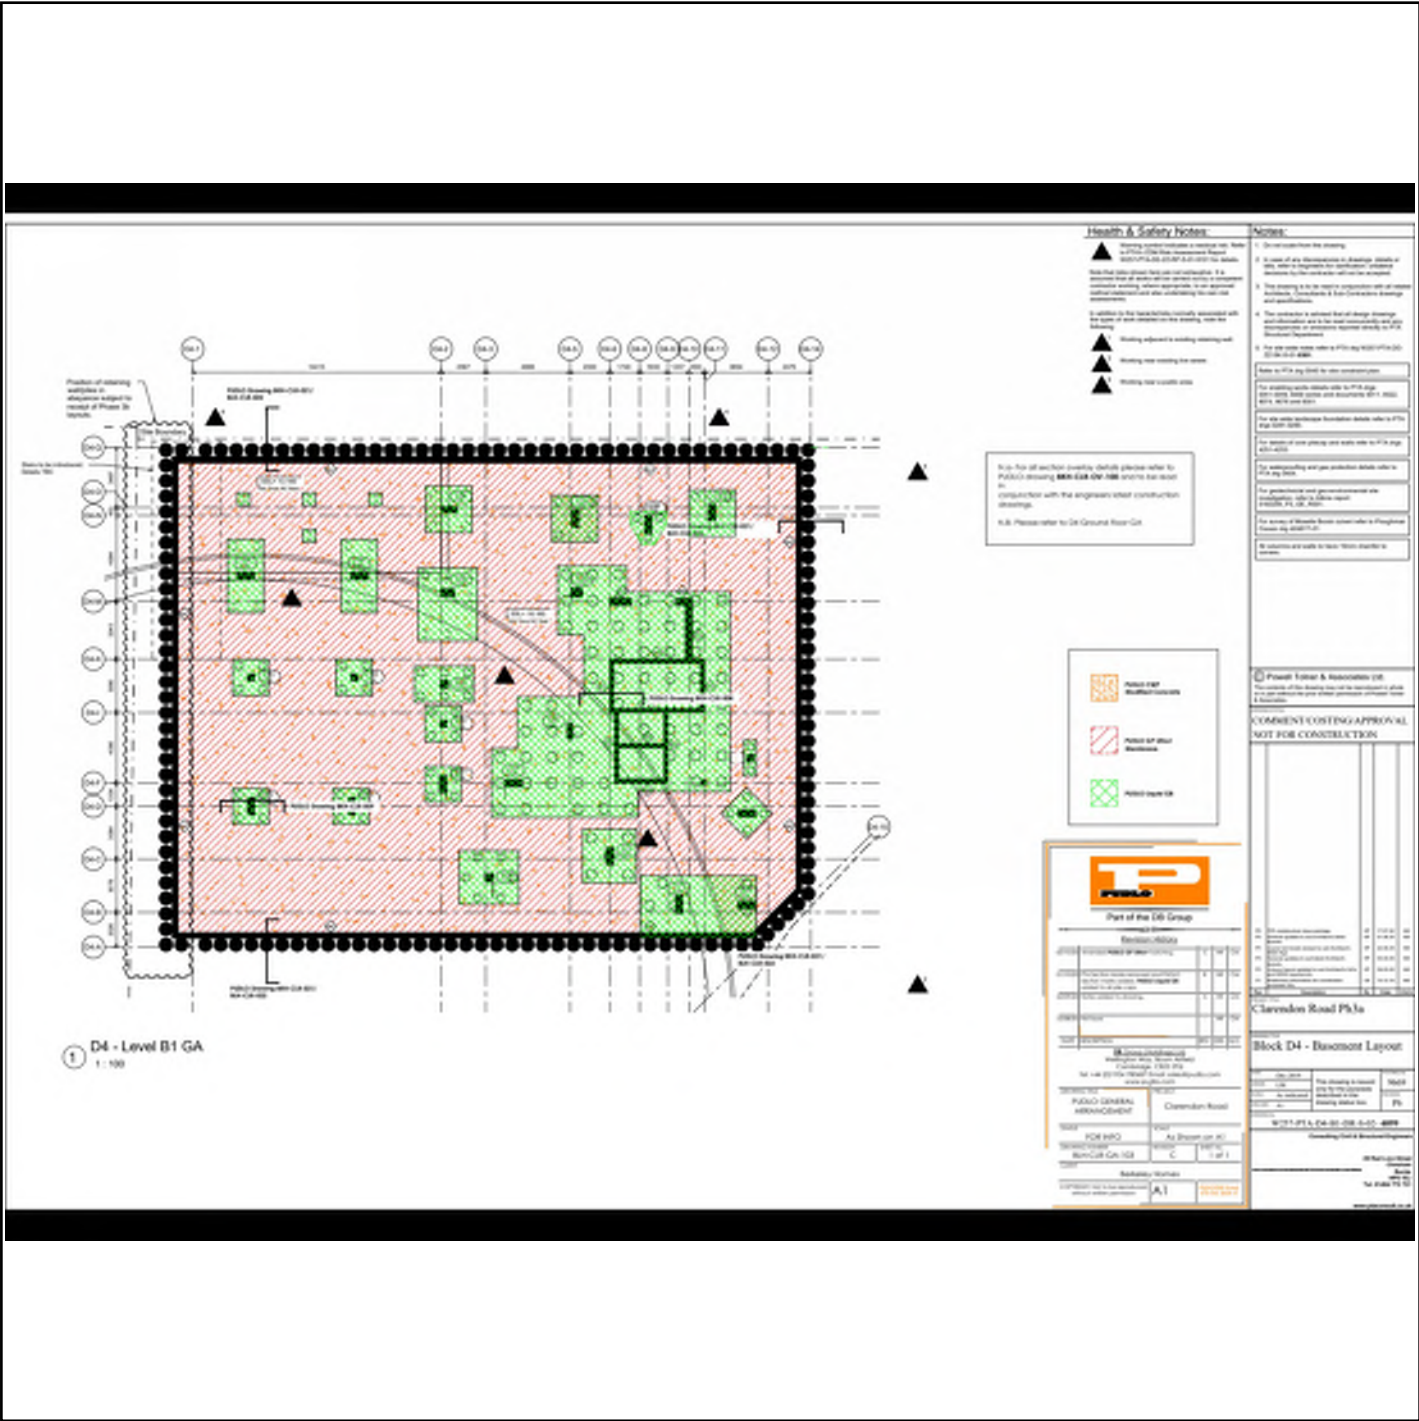




GEOSHIELD Verification Plan



DETAILS

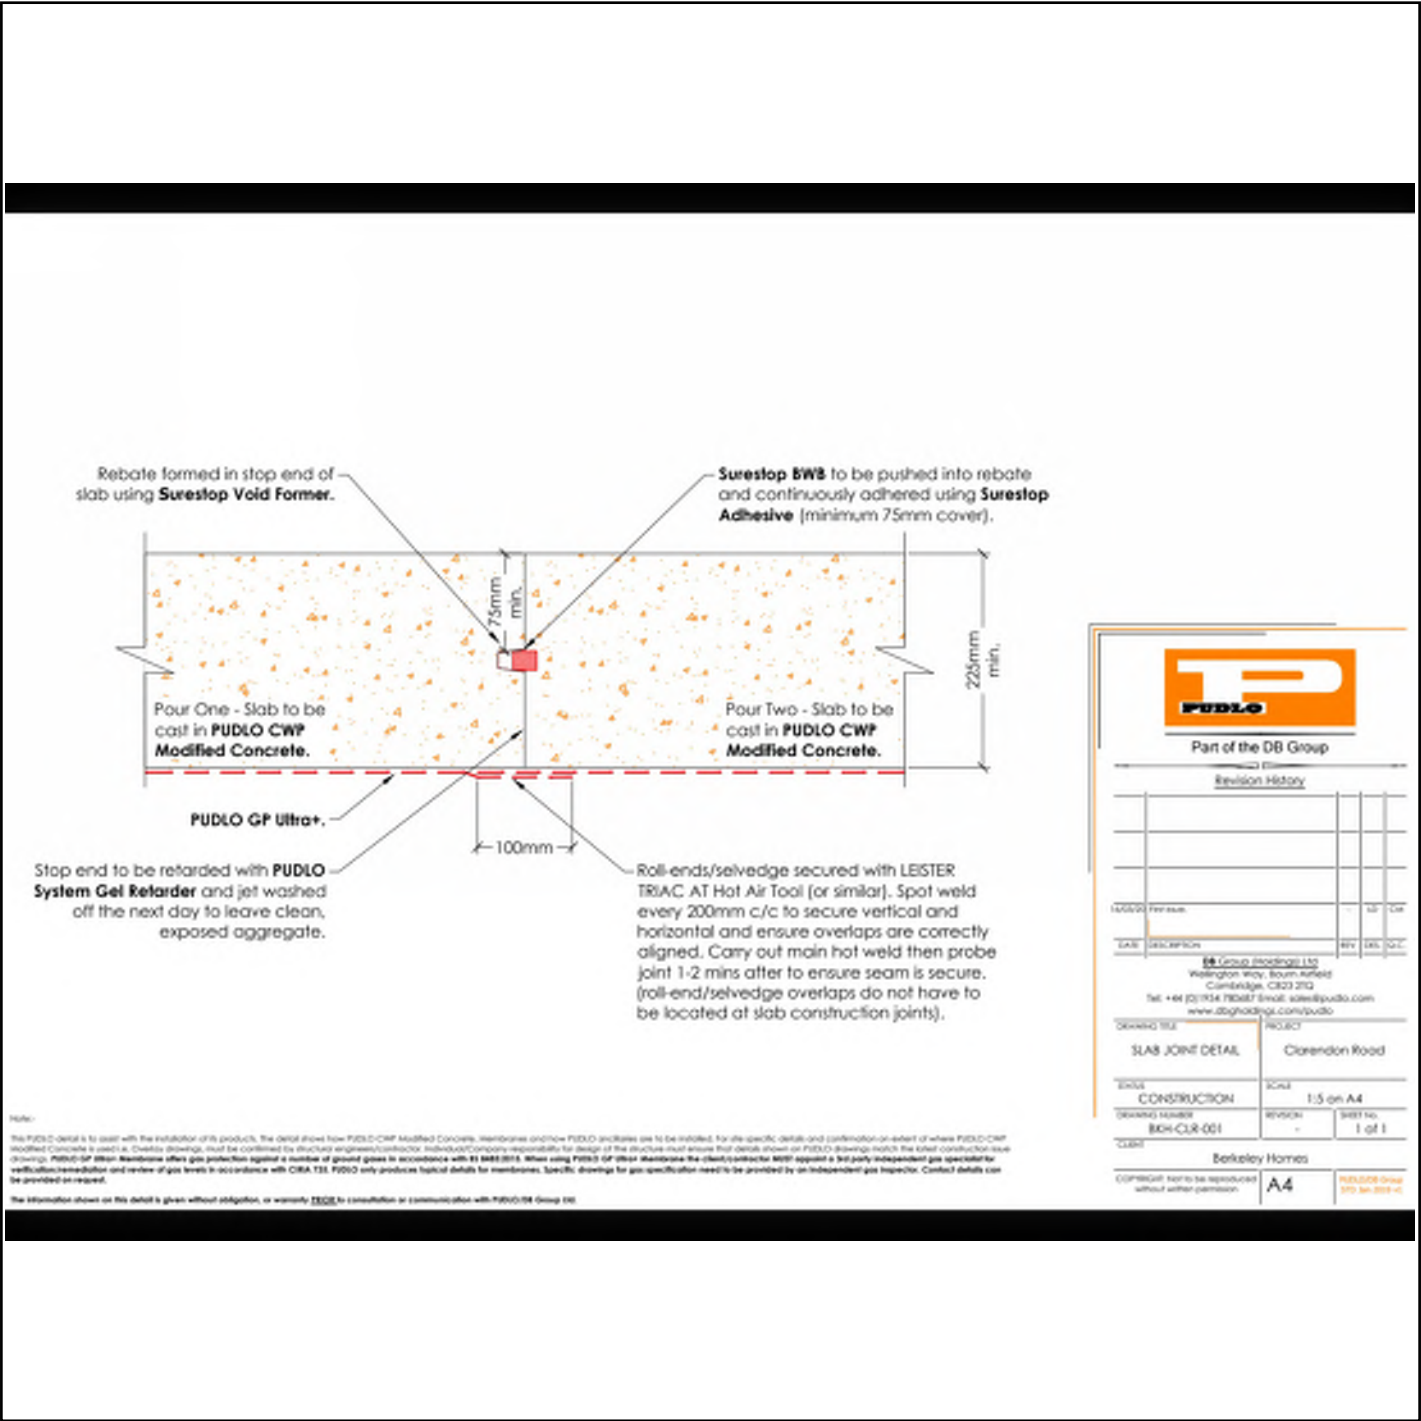




GEOSHIELD Verification Plan



DETAILS

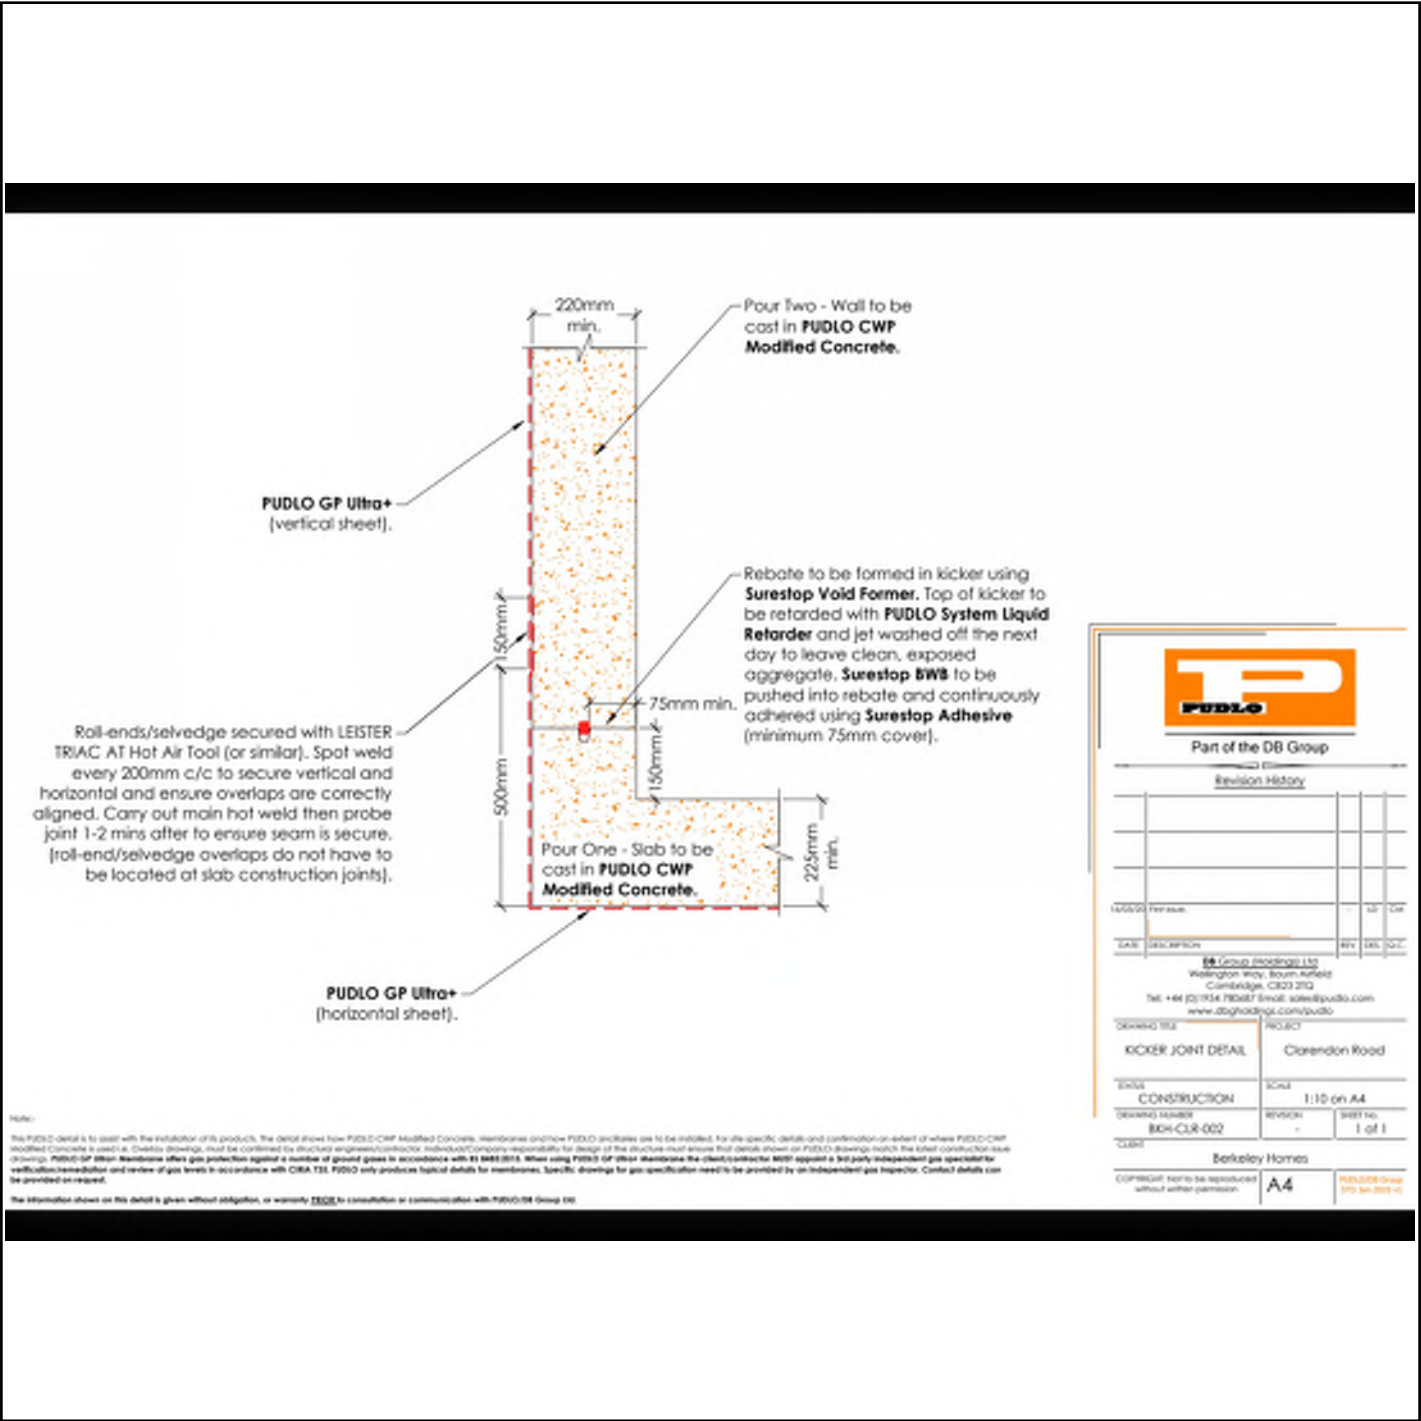




GEOSHIELD Verification Plan



DETAILS

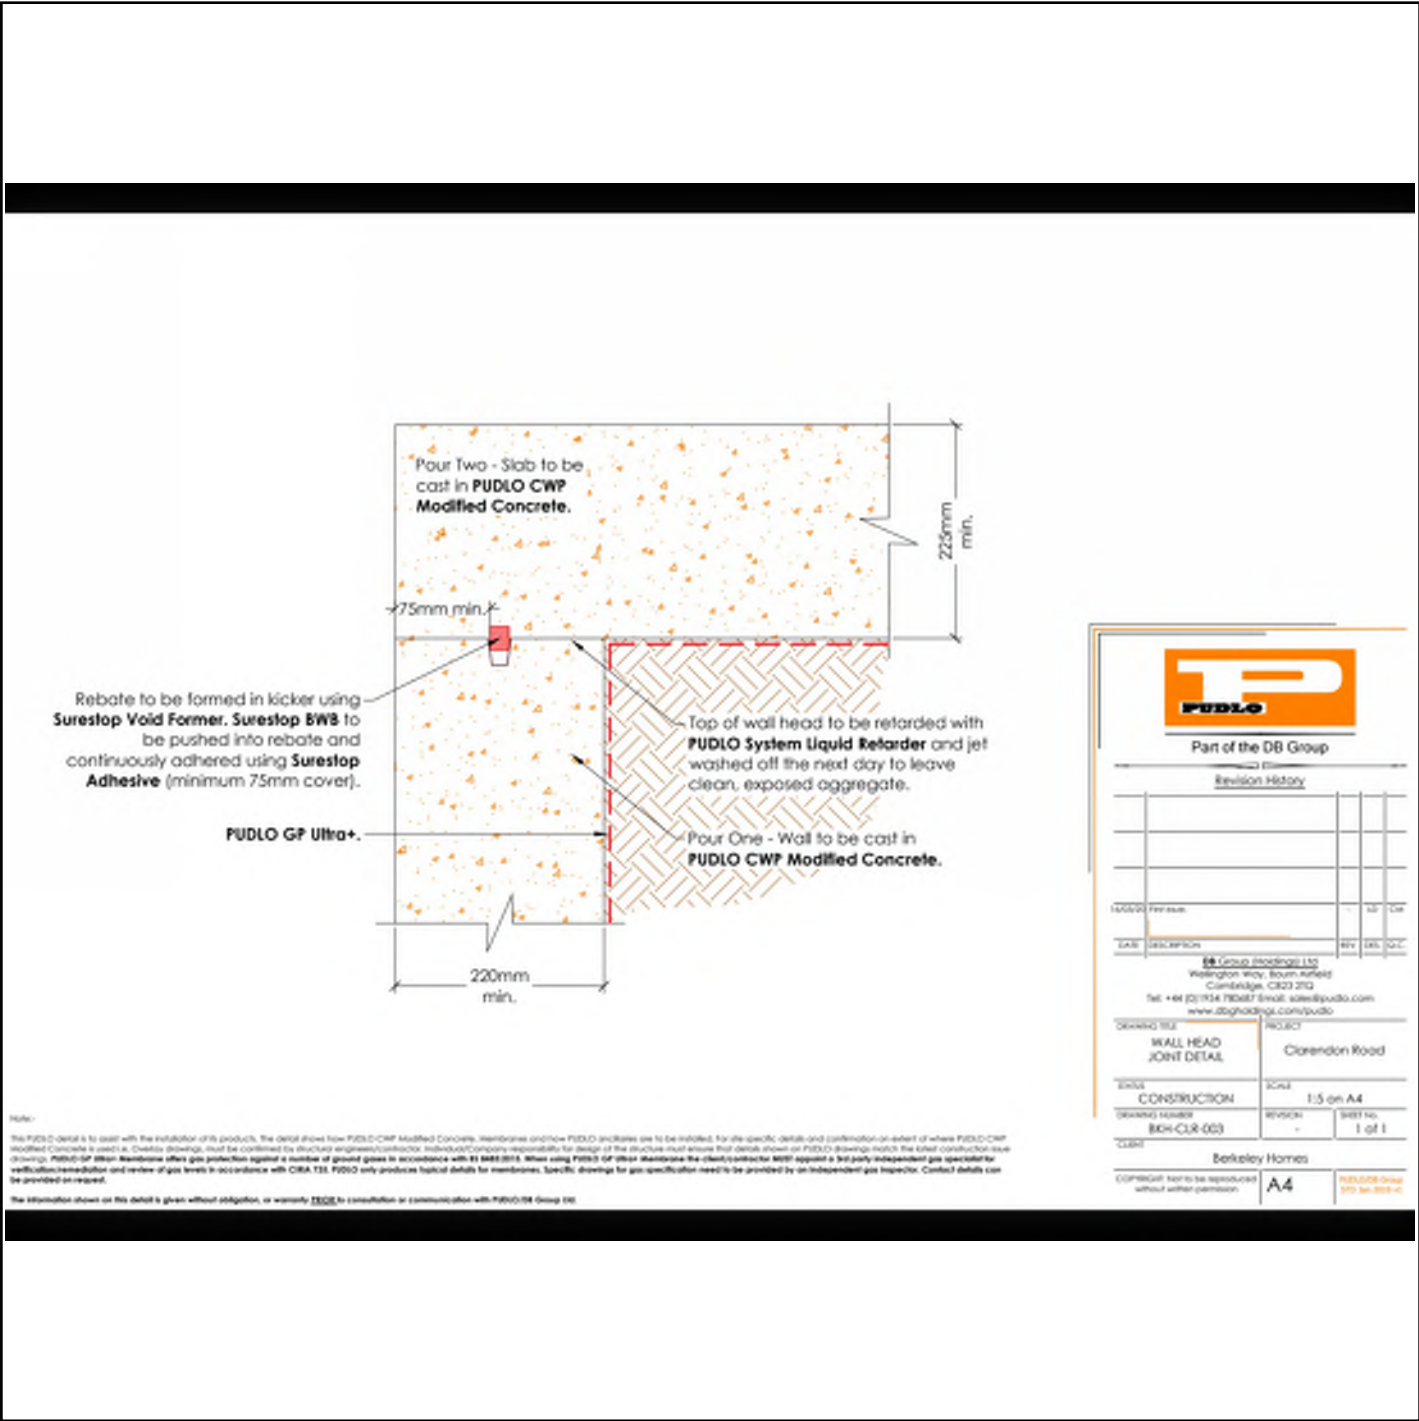




GEOSHIELD Verification Plan



DETAILS

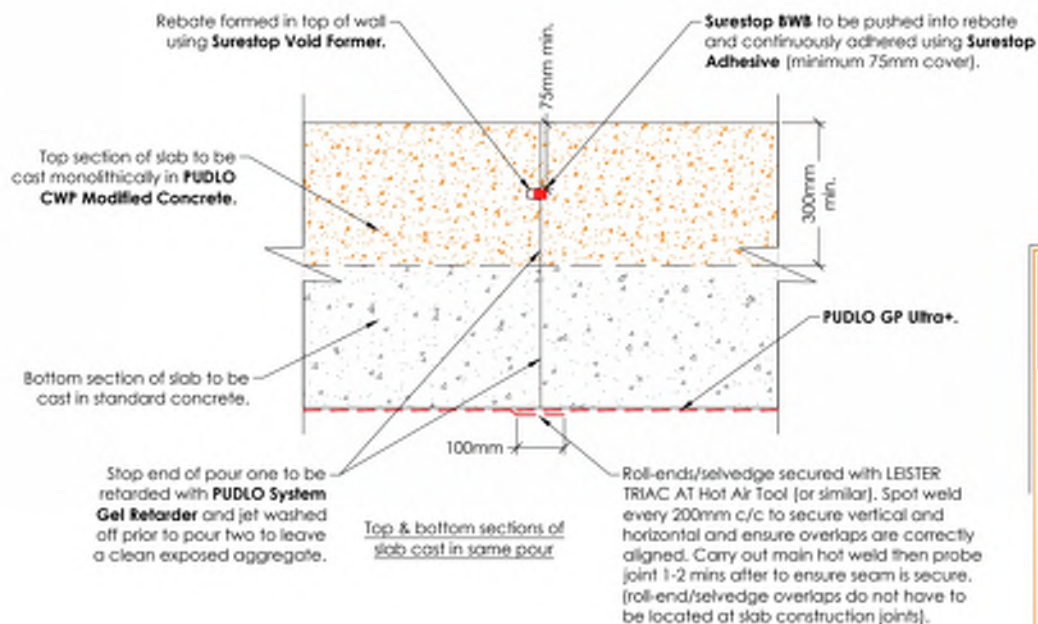

PUDLO

Part of the DB Group

Revision History

REV	DATE	DESCRIPTION
1	10/10/18	Initial Issue
2	10/10/18	Revised
3	10/10/18	Revised
4	10/10/18	Revised
5	10/10/18	Revised
6	10/10/18	Revised
7	10/10/18	Revised
8	10/10/18	Revised
9	10/10/18	Revised
10	10/10/18	Revised

DB Group (Holdings) Ltd
Wellington Way, South Ayrfield
Cambridge, CB23 2TQ
Tel: +44 (0)1354 780877 Email: sales@pudlo.com
www.dbholdings.com/pudlo

DETAILED TITLE: DEEP SLAB JOINT DETAIL PROJECT: Clarendon Road

STATUS: CONSTRUCTION Scale: 1:10 on A4

DESIGNED BY: BKH-CUR-004 Revision: 1 SHEET NO: 1 of 1

CHECKED BY: Berkeley Homes


Copyright: Not to be reproduced without written permission. A4 PUDLO Group 010 100 000 000



GEOSHIELD Verification Plan



DETAILS

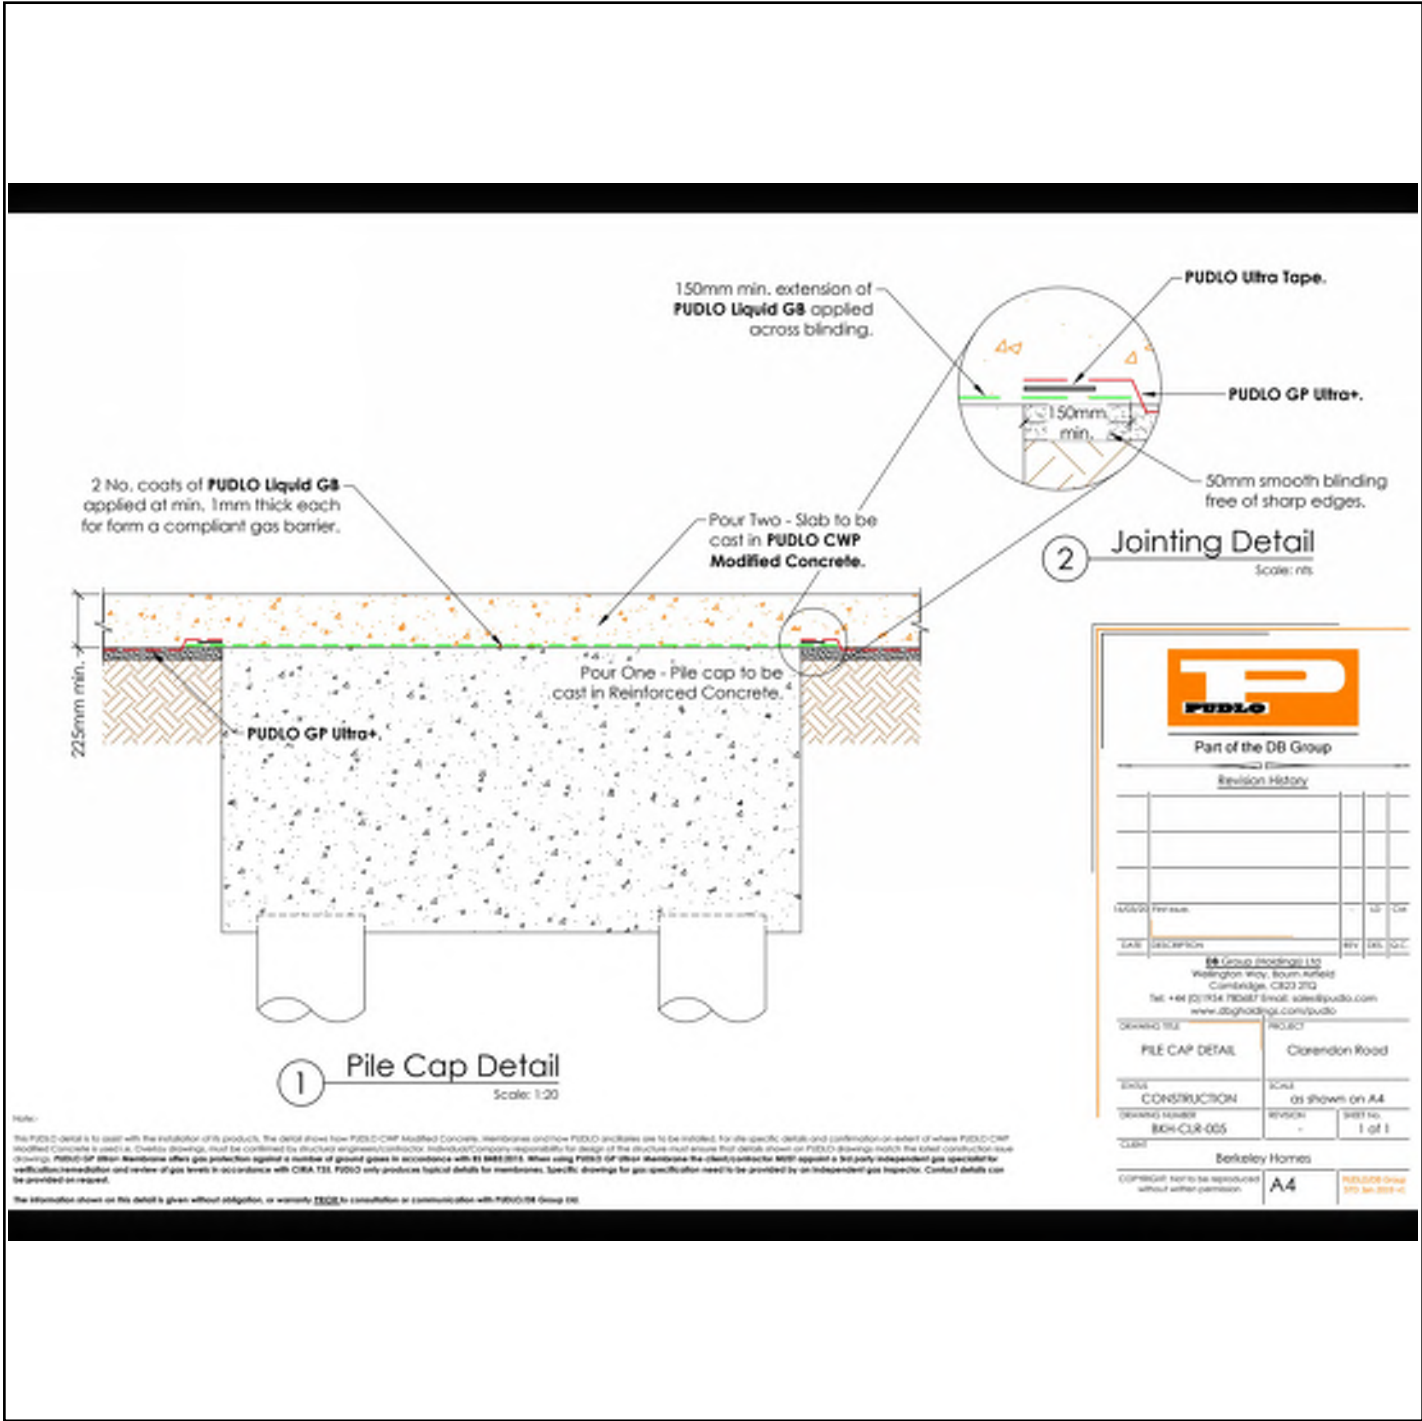


Pile Cap Detail



GEOSHIELD Verification Plan



DETAILS

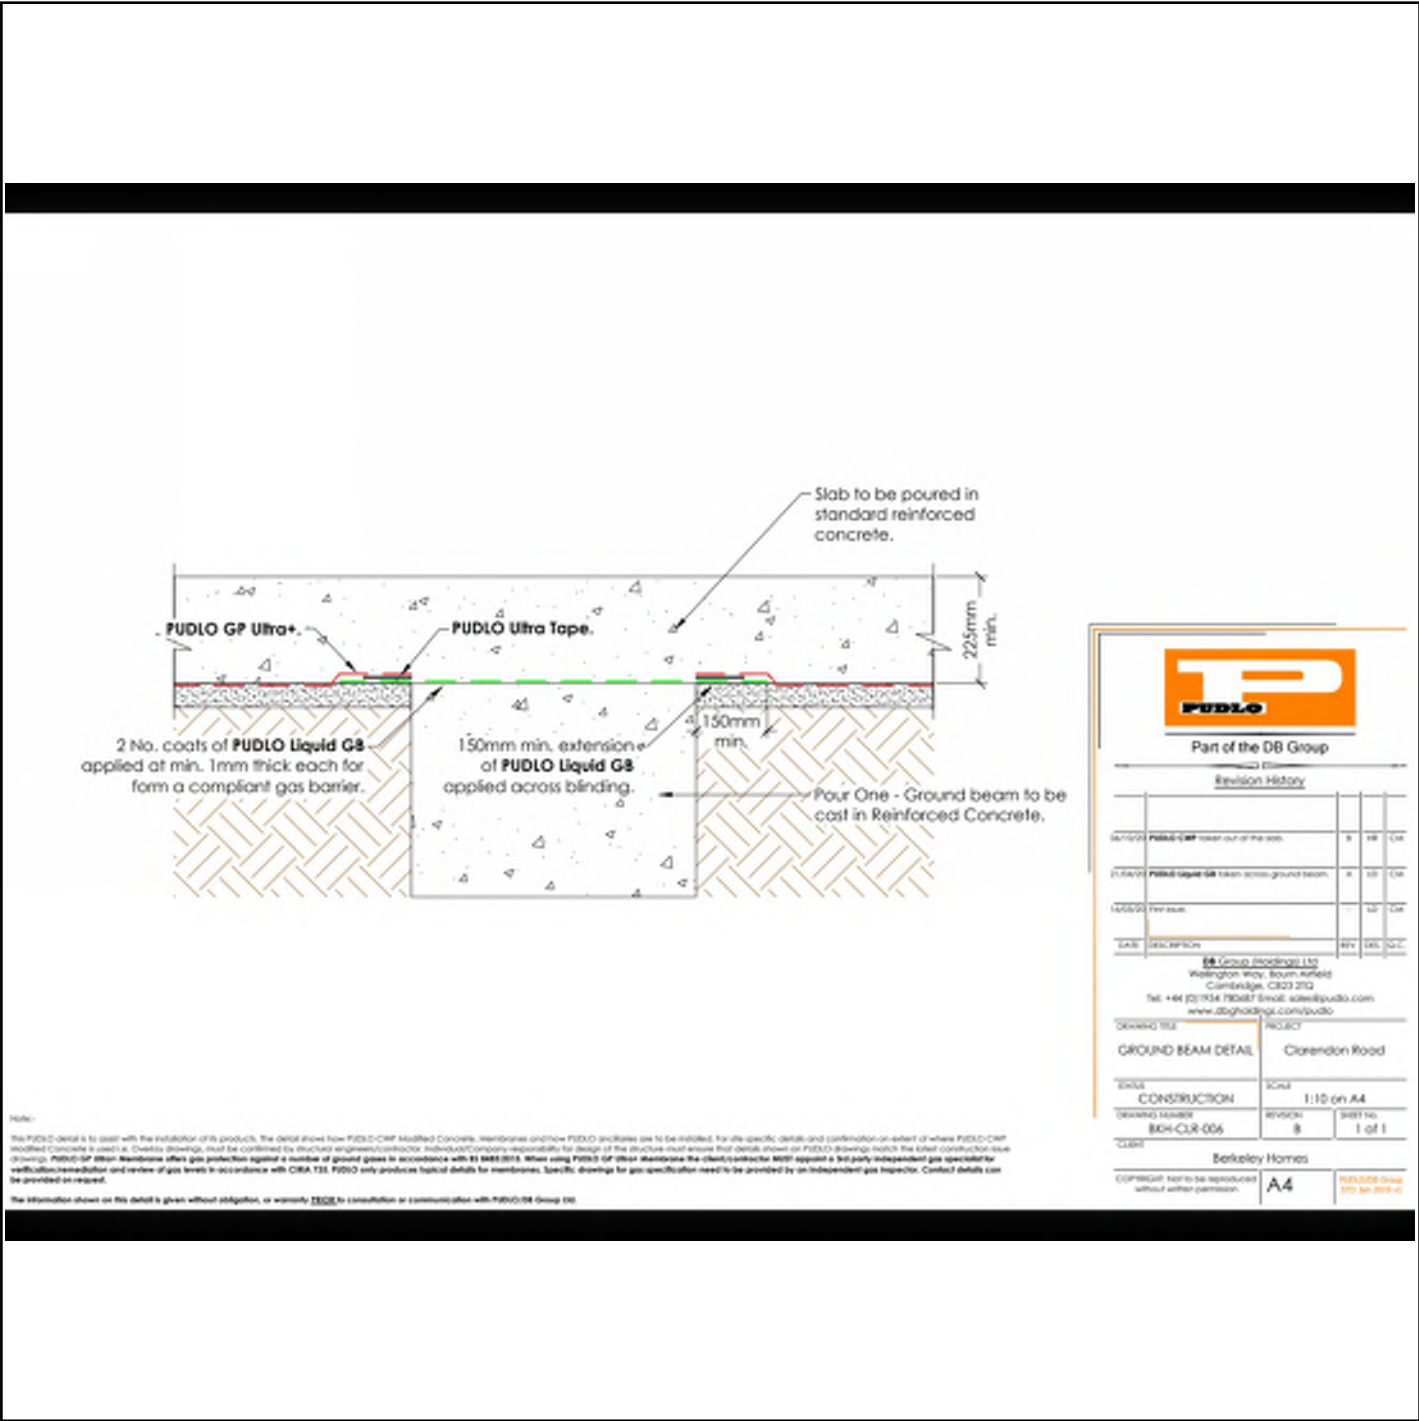




GEOSHIELD Verification Plan




DETAILS

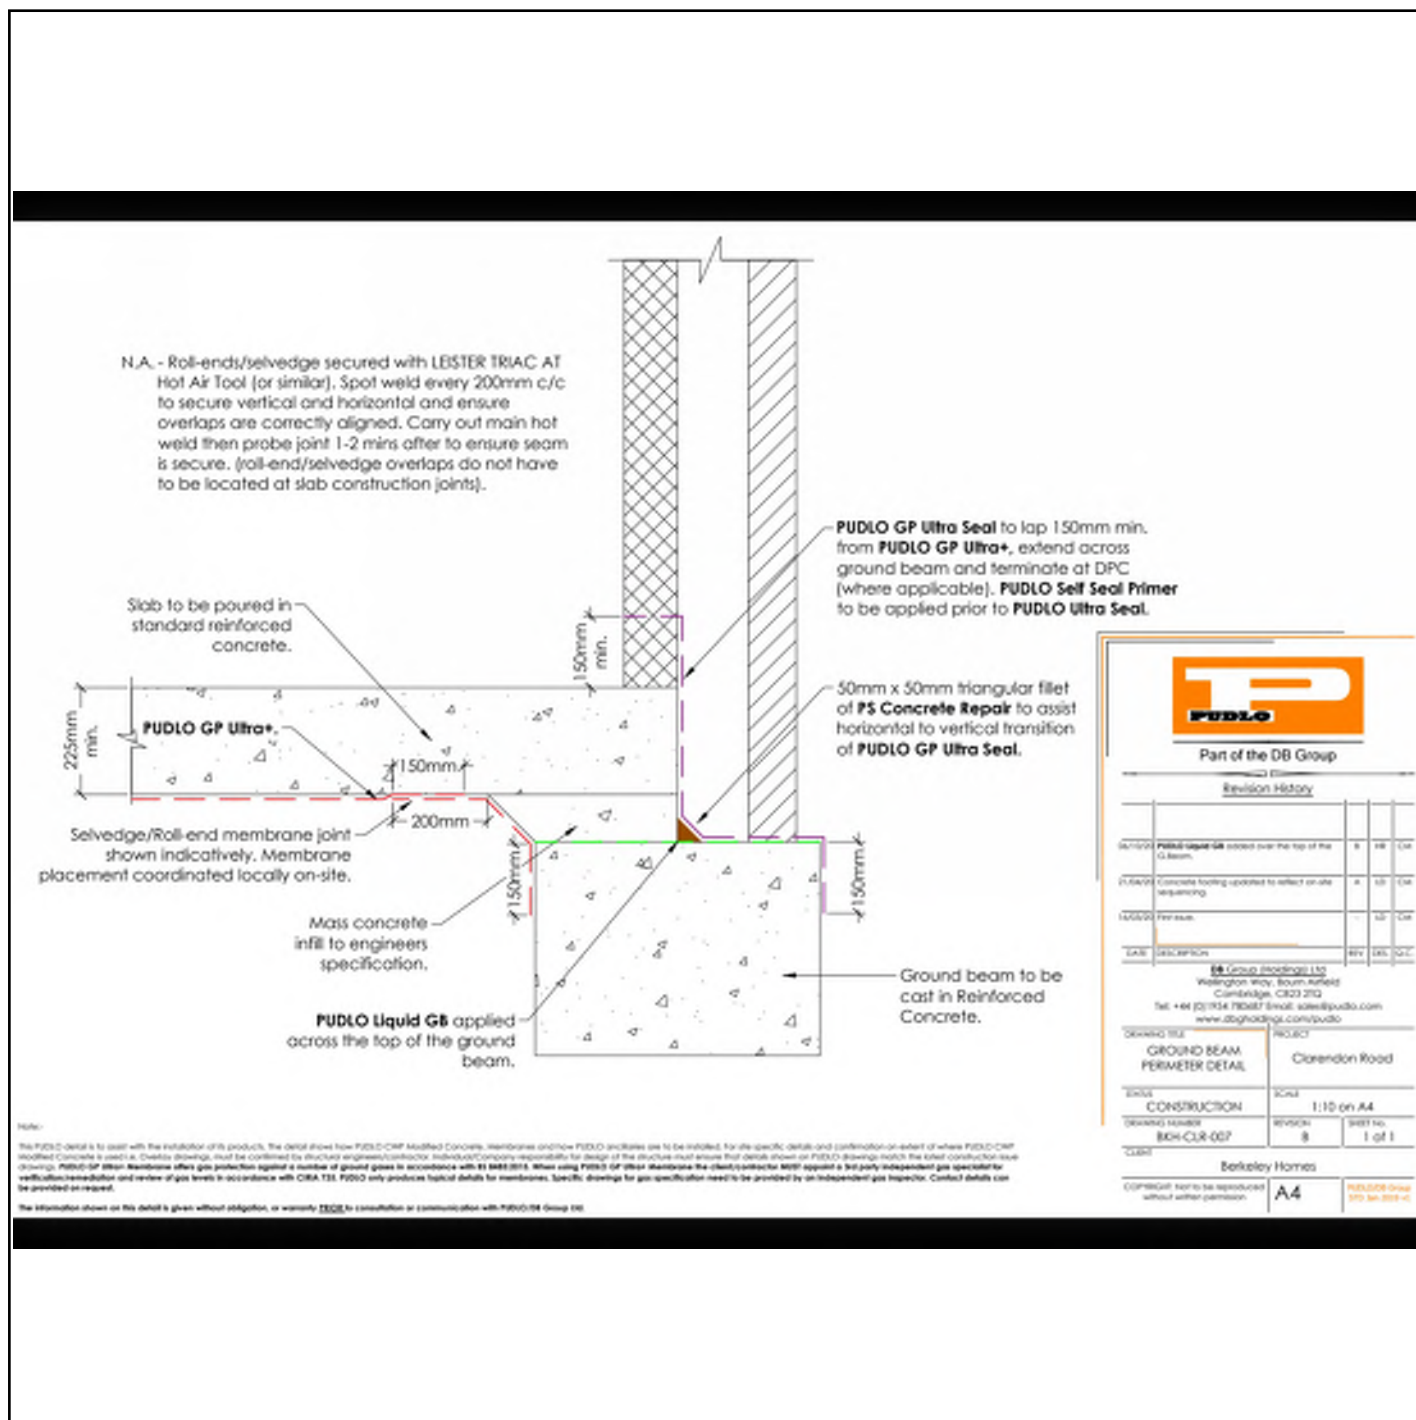

Ground Beam Perimeter Detail



DETAILS

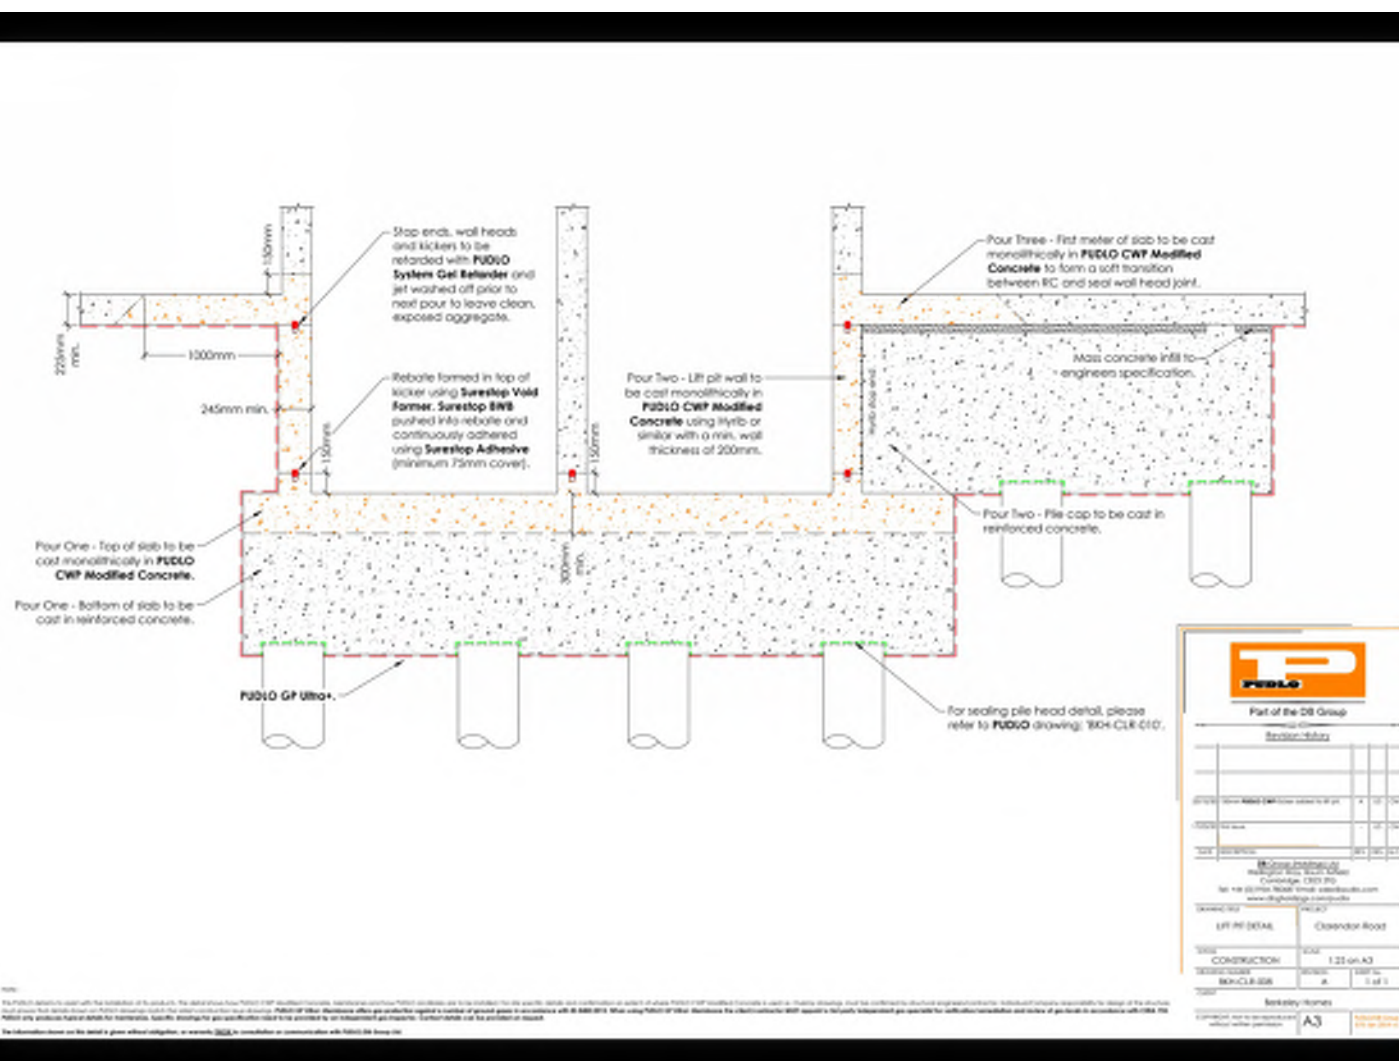


Lift Pit Detail



GEOSHIELD Verification Plan




DETAILS

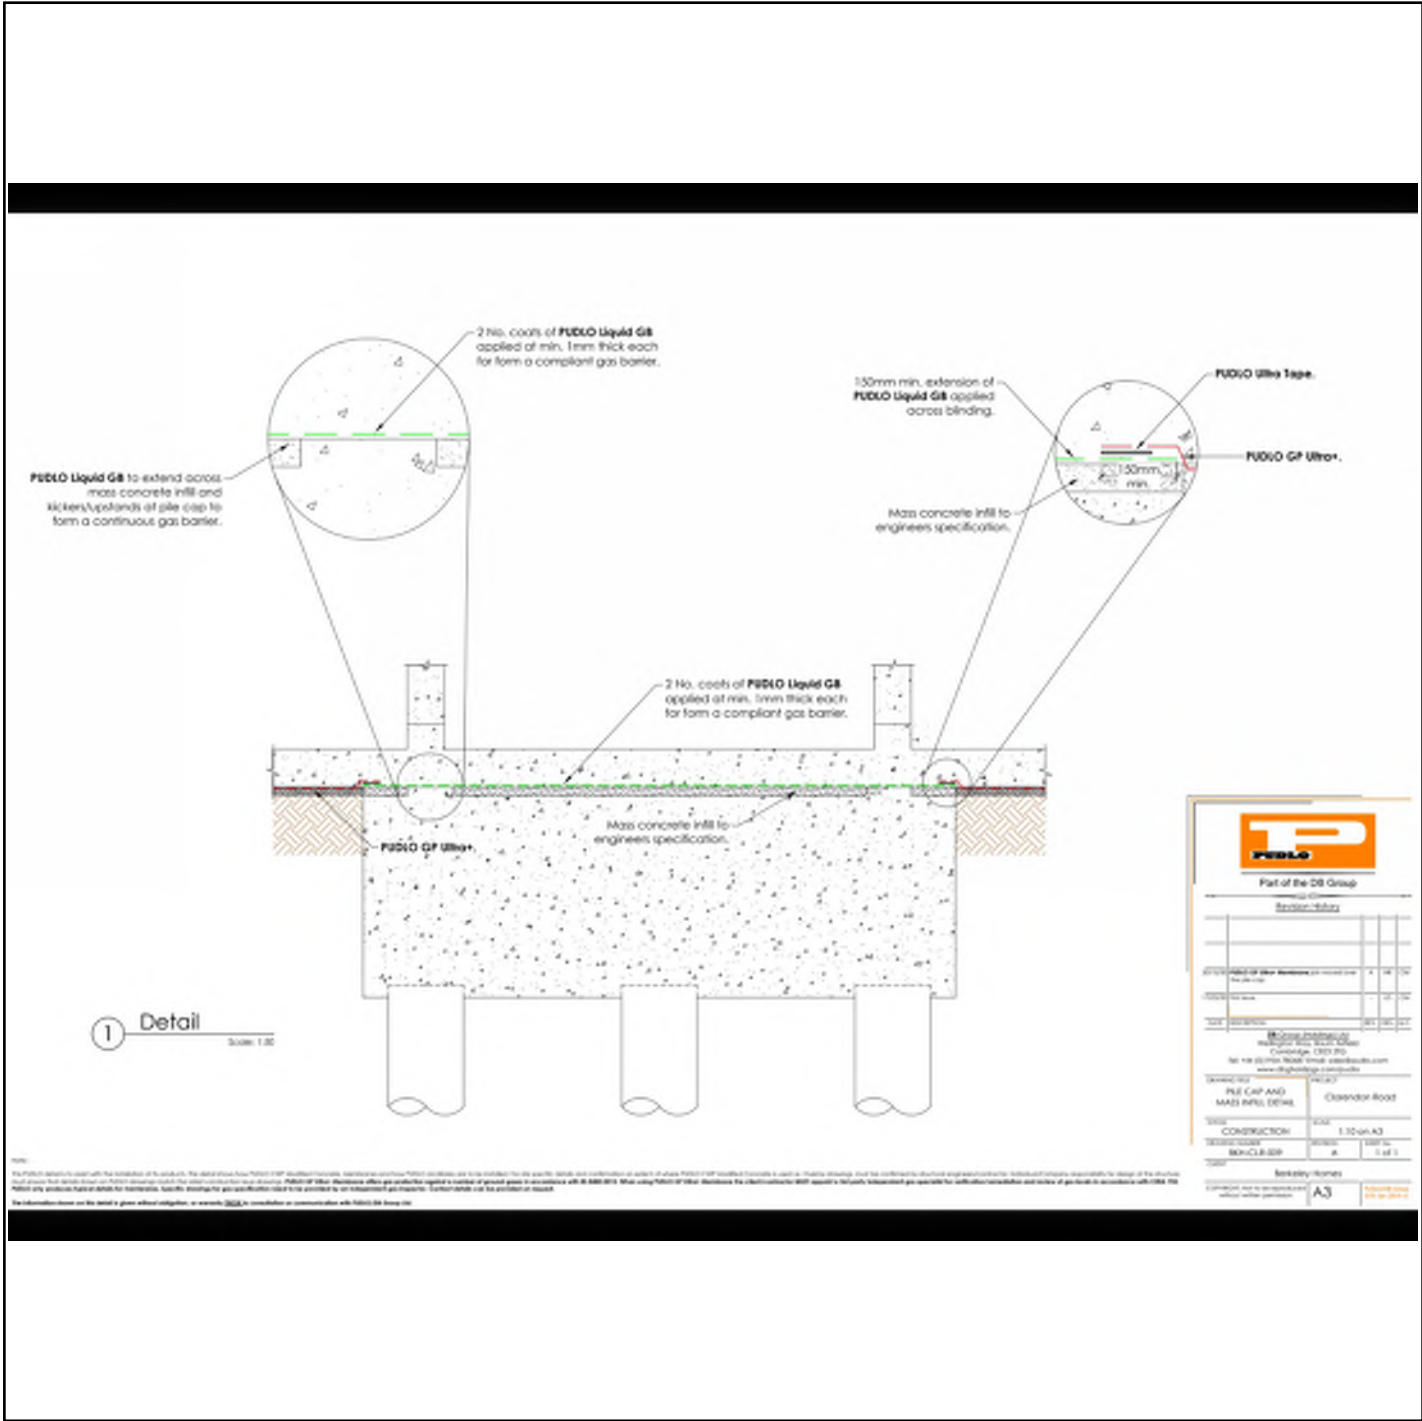




GEOSHIELD Verification Plan

DETAILS

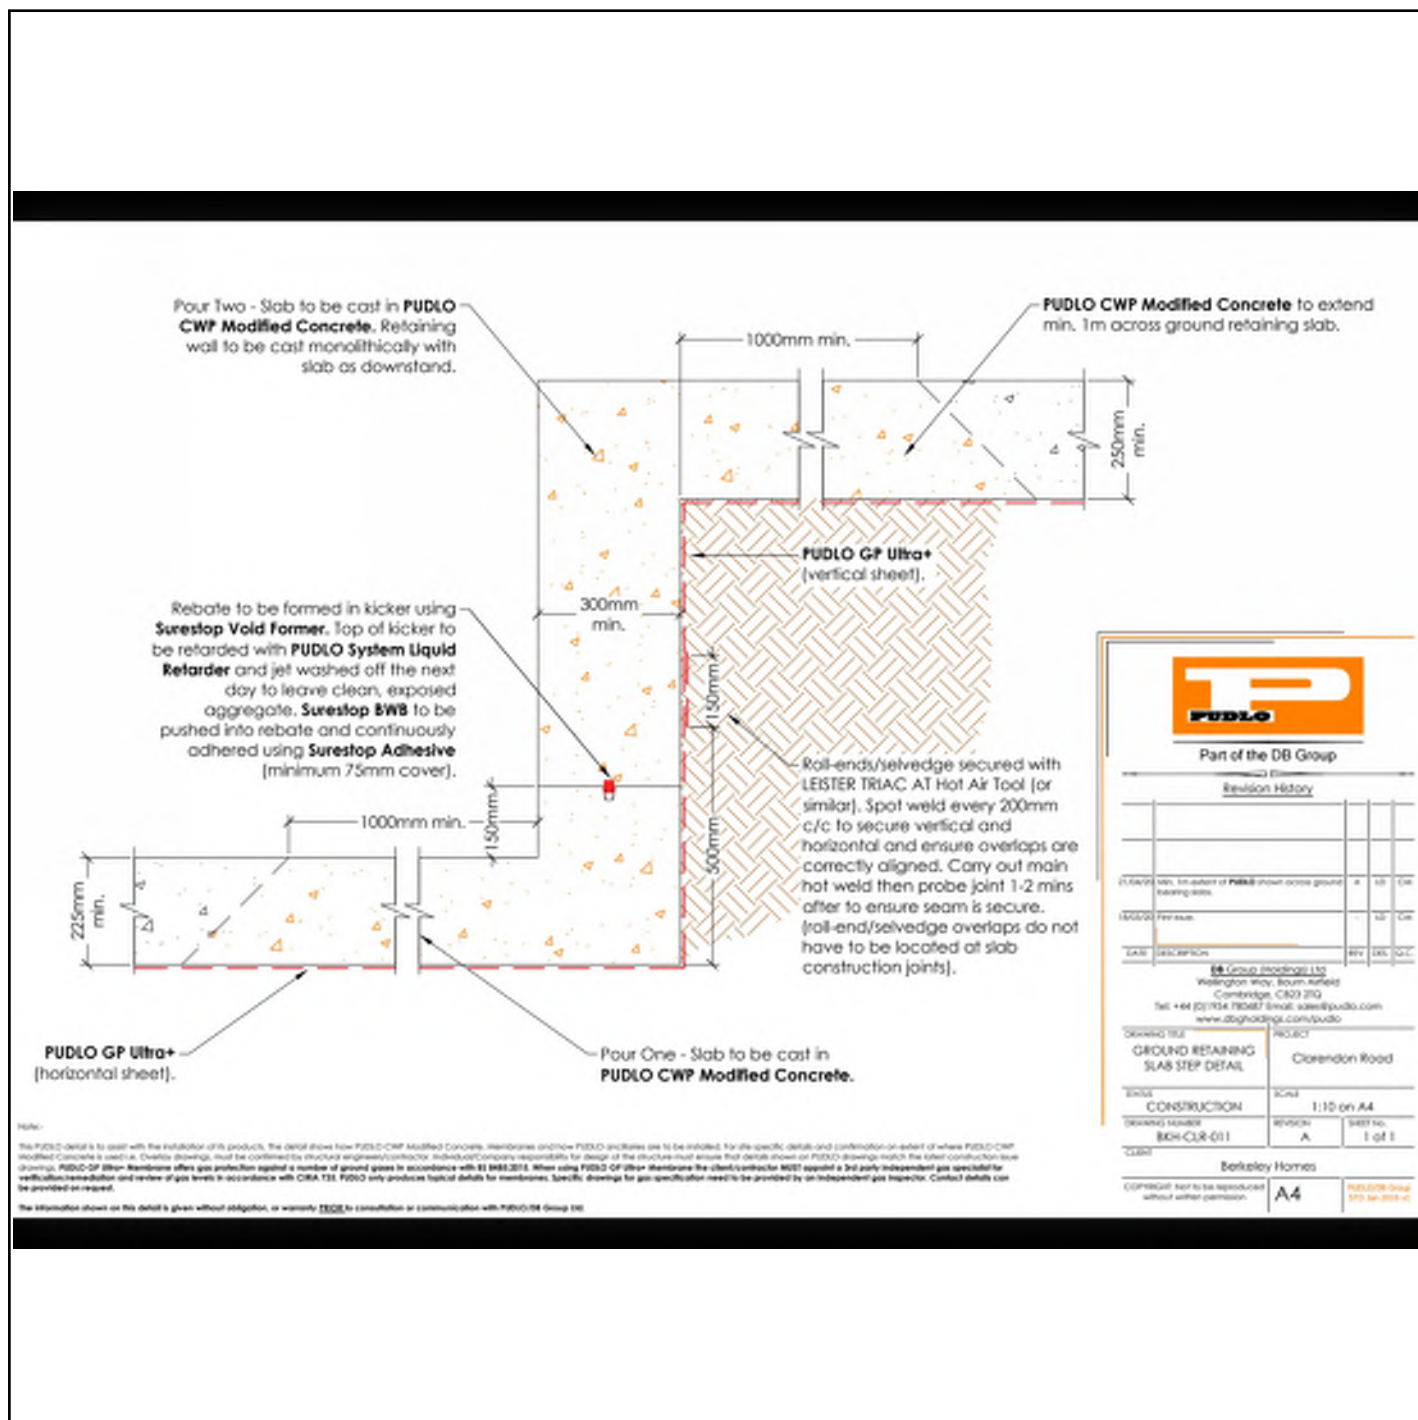


GEOSHIELD Verification Plan


DETAILS

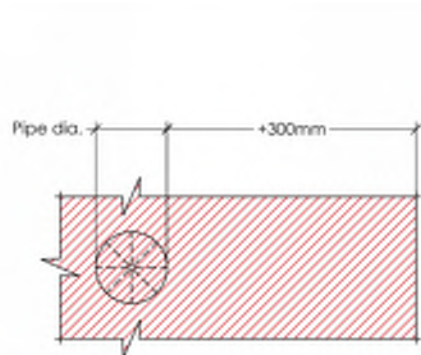

2 Membrane Patch Detail

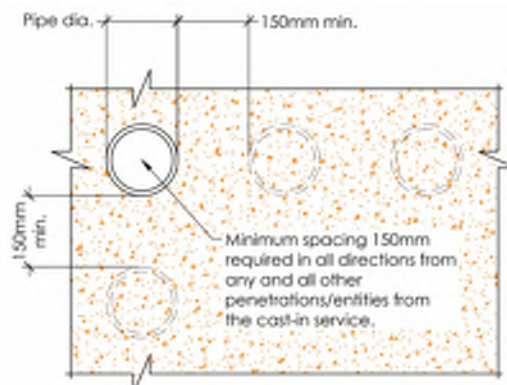

3 Penetration Spacing Detail

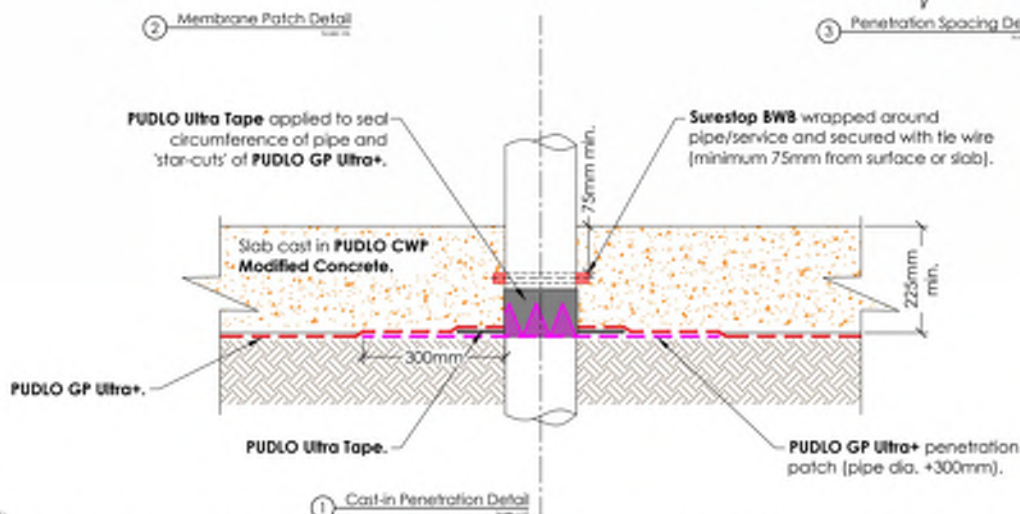


1 Cast-in Penetration Detail

Note:
This PUDLO detail is to assist with the installation of this product. The detail shows how PUDLO CWP Modified Concrete, membranes and how PUDLO indicates are to be installed, for site specific details and confirmation on extent of where PUDLO CWP Modified Concrete is used. Details drawings, must be confirmed by structural engineers/contractor. Individual company responsibility for design of the structure must ensure that details shown on PUDLO drawings match the other construction site drawings. PUDLO GP Ultra+ membrane offers gas protection against a number of ground gases in accordance with its BRE BREB. When using PUDLO GP Ultra+ please ensure the client/contractor BREB report is held by an independent gas specialist for verification/audit and review of gas levels in accordance with CIRA T35. PUDLO only produces typical details for membranes. Specific drawings for gas specification need to be provided by an independent gas inspector. Contact details can be provided on request.
The information shown on this detail is given without obligation, or warranty PUDLO in consultation or communication with PUDLO/DB Group Ltd.

PUDLO	
Part of the DB Group	
Revision History	
NO.	DESCRIPTION
1	Initial issue
2	Revised
3	Revised
4	Revised
5	Revised
6	Revised
7	Revised
8	Revised
9	Revised
10	Revised
11	Revised
12	Revised
13	Revised
14	Revised
15	Revised
16	Revised
17	Revised
18	Revised
19	Revised
20	Revised
21	Revised
22	Revised
23	Revised
24	Revised
25	Revised
26	Revised
27	Revised
28	Revised
29	Revised
30	Revised
31	Revised
32	Revised
33	Revised
34	Revised
35	Revised
36	Revised
37	Revised
38	Revised
39	Revised
40	Revised
41	Revised
42	Revised
43	Revised
44	Revised
45	Revised
46	Revised
47	Revised
48	Revised
49	Revised
50	Revised
51	Revised
52	Revised
53	Revised
54	Revised
55	Revised
56	Revised
57	Revised
58	Revised
59	Revised
60	Revised
61	Revised
62	Revised
63	Revised
64	Revised
65	Revised
66	Revised
67	Revised
68	Revised
69	Revised
70	Revised
71	Revised
72	Revised
73	Revised
74	Revised
75	Revised
76	Revised
77	Revised
78	Revised
79	Revised
80	Revised
81	Revised
82	Revised
83	Revised
84	Revised
85	Revised
86	Revised
87	Revised
88	Revised
89	Revised
90	Revised
91	Revised
92	Revised
93	Revised
94	Revised
95	Revised
96	Revised
97	Revised
98	Revised
99	Revised
100	Revised
101	Revised
102	Revised
103	Revised
104	Revised
105	Revised
106	Revised
107	Revised
108	Revised
109	Revised
110	Revised
111	Revised
112	Revised
113	Revised
114	Revised
115	Revised
116	Revised
117	Revised
118	Revised
119	Revised
120	Revised
121	Revised
122	Revised
123	Revised
124	Revised
125	Revised
126	Revised
127	Revised
128	Revised
129	Revised
130	Revised
131	Revised
132	Revised
133	Revised
134	Revised
135	Revised
136	Revised
137	Revised
138	Revised
139	Revised
140	Revised
141	Revised
142	Revised
143	Revised
144	Revised
145	Revised
146	Revised
147	Revised
148	Revised
149	Revised
150	Revised
151	Revised
152	Revised
153	Revised
154	Revised
155	Revised
156	Revised
157	Revised
158	Revised
159	Revised
160	Revised
161	Revised
162	Revised
163	Revised
164	Revised
165	Revised
166	Revised
167	Revised
168	Revised
169	Revised
170	Revised
171	Revised
172	Revised
173	Revised
174	Revised
175	Revised
176	Revised
177	Revised
178	Revised
179	Revised
180	Revised
181	Revised
182	Revised
183	Revised
184	Revised
185	Revised
186	Revised
187	Revised
188	Revised
189	Revised
190	Revised
191	Revised
192	Revised
193	Revised
194	Revised
195	Revised
196	Revised
197	Revised
198	Revised
199	Revised
200	Revised
201	Revised
202	Revised
203	Revised
204	Revised
205	Revised
206	Revised
207	Revised
208	Revised
209	Revised
210	Revised
211	Revised
212	Revised
213	Revised
214	Revised
215	Revised
216	Revised
217	Revised
218	Revised
219	Revised
220	Revised
221	Revised
222	Revised
223	Revised
224	Revised
225	Revised
226	Revised
227	Revised
228	Revised
229	Revised
230	Revised
231	Revised
232	Revised
233	Revised
234	Revised
235	Revised
236	Revised
237	Revised
238	Revised
239	Revised
240	Revised
241	Revised
242	Revised
243	Revised
244	Revised
245	Revised
246	Revised
247	Revised
248	Revised
249	Revised
250	Revised
251	Revised
252	Revised
253	Revised
254	Revised
255	Revised
256	Revised
257	Revised
258	Revised
259	Revised
260	Revised
261	Revised
262	Revised
263	Revised
264	Revised
265	Revised
266	Revised
267	Revised
268	Revised
269	Revised
270	Revised
271	Revised
272	Revised
273	Revised
274	Revised
275	Revised
276	Revised
277	Revised
278	Revised
279	Revised
280	Revised
281	Revised
282	Revised
283	Revised
284	Revised
285	Revised
286	Revised
287	Revised
288	Revised
289	Revised
290	Revised
291	Revised
292	Revised
293	Revised
294	Revised
295	Revised
296	Revised
297	Revised
298	Revised
299	Revised
300	Revised
301	Revised
302	Revised
303	Revised
304	Revised
305	Revised
306	Revised
307	Revised
308	Revised
309	Revised
310	Revised
311	Revised
312	Revised
313	Revised
314	Revised
315	Revised
316	Revised
317	Revised
318	Revised
319	Revised
320	Revised
321	Revised
322	Revised
323	Revised
324	Revised
325	Revised
326	Revised
327	Revised
328	Revised
329	Revised
330	Revised
331	Revised
332	Revised
333	Revised
334	Revised
335	Revised
336	Revised
337	Revised
338	Revised
339	Revised
340	Revised
341	Revised
342	Revised
343	Revised
344	Revised
345	Revised
346	Revised
347	Revised
348	Revised
349	Revised
350	Revised
351	Revised
352	Revised
353	Revised
354	Revised
355	Revised
356	Revised
357	Revised
358	Revised
359	Revised
360	Revised
361	Revised
362	Revised
363	Revised
364	Revised
365	Revised
366	Revised
367	Revised
368	Revised
369	Revised
370	Revised
371	Revised
372	Revised
373	Revised
374	Revised
375	Revised
376	Revised
377	Revised
378	Revised
379	Revised
380	Revised
381	Revised
382	Revised
383	Revised
384	Revised
385	Revised
386	Revised
387	Revised
388	Revised
389	Revised
390	Revised
391	Revised
392	Revised
393	Revised
394	Revised
395	Revised
396	Revised
397	Revised
398	Revised
399	Revised
400	Revised
401	Revised
402	Revised
403	Revised
404	Revised
405	Revised
406	Revised
407	Revised
408	Revised
409	Revised
410	Revised
411	Revised
412	Revised
413	Revised
414	Revised
415	Revised
416	Revised
417	Revised
418	Revised
419	Revised
420	Revised
421	Revised
422	Revised
423	Revised
424	Revised
425	Revised
426	Revised
427	Revised
428	Revised
429	Revised
430	Revised
431	Revised
432	Revised
433	Revised
434	Revised
435	Revised
436	Revised
437	Revised
438	Revised
439	Revised
440	Revised
441	Revised
442	Revised
443	Revised
444	Revised
445	Revised
446	Revised
447	Revised
448	Revised
449	Revised
450	Revised
451	Revised
452	Revised
453	Revised
454	Revised
455	Revised
456	Revised
457	Revised
458	Revised
459	Revised
460	Revised
461	Revised
462	Revised
463	Revised
464	Revised
465	Revised
466	Revised
467	Revised
468	Revised
469	Revised
470	Revised
471	Revised
472	Revised
473	Revised
474	Revised
475	

GEOSHIELD Verification Plan

DETAILS

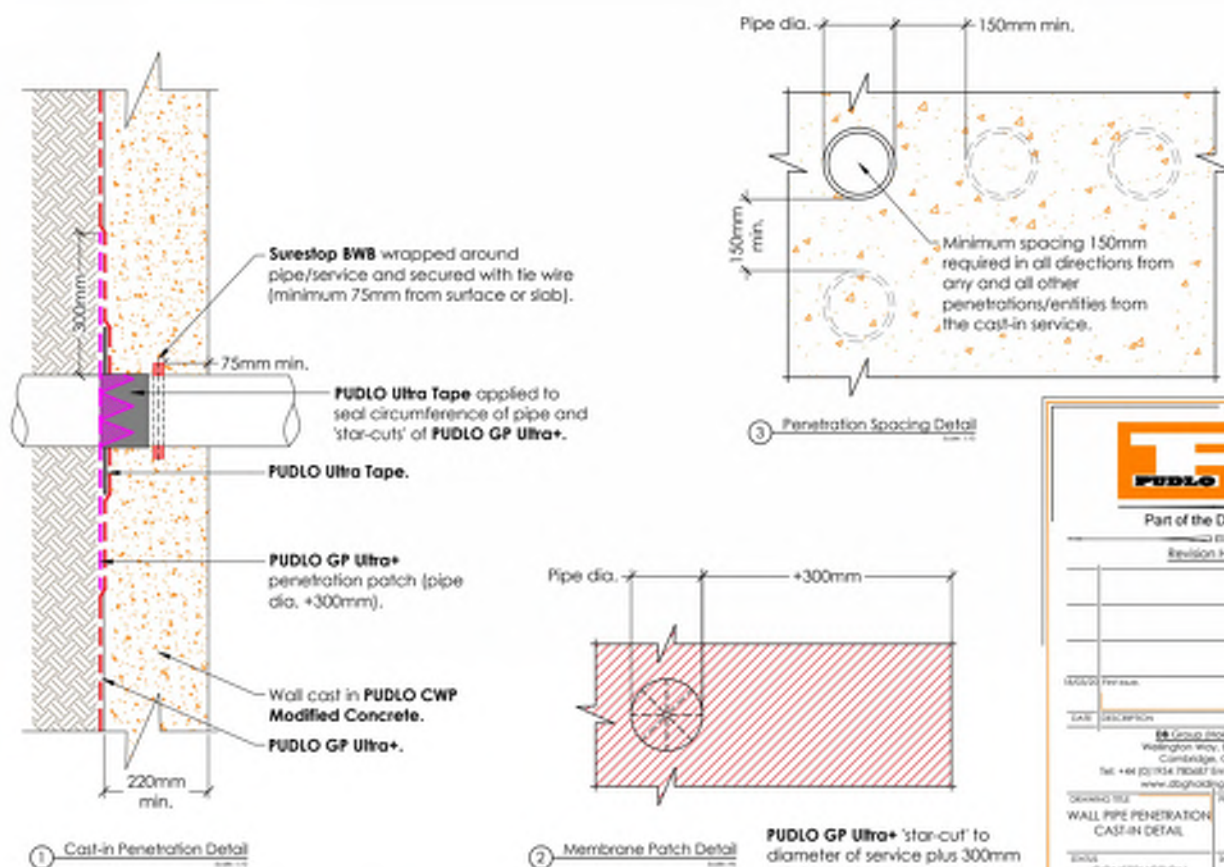

PUDLO

Part of the DB Group

Revision History

NO.	DESCRIPTION	REV.	DATE	BY	CHK.
1	Issue for construction	1	10/01/2024	DB Group	DB Group

DB Group Holdings Ltd
Warrington Way, Bourn Airfield
Cambridge, CB3 2TQ
Tel: +44 (0)1934 780877 Email: sales@pudlo.com
www.dbgroup.co.uk/pudlo

PROJECT: Clarendon Road

CONSTRUCTION: as shown on A4

REVISION: 1

SHEET NO: 1 of 1

CLIENT: Berkeley Homes



Copyright: Not to be reproduced without written permission.

A4

PUDLO Group Ltd 2024



DETAILS

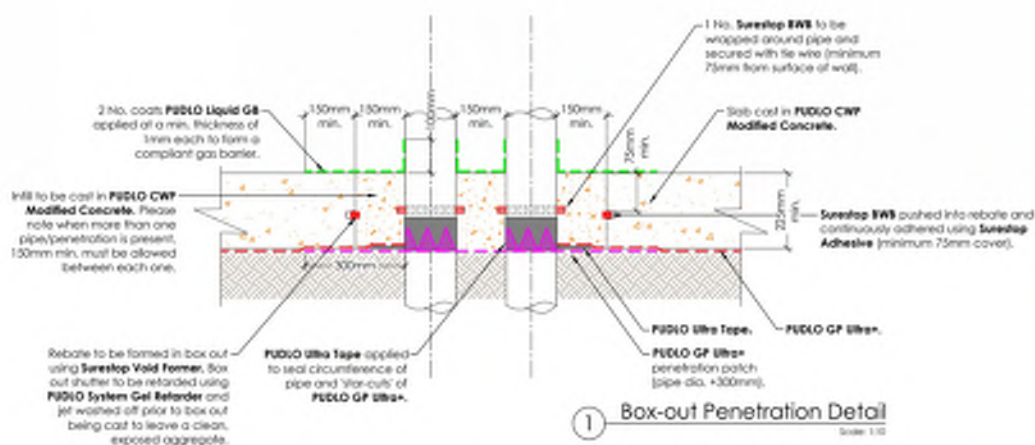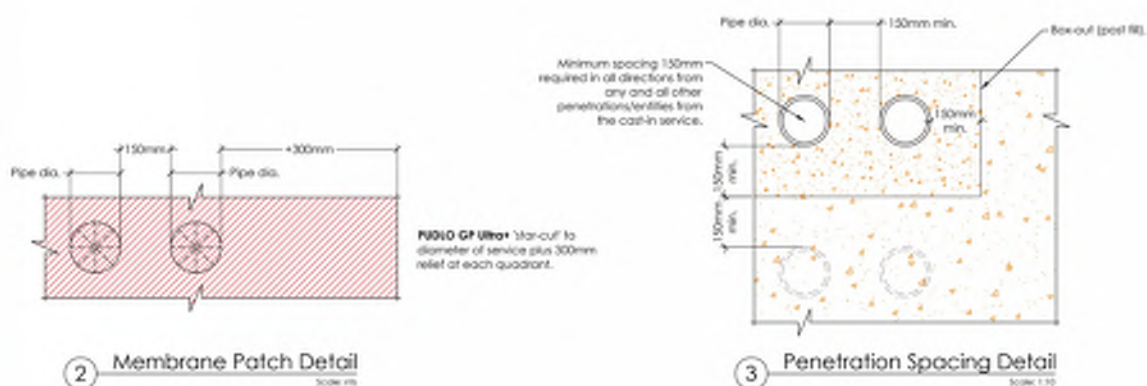[illegible]

© 2019 Bentley Systems, Incorporated. Bentley, the "B" Bentley logo, MicroStation, and MicroStation V8i are registered trademarks or trademarks of Bentley Systems, Incorporated or Bentley Software, Inc. All other brands and product names are trademarks of their respective owners. Bentley reserves the right to alter product offerings and specifications at any time without notice, and is not responsible for typographical or graphical errors that appear in this document. DATED: 2019.05.01

For information about our full range of services, visit www.2020.org or contact us at 1-800-2020-2020.



Diagram 1: Box-out Penetration Detail
 Scale: 1:10
 Labels: FUDLO GF Ultra, FUDLO Ultra Tape, FUDLO Liquid GB, Wall cast in FUDLO CWP Modified Concrete, 2 No. coats FUDLO Liquid GB applied at a min. thickness of 1mm each to form a compliant gas barrier.

Diagram 2: Membrane Patch Detail
 Scale: n/a
 Labels: Rebate to be formed in box out using Surestop Void Former. Box out shutter to be retarded using FUDLO System Gel Refractor and jet washed off prior to box out being cast to leave a clean, exposed aggregate. FUDLO GF Ultra, FUDLO Ultra Tape, FUDLO CWP Modified Concrete.

Diagram 3: Penetration Spacing Detail
 Scale: 1:10
 Labels: FUDLO GF Ultra, FUDLO Ultra Tape, FUDLO Liquid GB, Surestop BWR pushed into rebate and continuously adhered using Surestop Adhesive (minimum 75mm cover), 1 No. Surestop BWR to be wrapped around pipe and secured with tie wire (minimum 75mm from surface of wall).


[illegible]

For information about our full range of services, visit www.2020.org or call 1-800-2020-2020.

Wall Pipe Penetration Box-Out Detail




DETAILS

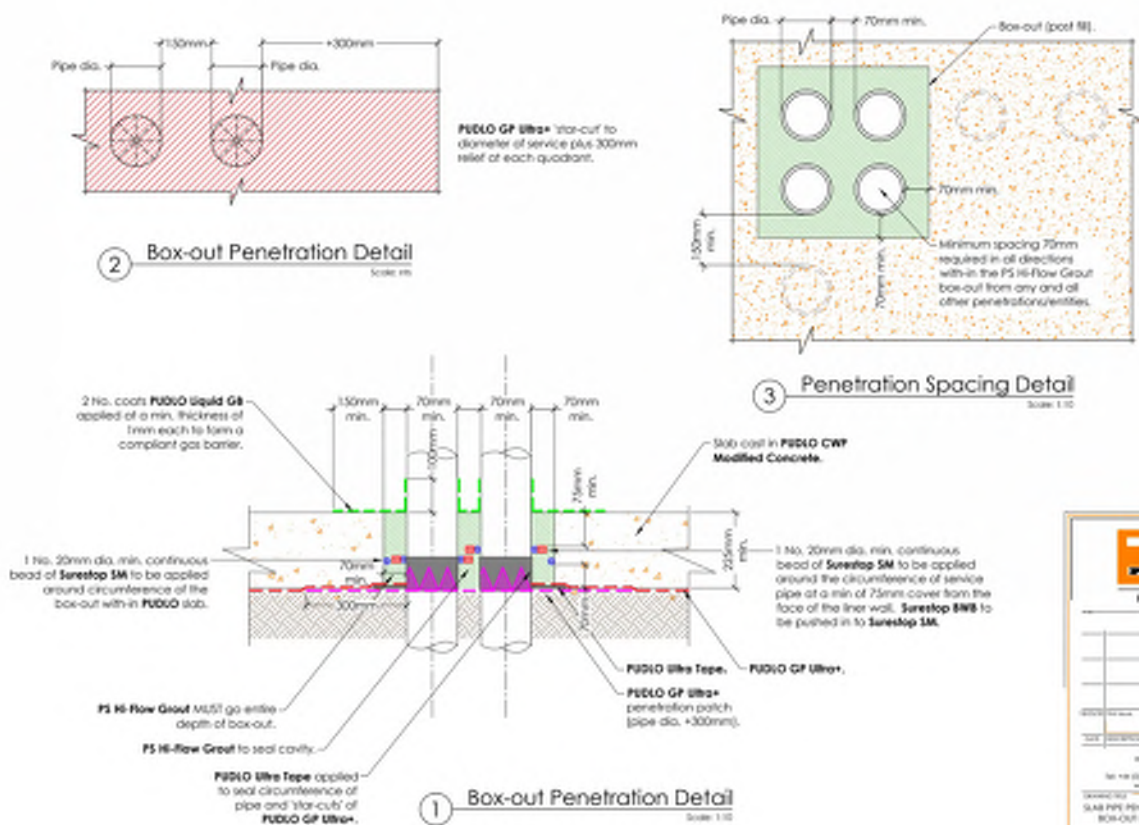[illegible]



DETAILS

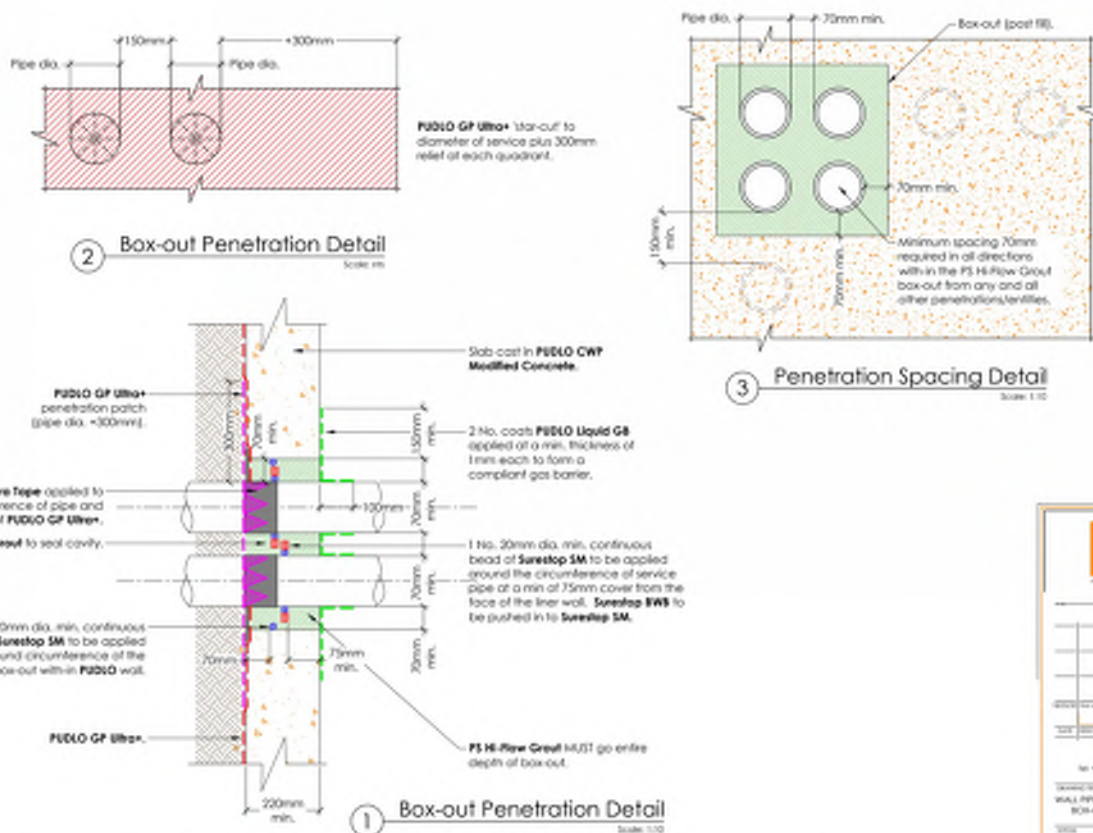

Part of the D8 Group

Section History

Section	Author	Revision	Date	Description
1.00	1.00	1.00	1.00	1.00
2.00	2.00	2.00	2.00	2.00
3.00	3.00	3.00	3.00	3.00
4.00	4.00	4.00	4.00	4.00
5.00	5.00	5.00	5.00	5.00
6.00	6.00	6.00	6.00	6.00
7.00	7.00	7.00	7.00	7.00
8.00	8.00	8.00	8.00	8.00
9.00	9.00	9.00	9.00	9.00
10.00	10.00	10.00	10.00	10.00
11.00	11.00	11.00	11.00	11.00
12.00	12.00	12.00	12.00	12.00
13.00	13.00	13.00	13.00	13.00
14.00	14.00	14.00	14.00	14.00
15.00	15.00	15.00	15.00	15.00
16.00	16.00	16.00	16.00	16.00
17.00	17.00	17.00	17.00	17.00
18.00	18.00	18.00	18.00	18.00
19.00	19.00	19.00	19.00	19.00
20.00	20.00	20.00	20.00	20.00
21.00	21.00	21.00	21.00	21.00
22.00	22.00	22.00	22.00	22.00
23.00	23.00	23.00	23.00	23.00
24.00	24.00	24.00	24.00	24.00
25.00	25.00	25.00	25.00	25.00
26.00	26.00	26.00	26.00	26.00
27.00	27.00	27.00	27.00	27.00
28.00	28.00	28.00	28.00	28.00
29.00	29.00	29.00	29.00	29.00
30.00	30.00	30.00	30.00	30.00
31.00	31.00	31.00	31.00	31.00
32.00	32.00	32.00	32.00	32.00
33.00	33.00	33.00	33.00	33.00
34.00	34.00	34.00	34.00	34.00
35.00	35.00	35.00	35.00	35.00
36.00	36.00	36.00	36.00	36.00
37.00	37.00	37.00	37.00	37.00
38.00	38.00	38.00	38.00	38.00
39.00	39.00	39.00	39.00	39.00
40.00	40.00	40.00	40.00	40.00
41.00	41.00	41.00	41.00	41.00
42.00	42.00	42.00	42.00	42.00
43.00	43.00	43.00	43.00	43.00
44.00	44.00	44.00	44.00	44.00
45.00	45.00	45.00	45.00	45.00
46.00	46.00	46.00	46.00	46.00
47.00	47.00	47.00	47.00	47.00
48.00	48.00	48.00	48.00	48.00
49.00	49.00	49.00	49.00	49.00
50.00	50.00	50.00	50.00	50.00
51.00	51.00	51.00	51.00	51.00
52.00	52.00	52.00	52.00	52.00
53.00	53.00	53.00	53.00	53.00
54.00	54.00	54.00	54.00	54.00
55.00	55.00	55.00	55.00	55.00
56.00	56.00	56.00	56.00	56.00
57.00	57.00	57.00	57.00	57.00
58.00	58.00	58.00	58.00	58.00
59.00	59.00	59.00	59.00	59.00
60.00	60.00	60.00	60.00	60.00
61.00	61.00	61.00	61.00	61.00
62.00	62.00	62.00	62.00	62.00
63.00	63.00	63.00	63.00	63.00
64.00	64.00	64.00	64.00	64.00
65.00	65.00	65.00	65.00	65.00



GEOSHIELD Verification Plan



DETAILS

100mm PUDLO Ultra Tape selvage joint.

300mm PUDLO Ultra EXT Tape roll-end joint.

Stagger roll ends to avoid multiple roll end jointing.

Block GeoTextile to face installer. (THIS SIDE)

Part of the DB Group

Revision History		
NO.	DESCRIPTION	REV.
1	Issue	1
2	Issue	2
3	Issue	3
4	Issue	4
5	Issue	5
6	Issue	6
7	Issue	7
8	Issue	8
9	Issue	9
10	Issue	10

DB Group Holdings Ltd
Wellington Way, South Afield
Cambridge, CB23 2TQ
Tel: +44 (0)1354 780877 Email: sales@pudlo.com
www.dbgroup.co.uk/pudlo

DESIGN TITLE	PROJECT
GP ULTRA+ OVERLAPPING DETAIL	Clarendon Road

TYPE	SCALE
CONSTRUCTION	1:100

DESIGNED BY	REVISION	SHEET NO.
BCH-CUR-018	1	1 of 1

Client: Berkeley Homes

Copyright: Not to be reproduced without written permission.

A4

PUDLO Group LTD 2018-2019

Note:
This PUDLO detail is to assist with the installation of this product. The detail shows how PUDLO-CRP Modified Concrete, membranes and how PUDLO indicates are to be installed. For site specific details and confirmation on extent of where PUDLO-CRP Modified Concrete is used in. Details drawings, must be confirmed by structural engineer/contractor. Individual/Company responsibility for design of the structure must ensure that details shown on PUDLO drawings match the other construction issue drawings. PUDLO-GP Ultra+ Resilience offers gas protection against a number of ground gases in accordance with its BRE BREB. When using PUDLO-GP Ultra+ Resilience the client/contractor must appoint a 3rd party independent gas specialist for verification, installation and review of gas levels in accordance with CIRA T35. PUDLO only produces typical details for membranes. Specific drawings for gas specification need to be provided by an independent gas inspector. Contact details can be provided on request.

The information shown on this detail is given without obligation, or warranty. PUDLO is consulted in communication with PUDLO/DB Group Ltd.






GEOSHIELD Verification Plan



DETAILS

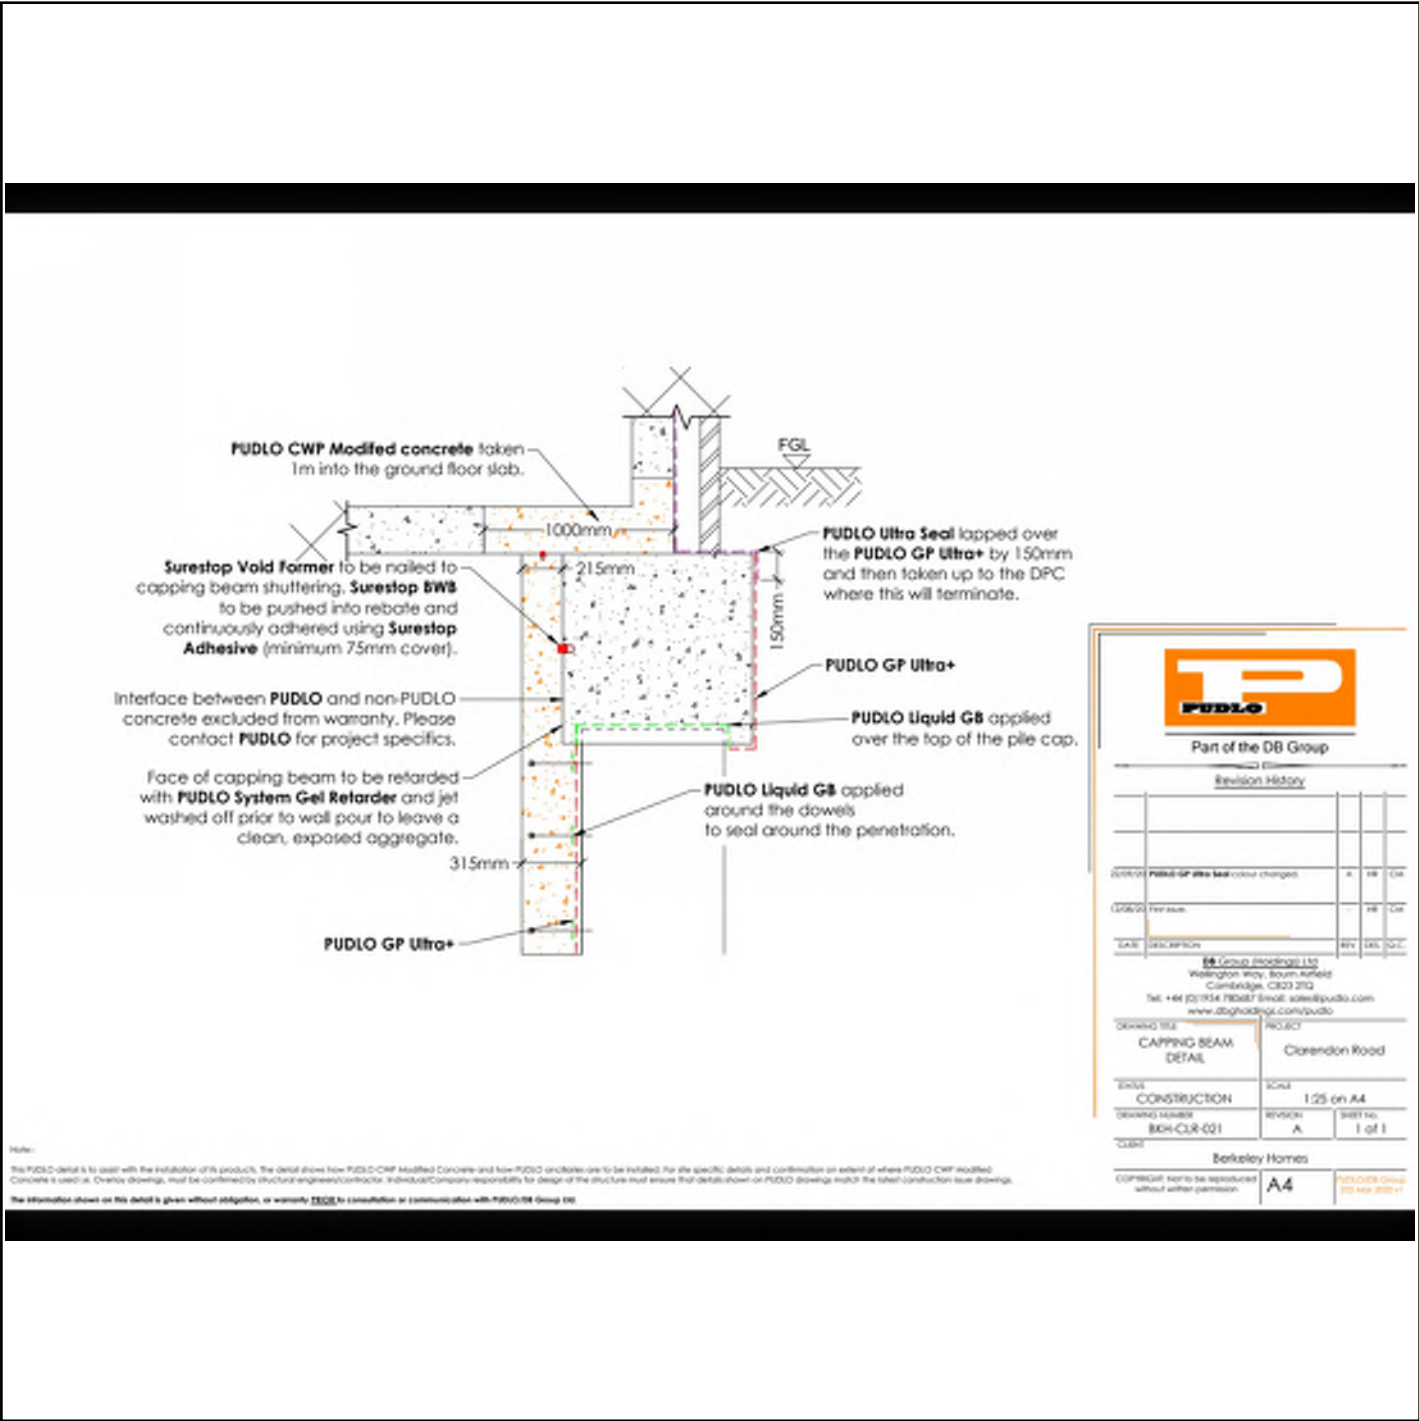

PUDLO

Part of the DB Group

Revision History

Rev	Description	Rev	Date
01	Initial issue		
02	Revised to include changes		
03	Revised to include changes		
04	Revised to include changes		

DB Group (Holdings) Ltd
Watlington Way, Bourn, Bedford
Cambridge, CB3 2TQ
Tel: +44 (0)1534 780877 Email: sales@pudlo.com
www.dbholdings.com/pudlo

PROJECT: Capping Beam Detail

Client: Clarendon Road

Scale: 1:25 on A4

Revision: A

Sheet No: 1 of 1

Project: Berkeley Homes

Copyright: Not to be reproduced without written permission.

A4


PUDLO Group Ltd
100 May 2024



GEOSHIELD Verification Plan



DETAILS

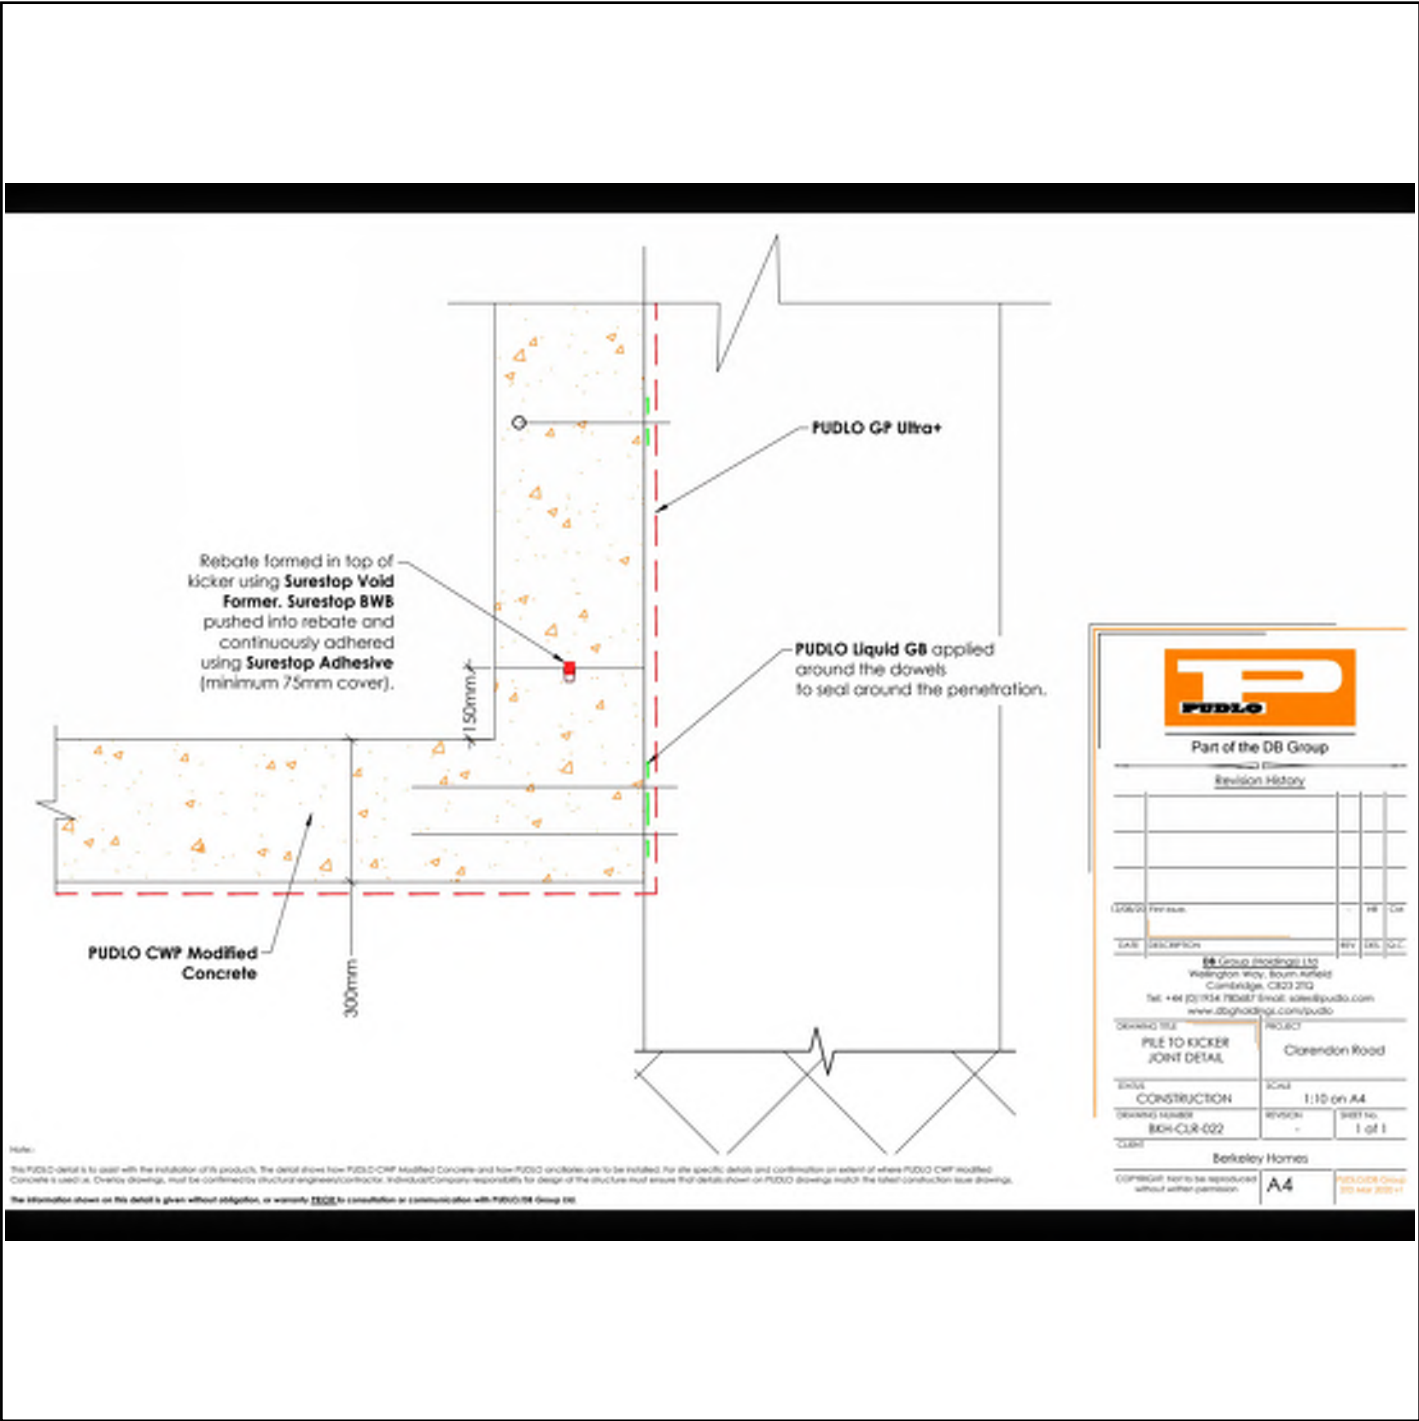




GEOSHIELD Verification Plan



DETAILS

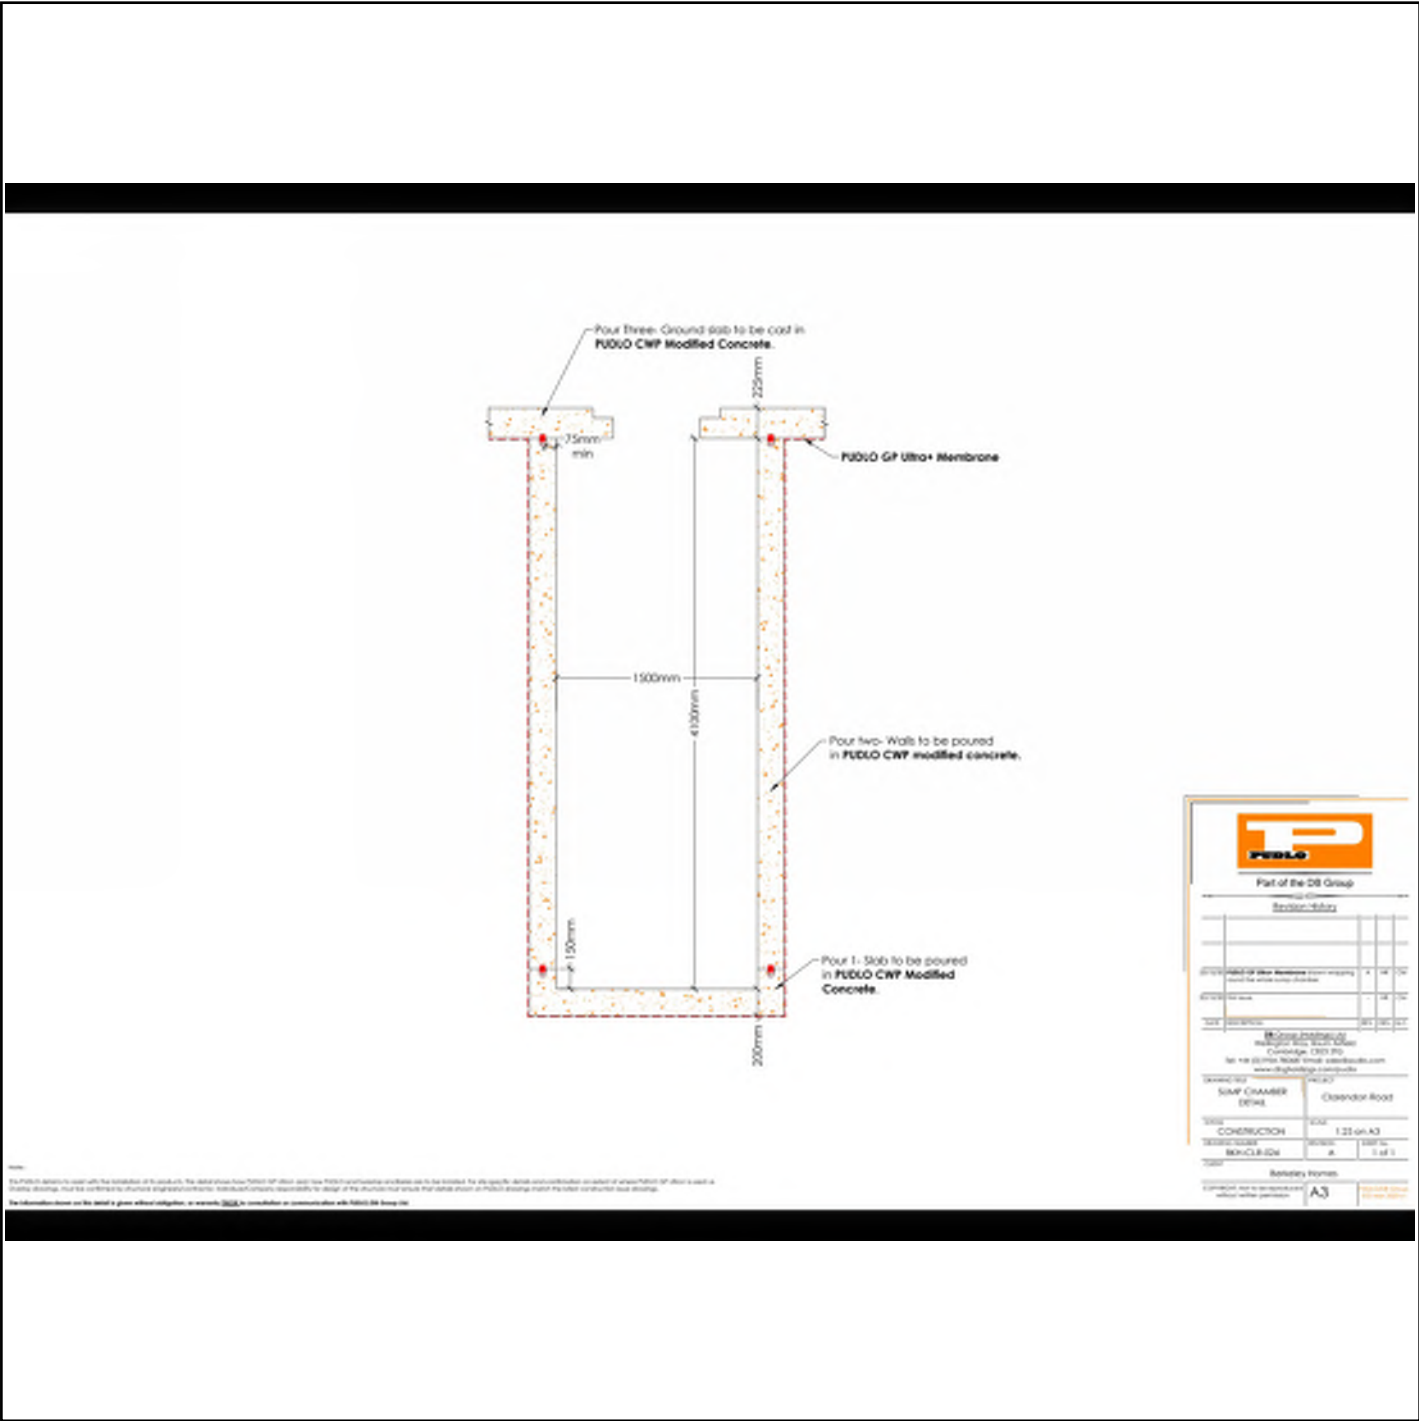

Sump Chamber Detail

GEOSHIELD
Verification Plan

BGA



CLIENT DETAILS

CLIENT CONTACT:

Rohallah De Sousa

CONTACTS ROLE:

Ground Construction Ltd

MOBILE PHONE:

02082387000

EMAIL ADDRESS:

RohallahDeSousa@GroundConstruction.com

CLIENT CONTACT:

CONTACTS ROLE:

MOBILE PHONE:

EMAIL ADDRESS

NOTES:



GEOSHIELD
Verification Plan



APPLICATION TEAM LEADERS

APPLICATOR NAME:

COMPANY:

APPLICATOR TEL:

APPLICATOR EMAIL:

APPLICATOR NAME:

COMPANY:

APPLICATOR TEL:

APPLICATOR EMAIL:

NOTES:

NOTES:

NOTES:

NOTES:



GEOSHIELD
Verification Plan



HEALTH AND SAFETY

INDUCTION:

YES



NO:



INDUCTION TIME:

To be confirmed at the pre-verification meeting

CSCS CARD:

YES



NO:



CSCS CARD NUMBER:

All installers will be required to provide their CSCS card

METHOD STATEMENT:

YES



NO:



RISK ASSESSMENT:

YES



NO:



COSHH:

YES



NO:



SITE SPECIFIC HAZARDS:

Materials falling from height

Slips, trips and falls

Excavations

Confined spaces

Plant



GEOSHIELD Verification Plan



NOTIFICATION:

24 HOURS:	YES	☐	NO	☒
48 HOURS:	YES	☒	NO	☐

REASON FOR VISIT:

DURING INSTALLATION:	☒	UNDERSLAB VENTILATION	☒
PRE - POUR:	☒	DPC MEMBRANE CONNECTION	☒
TESTING:	☒	OTHER	☐

TRAINING LEVEL:

SPECIALIST CONTRACTOR:	YES	☐	NO	☒
NVQ LEVEL 2:	YES	☐	NO	☒
COMPETENT APPLICATOR:	YES	☒	NO	☐
TOOLBOX BY GEOSHIELD:	YES	☒	NO	☐

NOTES:	They are competent installers and will be assessed by GeoShield at the
NOTES:	pre-contract meeting. GeoShield will toolbox talk but any further assistance required
NOTES:	Geoshield can do so during inspection.
NOTES:	

GAS REGIME:				
CS1/Green	YES	☐	NO	☒
CS2/Amber	YES	☒	NO	☐
CS3/Amber 2	YES	☐	NO	☒
CS3/ or above/Red	YES	☐	NO	☒
VOC	YES	☒	NO	☐
RADON BASIC	YES	☐	NO	☒
RADON FULL	YES	☒	NO	☒

Building Type:

TYPE A

POINTS REQUIRED UNDER BS8485 2015

3.5 POINTS

POINTS GAINED FROM BS8485 2015

Score for Structural Barrier:

1.5 POINTS

Grade 2 basement:

N/A

Grade 3 basement:

N/A

Score for Venting:

N/A

Car park:

N/A

Score for Membrane:

2.0 POINTS

POINTS ACHIEVED UNDER BS8485 2015

3.5 POINTS



GEOSHIELD Verification Plan



TESTING:

VISUAL: PICK and PROBE

YES



NO

☐

NON-DESTRUCTIVE SMOKE TEST:

YES

☐

NO

☒

NON-DESTRUCTIVE COMPRESSED AIR LANCE:

YES



NO

☐

DESTRUCTIVE JOINT TESTING:

YES

☐

NO

☒

NON-DESTRUCTIVE TRACER GAS:

YES

☐

NO

☒

DIELECTRIC POROSITY TEST:

YES

☐

NO

☒

PUMP TEST FOR "Twinny" WELD

YES

☐

NO

☒

NOTES:

Air Lance testing will be carried out on all welded joints in accordance with

NOTES:

CIRIA 735. Remaining works will be visually inspected and mechanically tested

NOTES:

to ensure a good bond is achieved. All testing will be in accordance with CIRIA

NOTES:

735 and documented for forward to the Local Planning Authority.

NOTES:

NOTES:

NOTES:



GEOSHIELD Verification Plan



RISK ASSESSMENT

SITE SPECIFIC CIRCUMSTANCES	1	2	3	4	5
Complexity of Design	1	2	3 ✓	4	5
Repetition of design	1	2 ✓	3	4	5
Experience of workforce	1	2	3 ✓	4	5
Gas regime	1	2 ✓	3	4	5
Project management experience	1 ✓	2	3	4	5
Installation conditions (exposed?)	1	2	3 ✓	4	5
Robust Project specific gas design	1 ✓	2	3	4	5

TYPE OF RISK	RANGE	RISK
High Risk	23 - 30	
Medium High Risk	19 - 22	22
Medium Risk	15 - 18	
Medium Low Risk	11 - 14	
Low Risk	0 - 10	

GeoShield have classed this project as a medium high risk. This is largely due to the installers being unknown and the challenging site conditions. Geoshield will lay down the parameters of verification visits during the pre start meeting to assist both the installer and the main contractor.



GEOSHIELD
Verification Plan



VERIFICATION REPORT

These items will be included in the report

- NUMBER 1

GAS MEMBRANE SPECIFICATION
- NUMBER 2

ELEMENTS OF THE GAS MEMBRANE
- NUMBER 3

DATE, TIME and WEATHER CONDITIONS
- NUMBER 4

PLANS and DETAILS ISSUED
- NUMBER 5

INSTALLATION PHOTO's RELATING TO GRID LINES
- NUMBER 6

REPORTING DEFECTS AND LOGGING IN REMEDIATION LOG
- NUMBER 7

AREAS OF LIMITATION (areas unable to inspect)
- NUMBER 8

LOGGING AND REPORTING RESULTS OF TESTING

VERIFICATION REPORT ISSUE

HARD COPY:

YES

☒

NO

☐

EMAIL:

YES

☒

NO

☐

DROP BOX LINK:

YES

☐

NO

☒

FLASH DRIVE:

YES

☒

NO

☐





GEOSHIELD Verification Plan



GEOSHIELD COMPETENCE

>GeoShield was founded in 2015

>GeoShield solely verifies, they are fully independent of installers, manufactures and geotechnical companies.

>GeoShield follow guidance in CIRIA 735 (sufficient experience, membership of relevant professional organisations) GeoShield are members of the BVC, BGA, ERA, The RADON Council, and UKRA

>Currently GeoShield hold the Chairmanship of the British Verification Council

>Two employees are NSAC Level 3 assessors for the NVQ 2 Gas Membrane install

>GeoShield were key in forming the NVQ 4 Verification qualification in which 2 Verification officers are undertaking this qualification

>GeoShield have the only qualified assessor for the NVQ 4 Verification qualification

>GeoShield Verification officers currently keep up to date CPD's

>All GeoShield Verification Officers have a full understanding of gas membrane install including 3 experienced (NVQ 2) installers in the GeoShield team

>GeoShield Verification Officers are all independent carrying there own air

compressors. Other testing equipment GeoShield have access to are 2 x Buckley

Dielectric Testing machines and also inert gas testing equipment



GEOSHIELD
Verification Plan



VERIFICATION PLAN

METHOD STATEMENT

The geotechnical survey report confirms the site is a CS2 site with continued monitoring for VOCs.

The proposed designs have been reviewed and Geoshield confirm they are compliant with the requirements of CS2 and VOCs.

In this pre verification plan it has laid out the:

> Design

> Specification

> Verification procedure

Testing and documenting of the ground gas membrane installation will be carried out in accordance with CIRIA 735. Geoshield will liaise with the installation team and main contractor to ensure all faults found are remediated.



GEOSHIELD
Verification Plan



SUBSTRATE METHOD STATEMENT

Substrate Type:

Block and Beam Construction	Yes		No	✓
-----------------------------	-----	--	----	---

Minimum Preparation	Swept Clear	Yes		No	
---------------------	-------------	-----	--	----	--

Minimum Preparation	Vacuuming	Yes		No	
---------------------	-----------	-----	--	----	--

Minimum Preparation	Compressed air to remove	Yes		No	
---------------------	--------------------------	-----	--	----	--

Minimum Preparation	Remove Mortar Droppings	Yes		No	
---------------------	-------------------------	-----	--	----	--

Stone Substrate	Yes	✓	No	
-----------------	-----	---	----	--

Minimum Preparation	Minimum 25mm Sand Blinding	Yes	✓	No	
---------------------	----------------------------	-----	---	----	--

Minimum Preparation	Limestone Dust	Yes		No	✓
---------------------	----------------	-----	--	----	---

Minimum Preparation	Compacted Substrate	Yes	✓	No	
---------------------	---------------------	-----	---	----	--

Minimum Preparation	No large stones	Yes	✓	No	
---------------------	-----------------	-----	---	----	--

Concrete Substrate	Yes	✓	No	
--------------------	-----	---	----	--

Minimum Preparation	No Hollows	Yes	✓	No	
---------------------	------------	-----	---	----	--

Minimum Preparation	Troweled Surface	Yes	✓	No	
---------------------	------------------	-----	---	----	--

Remarks:	Concrete blinding and concrete floors to have smooth float finish after
----------	---

pour when wet.	
----------------	--

--	--



GEOSHIELD
Verification Plan



PROTECTION METHOD STATEMENT

Protection Type:

Protection Board	Yes	☐	No	☒
------------------	-----	--------------------------	----	-------------------------------------

Protection Fleece	Yes	☐	No	☒
-------------------	-----	--------------------------	----	-------------------------------------

Insulation	Yes	☐	No	☒
------------	-----	--------------------------	----	-------------------------------------

Where Protection Board is installed in the gas remediation strategy the

verifier must be allowed access to inspect the membrane

Remarks:	Protection Board has not been specified in the design details.
----------	--

WHERE NO PROTECTION BOARD SPECIFIED

Protection Board has not been specified. The concrete slab will be poured directly on the ground gas

membrane. Geoshield will need to liaise with the steel fixers and explain the importance of not damaging

the membrane during installation. All steel rebar to be carried flat and stood on its end. This may require

monitoring to ensure damage is done to the membrane after installation.

Remarks:	
----------	--

Concrete Spacers	Yes	☒	No	☐
------------------	-----	-------------------------------------	----	--------------------------

Plastic 'Tric-Trac'	Yes	☐	No	☒
---------------------	-----	--------------------------	----	-------------------------------------



GEOSHIELD Verification Plan



PRE-CONTRACT MEETING

Items for discussion at the Pre-Contract meeting

☐

>Induction Procedure

☐

>Identification of installation team and point of contact

☐

>Identification of Project management team

☐

>Identification of Sub-Contractors associated with membrane installation

☐

>Validation of Membrane and design specification

☐

>Verification procedure

☐

>Notifications for Verification

☐

>Preparation of substrate

☐

>Program of works

☐

>Utility entry

☐

>Protection of Membrane

☐

>Remediation Procedure

☐

>Testing Procedures

☐

>Sign off Procedure

☐

>Installer PI

☐

All information is assumed correct at time of issue.

DATE:

10th November 2020



GEOSHIELD Verification Plan



GEOSHIELD SUMMARY RISK ASSESSMENT

BS8485 Building Type		1		2		3		4		5
Profile of Project (school, warehouse)		1		2		3		4		5
Past history of contractor		1		2		3		4		5
Past history of the installer		1		2		3		4		5
Installers hold NVQ 2		1		2		3		4		5
Specific gas design		1		2		3		4		5
Design conforms to BS8485		1		2		3		4		5
Materials conform to BS8485		1		2		3		4		5
Verification follows CIRIA 735		1		2		3		4		5
BS8485 Gas Classification		1		2		3		4		5
VOC		1		2		3		4		5
Complexity of Design		1		2		3		4		5
Repitition of Design		1		2		3		4		5
Installation environment		1		2		3		4		5
Substrate design		1		2		3		4		5
Membrane protection		1		2		3		4		5
Low risk					Low - Medium					
Medium					Medium - High					
High										



PRE-CONTRACT MEETING SUMMARY

[illegible]
