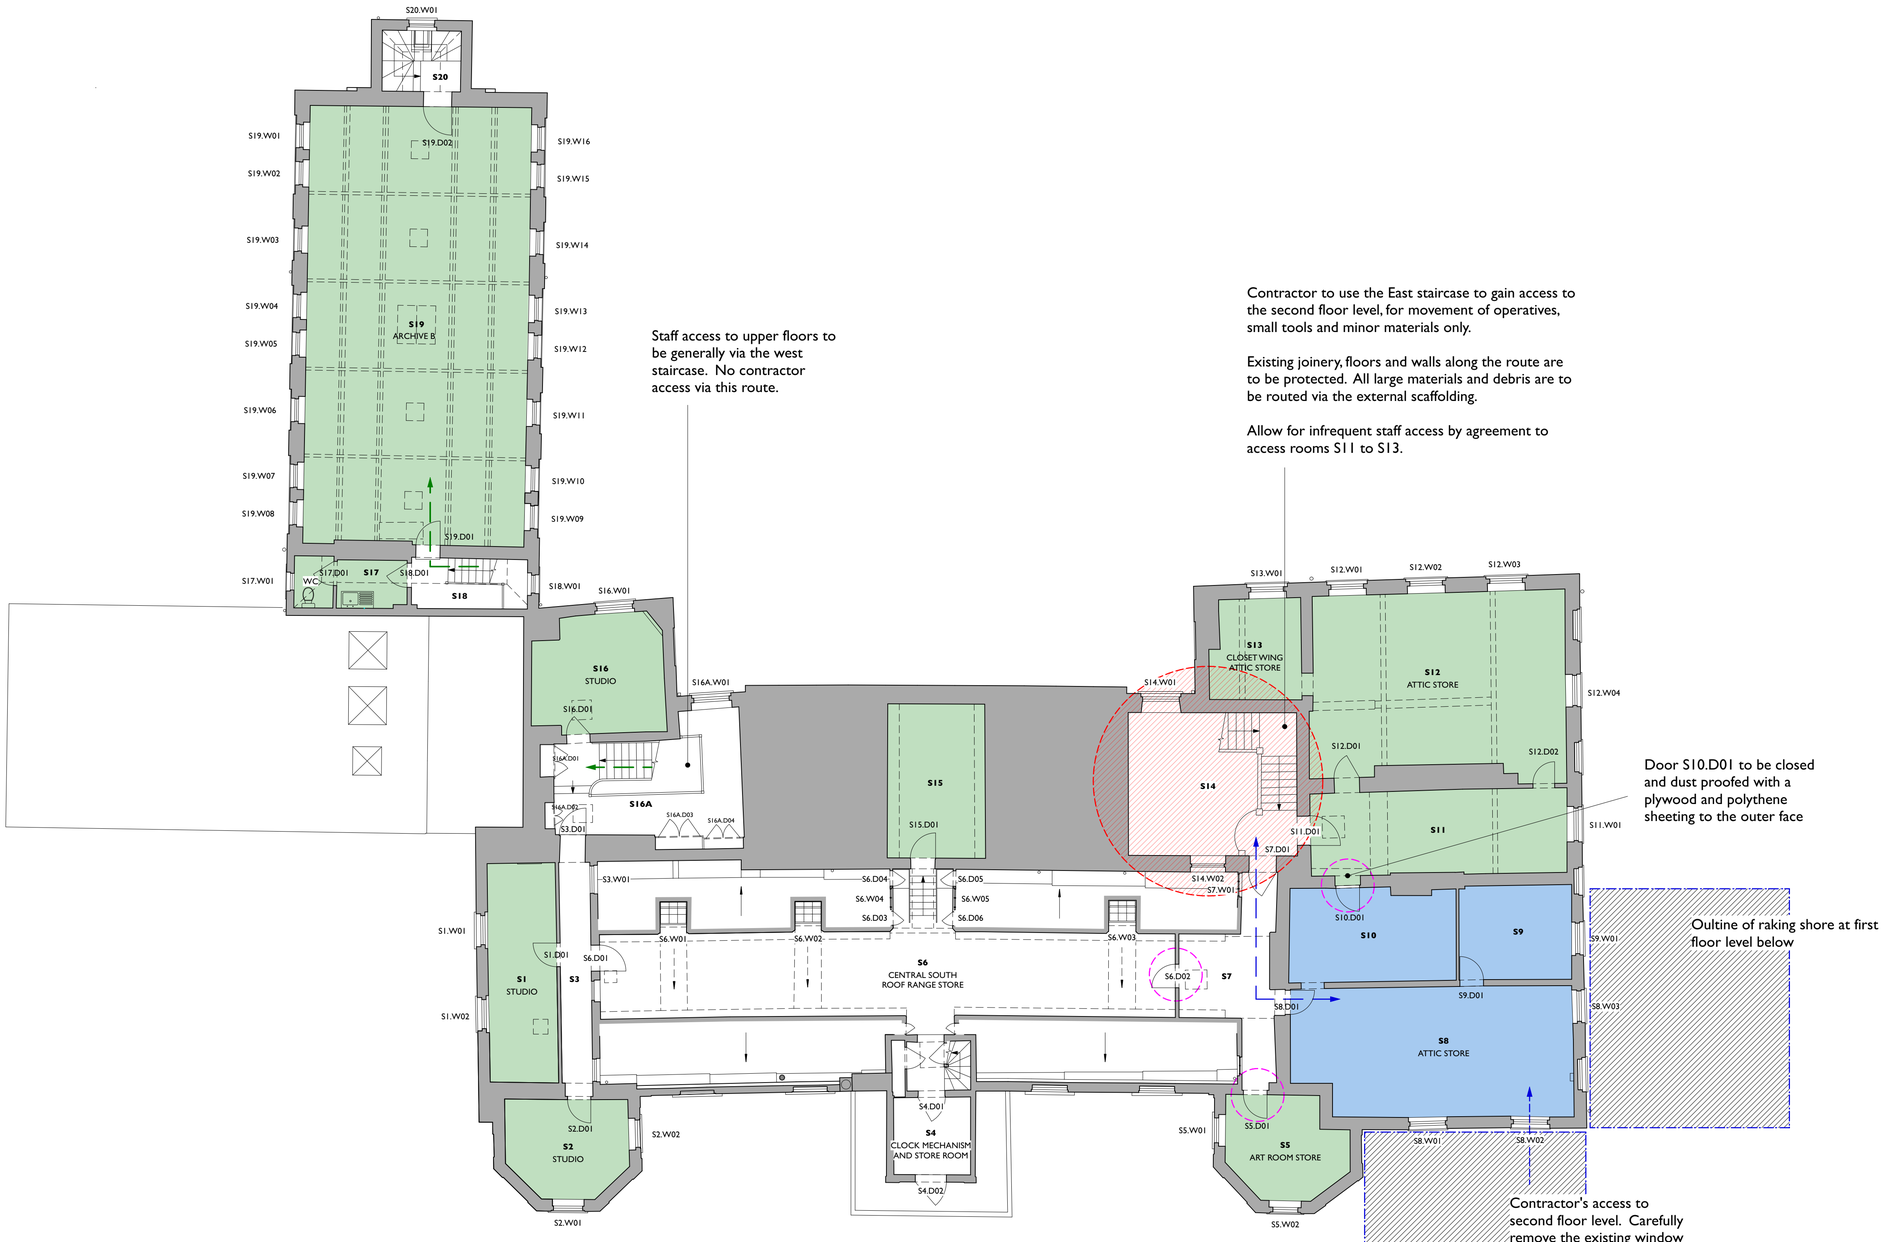


Staff access to upper floors to be generally via the west staircase. No contractor access via this route.

Contractor to use the East staircase to gain access to the second floor level, for movement of operatives, small tools and minor materials only.

Existing joinery, floors and walls along the route are to be protected. All large materials and debris are to be routed via the external scaffolding.

Allow for infrequent staff access by agreement to access rooms S11 to S13.

Door S10.D01 to be closed and dust proofed with a plywood and polythene sheeting to the outer face

Outline of raking shore at first floor level below

Contractor's access to second floor level. Carefully remove the existing window sashes and frame, and install a new frame and secure painted flush security door to the opening, to be maintained for the duration of the works. Reinstate window joinery on completion. Prefered window position to be agreed on site.

External access scaffolding, forming a working platform at second floor level to aid installation of new steel work and removal of debris. Scaffolding design to be undertaken by the contractors temporary works engineer and erected in accordance with the specification, without fixings being made to the building. Do not assume that skips can be located at the foot of the scaffolding and allowance should be made for removing all debris to skips located in th carpark compound.

SECOND FLOOR - OPERATIONS AND LOGISTICS PLAN
MAIN CONTRACT WORKS

0 1 2 3 4 5m

NOTE

1. This drawing is copyright.
2. All dimensions must be checked on site before proceeding.
3. Dimensions of new work are to be adjusted to suit the existing building where necessary. Do not assume that the existing structure or details are plumb, square or level.
4. The contractor must report any discrepancies to the architect before proceeding.
5. All products are to be used strictly in accordance with the manufacturer's instructions.

KEY

- MEND Funded Works - Enabling Works (Site Area)
- Staff / Back of House Spaces
- Public Spaces - Access to be maintained for the duration of the works
- Contractor Access Routes
- Staff Access Routes
- Public Access Routes
- Areas of Cross Over
- Doors between working and non-work areas to be kept closed and dust proofed
- Area of Scaffold

REVISIONS

C Nov 2023. Key Updated
B Oct 2023. Additional notes added and drawing updated to indicate final arrangements.
A Aug 2023 Additional notes added following initial Client comment

Rodney Melville + Partners
CHARTERED ARCHITECTS
HISTORIC BUILDING CONSULTANTS

10 EUSTON PLACE
LEAMINGTON SPA
WARWICKSHIRE
CV32 4LJ
T 01926 881311
F 01926 451766

E architects@rmpuk.com
www.rmpuk.com
Rodney Melville and Partners Limited

Client
London Borough of Haringey Council

Project
Bruce Castle

Title
Second Floor
Operations and Logistics Plan - Main Contract Works

Scale	1:100 @ A1	Job No	7440
Date	Aug 2023	Drwg No	172
Drawn	HB	Rev	C
