


Programme of Remedial and Restoration Work

Works to complete essential repair, restoration and secure protection of the building over the imminent winter period.

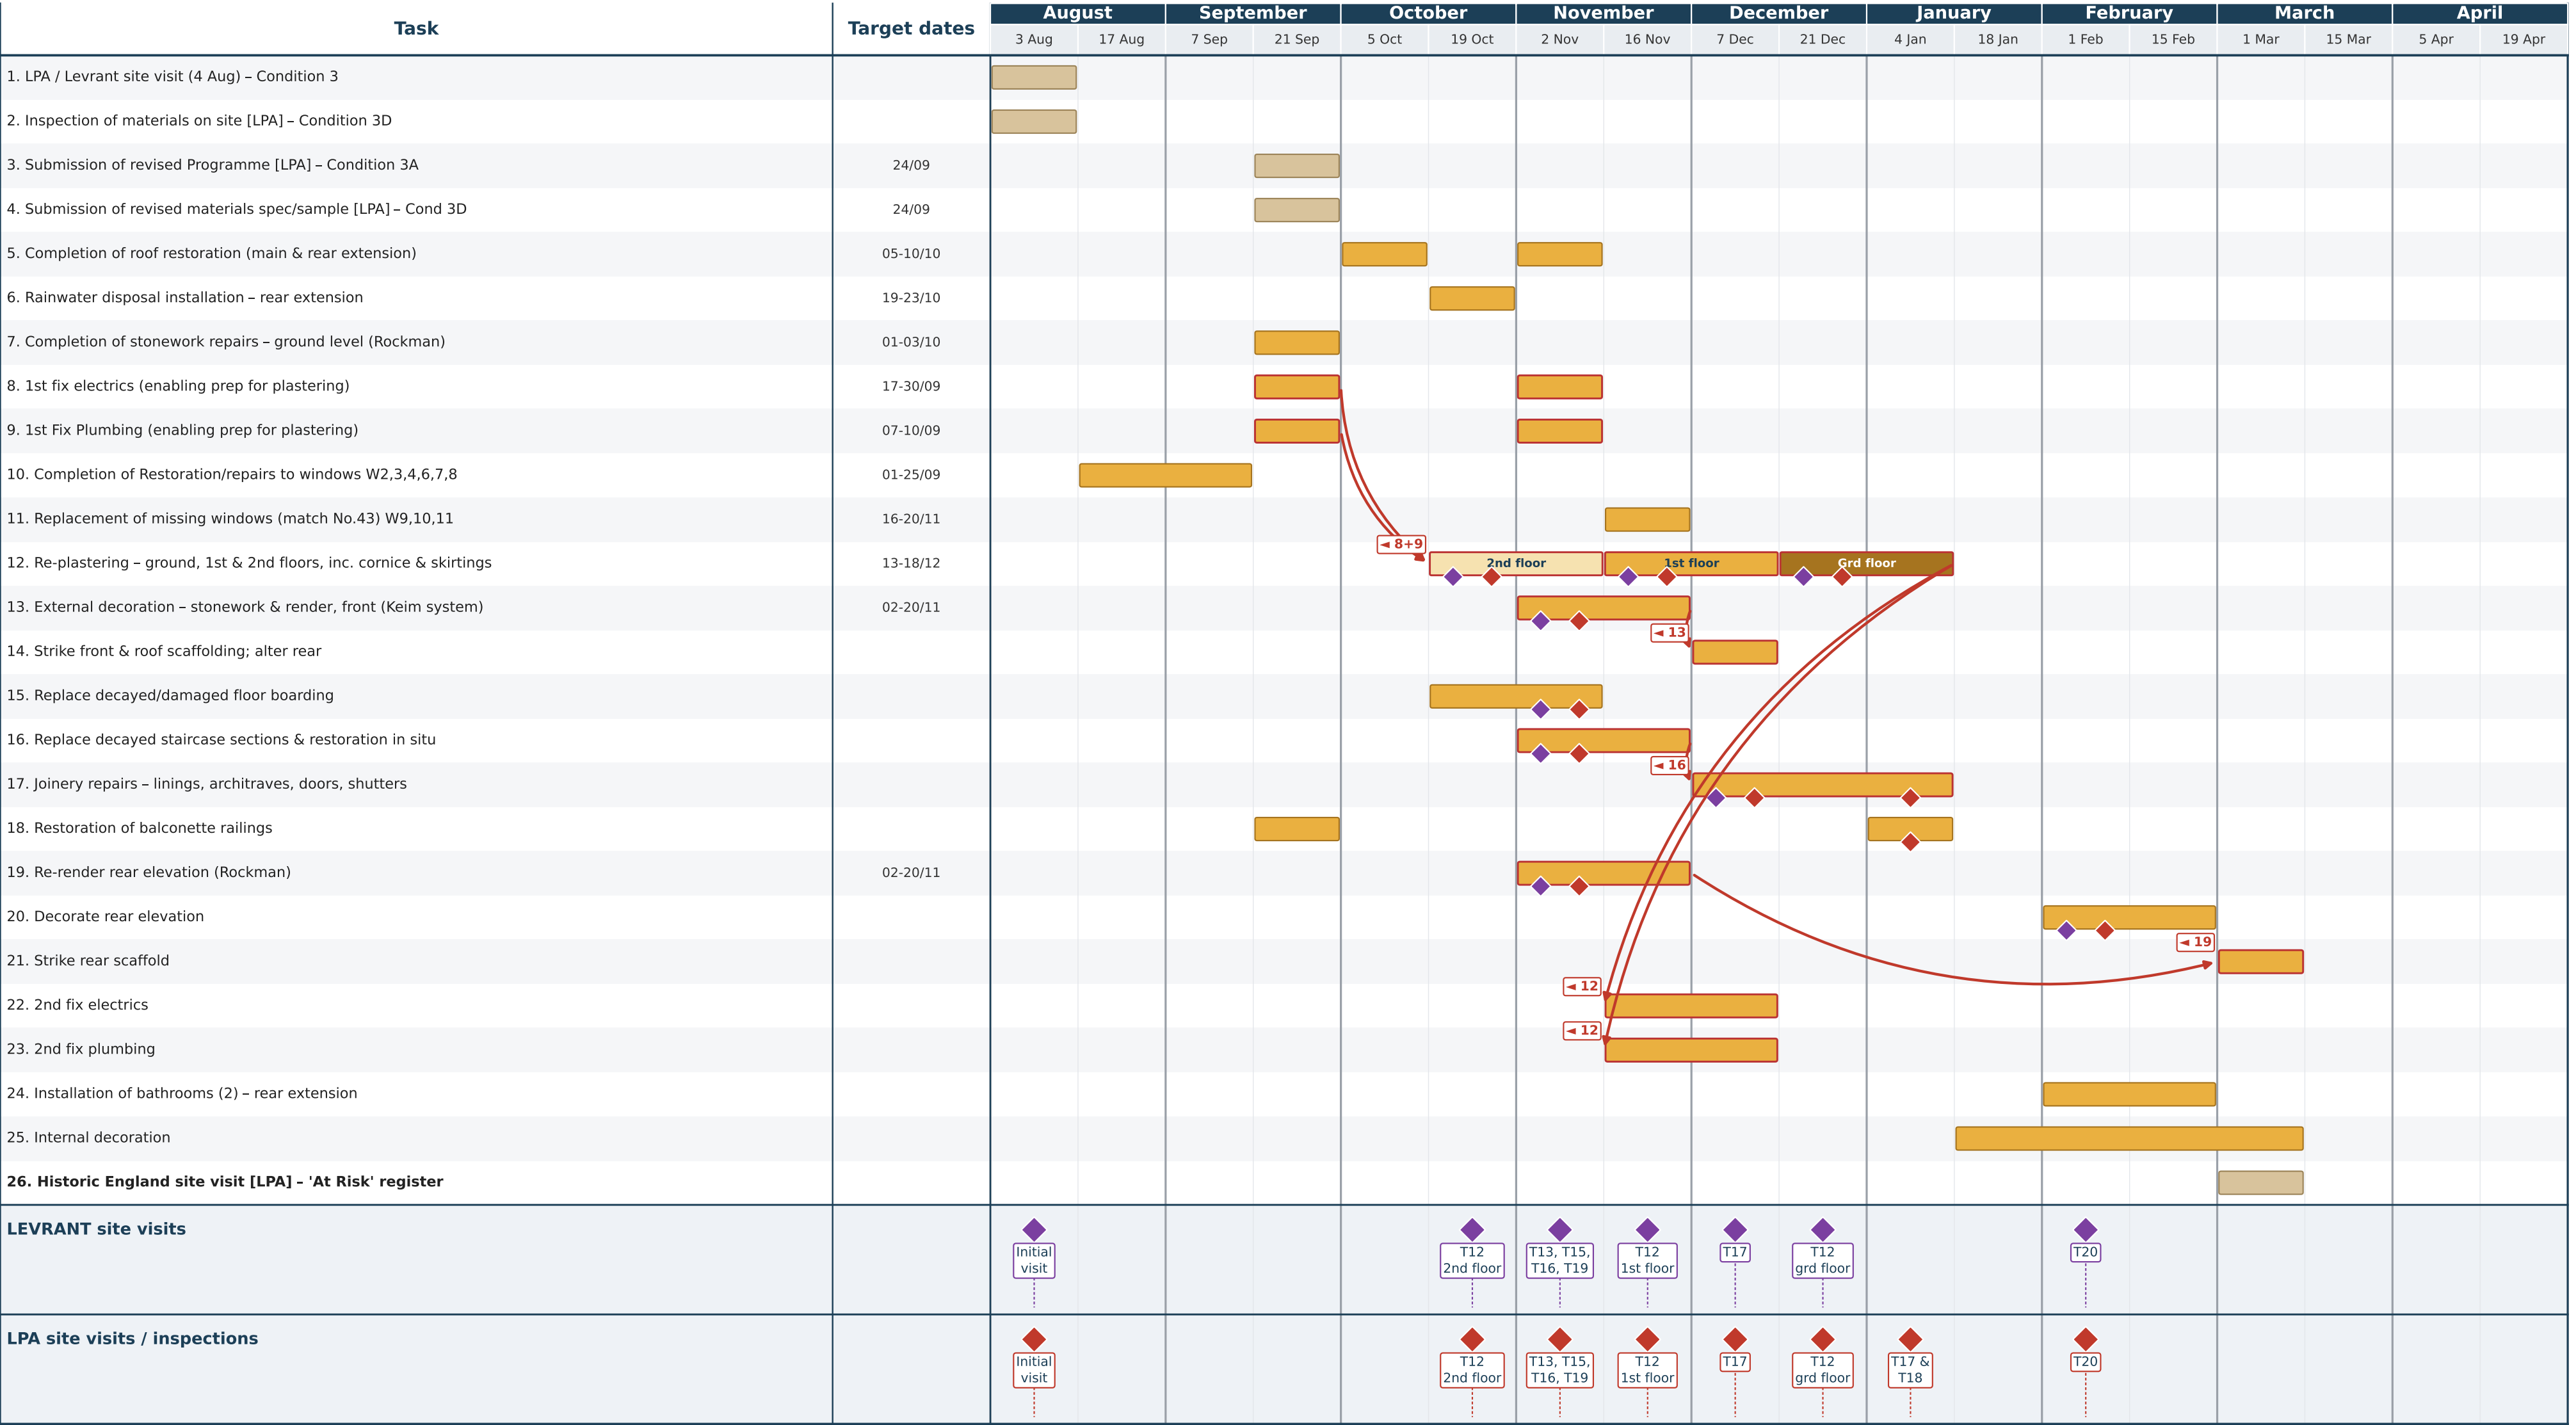

Dependencies shown: Task 12 (re-plastering) starts only once the September phase of Tasks 8 & 9 (1st fix electrics/plumbing) is complete; Task 14 starts once Task 13 is complete; Task 17 starts once Task 16 is complete; Task 21 starts once Task 19 is complete; Tasks 22 & 23 start once Task 12 is complete. Note: as currently shaded, Tasks 22 & 23 begin 16 Nov while Task 12 does not finish until 18 Jan– please confirm this overlap is intended. Bars and arrows for linked tasks are outlined in red.

Column dates: 1st column = 1st Monday of the month; 2nd column = the Monday after mid-month. Programme year assumed Aug 2026- Apr 2027 – please confirm.
